







































ID	Task Name	Duration	Start	Finish	H2	H1
1	UPDATED as of February 1, 2025					
2	SCE - Local RCI Solicitation	679 days	Tue 8/21/18	Fri 3/26/21		
3	SCE - RFA Preparation	40 days	Tue 8/21/18	Mon 10/15/18		
4	SCE - RFA Release	1 day	Fri 11/9/18	Fri 11/9/18		
5	SCE - RFA Abstract Creation Duration	30 days	Sat 11/10/18	Thu 12/20/18		
6	SCE - RFA Evaluation	82 days	Fri 12/21/18	Mon 4/15/19		
7	SCE - RFA Review with EE PRG	1 day	Tue 4/16/19	Tue 4/16/19		
8	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/21/19	Tue 5/21/19		
9	SCE - RFP Preparation	175 days	Wed 5/22/19	Tue 1/21/20		
10	SCE - RFP Release	1 day	Wed 1/22/20	Wed 1/22/20		
11	SCE - RFP Proposal Creation Duration	25 days	Thu 1/23/20	Wed 2/26/20		
12	SCE - RFP Evaluation	38 days	Thu 2/27/20	Mon 4/20/20		
13	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20		
14	SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20		
15	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20		
16	SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20		
17	SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20		
18	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20		
19	SCE - Advice Letter Approved	1 day	Wed 12/30/20	Wed 12/30/20		
20	SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21		
21	SCE - SW Lighting	518 days	Wed 4/3/19	Fri 3/26/21		
22	SCE - RFA Preparation	55 days	Wed 4/3/19	Tue 6/18/19		
23	SCE - RFA Release	1 day	Tue 7/2/19	Tue 7/2/19		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
24	SCE - RFA Abstract Creation Duration	20 days	Wed 7/3/19	Tue 7/30/19		
25	SCE - RFA Evaluation	34 days	Wed 7/31/19	Mon 9/16/19		
26	SCE - RFA Review with EE PRG	1 day	Tue 9/17/19	Tue 9/17/19		
27	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/24/19	Tue 9/24/19		
28	SCE - RFP Preparation	84 days	Wed 9/25/19	Mon 1/20/20		
29	SCE - RFP Release	1 day	Thu 2/6/20	Thu 2/6/20		
30	SCE - RFP Proposal Creation Duration	27 days	Fri 2/7/20	Mon 3/16/20		
31	SCE - RFP Evaluation	25 days	Tue 3/17/20	Mon 4/20/20		
32	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/7/20	Thu 5/7/20		
33	SCE - RFP Review with EE PRG	1 day	Tue 4/21/20	Tue 4/21/20		
34	SCE - Contract Negotiation and Development	72 days	Fri 5/8/20	Mon 8/17/20		
35	SCE - Contract Review with EE PRG	1 day	Tue 8/18/20	Tue 8/18/20		
36	SCE - Final Award and Contract Signed	1 day	Wed 9/30/20	Wed 9/30/20		
37	SCE - Submit Advice Letter	43 days	Thu 10/1/20	Mon 11/30/20		
38	SCE - Advice Letter Approved	1 day	Wed 12/23/20	Wed 12/23/20		
39	SCE - Implementation Plan	60 days	Mon 1/4/21	Fri 3/26/21		
40	SCE - Local Public Sector Solicitation	573 days	Mon 8/31/20	Wed 11/9/22		
41	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20		
42	SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20		
43	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20		
44	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21		
45	SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21		
46	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
47	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21		
48	SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21		
49	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21		
50	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21		
51	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21		
52	SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21		
53	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21		
54	SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21		
55	SCE - Final Award and Contract Signed	1 day	Tue 12/14/21	Tue 12/14/21		
56	SCE - Submit Advice Letter	37 days	Wed 12/15/21	Thu 2/3/22		
57	SCE - Submit Advice Letter	48 days	Wed 12/15/21	Fri 2/18/22		
58	SCE - Advice Letter Approved	1 day	Thu 8/18/22	Thu 8/18/22		
59	SCE - Implementation Plan	60 days	Thu 8/18/22	Wed 11/9/22		
60	SCE - Local Agriculture Solicitation	512 days	Mon 8/31/20	Tue 8/16/22		
61	SCE - RFA Preparation	33 days	Mon 8/31/20	Wed 10/14/20		
62	SCE - RFA Release	1 day	Thu 11/5/20	Thu 11/5/20		
63	SCE - RFA Abstract Creation Duration	25 days	Fri 11/6/20	Thu 12/10/20		
64	SCE - RFA Evaluation	25 days	Fri 12/11/20	Thu 1/14/21		
65	SCE - RFA Review with EE PRG	1 day	Tue 1/19/21	Tue 1/19/21		
66	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/4/21	Thu 2/4/21		
67	SCE - RFP Preparation	65 days	Thu 12/10/20	Wed 3/10/21		
68	SCE - RFP Release	1 day	Thu 4/1/21	Thu 4/1/21		
69	SCE - RFP Proposal Creation Duration	30 days	Fri 4/2/21	Thu 5/13/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	H2	H1
70	SCE - RFP Evaluation	20 days	Fri 5/14/21	Thu 6/10/21		
71	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/28/21	Mon 6/28/21		
72	SCE - RFP Review with EE PRG	1 day	Tue 6/15/21	Tue 6/15/21		
73	SCE - Contract Negotiation and Development	97 days	Tue 6/29/21	Wed 11/10/21		
74	SCE - Final Award and Contract Signed	1 day	Mon 12/20/21	Mon 12/20/21		
75	SCE - Submit Advice Letter	33 days	Tue 12/21/21	Thu 2/3/22		
76	SCE - Contract Review with EE PRG	1 day	Tue 11/16/21	Tue 11/16/21		
77	SCE - Final Award and Contract Signed	1 day	Wed 12/15/21	Wed 12/15/21		
78	SCE - Submit Advice Letter	56 days	Thu 12/16/21	Thu 3/3/22		
79	SCE - Advice Letter Approved	1 day	Fri 4/22/22	Fri 4/22/22		
80	SCE - Implementation Plan	60 days	Sat 4/23/22	Thu 7/14/22		
81	SCE - SW Water/Wastewater Solicitation	522 days	Mon 11/16/20	Tue 11/15/22		
82	SCE - RFA Preparation	70 days	Mon 11/16/20	Fri 2/19/21		
83	SCE - RFA Release	1 day	Thu 3/4/21	Thu 3/4/21		
84	SCE - RFA Abstract Creation Duration	29 days	Thu 3/4/21	Tue 4/13/21		
85	SCE - RFA Evaluation	20 days	Wed 4/14/21	Tue 5/11/21		
86	SCE - RFA Review with EE PRG	1 day	Tue 5/18/21	Tue 5/18/21		
87	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 5/27/21	Thu 5/27/21		
88	SCE - RFP Preparation	34 days	Mon 4/19/21	Thu 6/3/21		
89	SCE - RFP Release	1 day	Thu 7/1/21	Thu 7/1/21		
90	SCE - RFP Proposal Creation Duration	25 days	Fri 7/2/21	Thu 8/5/21		
91	SCE - RFP Evaluation	41 days	Fri 8/6/21	Fri 10/1/21		
92	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/26/21	Tue 10/26/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	H2	H1
93	SCE - RFP Review with EE PRG	1 day	Tue 10/19/21	Tue 10/19/21		
94	SCE - Contract Negotiation and Development	94 days	Wed 10/27/21	Mon 3/7/22		
95	SCE - Contract Review with EE PRG	1 day	Tue 3/15/22	Tue 3/15/22		
96	SCE - Final Award and Contract Signed	1 day	Tue 4/19/22	Tue 4/19/22		
97	SCE - Submit Advice Letter	40 days	Wed 4/20/22	Tue 6/14/22		
98	SCE - Advice Letter Approved	26 days	Wed 6/15/22	Wed 7/20/22		
99	SCE - Implementation Plan	44 days	Thu 7/21/22	Tue 9/20/22		
100	SCE - SW ETP Solicitation	466 days	Fri 5/1/20	Fri 2/11/22		
101	SCE - RFA Preparation	57 days	Fri 5/1/20	Mon 7/20/20		
102	SCE - RFA Release	1 day	Tue 8/4/20	Tue 8/4/20		
103	SCE - RFA Abstract Creation Duration	24 days	Fri 8/7/20	Wed 9/9/20		
104	SCE - RFA Evaluation	16 days	Thu 9/10/20	Thu 10/1/20		
105	SCE - RFA Review with EE PRG	1 day	Tue 10/20/20	Tue 10/20/20		
106	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/27/20	Tue 10/27/20		
107	SCE - RFP Preparation	42 days	Tue 9/8/20	Wed 11/4/20		
108	SCE - RFP Release	1 day	Tue 1/5/21	Tue 1/5/21		
109	SCE - RFP Proposal Creation Duration	37 days	Tue 1/5/21	Wed 2/24/21		
110	SCE - RFP Evaluation	28 days	Wed 2/24/21	Fri 4/2/21		
111	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/27/21	Tue 4/27/21		
112	SCE - RFP Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21		
113	SCE - Contract Negotiation and Development	69 days	Wed 4/21/21	Mon 7/26/21		
114	SCE - Contract Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21		
115	SCE - Final Award and Contract Signed	1 day	Tue 9/14/21	Tue 9/14/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
116	SCE - Submit Advice Letter	18 days	Wed 9/15/21	Fri 10/8/21		
117	SCE - Advice Letter Approved	1 day	Tue 11/9/21	Tue 11/9/21		
118	SCE - Implementation Plan	60 days	Wed 11/10/21	Tue 2/1/22		
119	SCE - SW Higher-Education Solicitation	547 days?	Thu 10/1/20	Fri 11/4/22		
120	SCE - RFA Preparation	89 days	Thu 10/1/20	Tue 2/2/21		
121	SCE - RFA Release	1 day	Thu 2/4/21	Thu 2/4/21		
122	SCE - RFA Abstract Creation Duration	19 days	Fri 2/5/21	Wed 3/3/21		
123	SCE - RFA Evaluation	31 days	Thu 3/4/21	Thu 4/15/21		
124	SCE - RFA Review with EE PRG	1 day	Tue 4/20/21	Tue 4/20/21		
125	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 4/29/21	Thu 4/29/21		
126	SCE - RFP Preparation	39 days	Mon 3/22/21	Thu 5/13/21		
127	SCE - RFP Release	1 day	Fri 5/28/21	Fri 5/28/21		
128	SCE - RFP Proposal Creation Duration	24 days	Fri 6/4/21	Wed 7/7/21		
129	SCE - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21		
130	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/30/21	Mon 8/30/21		
131	SCE - RFP Review with EE PRG	1 day	Tue 8/17/21	Tue 8/17/21		
132	SCE - Contract Negotiation and Development	95 days	Fri 9/3/21	Thu 1/13/22		
133	SCE - Contract Review with EE PRG	1 day	Tue 1/18/22	Tue 1/18/22		
134	SCE - Final Award and Contract Signed	1 day	Sun 3/6/22	Sun 3/6/22		
135	SCE - Submit Advice Letter	1 day	Tue 4/19/22	Tue 4/19/22		
136	SCE - Advice Letter Approved	1 day	Mon 8/15/22	Mon 8/15/22		
137	SCE - Implementation Plan	60 days	Mon 8/15/22	Fri 11/4/22		
138	SCE - Local Equity Residential and SMB	384 days?	Tue 2/15/22	Fri 8/4/23		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
139	SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22		
140	SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22		
141	SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22		
142	SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22		
143	SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22		
144	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22		
145	SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22		
146	SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22		
147	SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22		
148	SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22		
149	SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22		
150	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22		
151	SCE - Contract Negotiation and Development	65 days	Wed 11/2/22	Tue 1/31/23		
152	SCE - Contract Review with EE PRG	1 day	Tue 2/21/23	Tue 2/21/23		
153	SCE - Final Award and Contract Signed	1 day	Thu 3/30/23	Thu 3/30/23		
154	SCE - Submit Advice Letter	22 days	Sun 4/3/22	Mon 5/2/22		
155	SCE - Advice Letter Approved	28 days	Tue 5/2/23	Thu 6/8/23		
156	SCE - Implementation Plan	45 days	Thu 6/8/23	Wed 8/9/23		
157						
158	SCE - Local Equity SMB	431 days?	Tue 2/15/22	Tue 10/10/23		
159	SCE - RFA Preparation	35 days	Tue 2/15/22	Mon 4/4/22		
160	SCE - RFA Release	1 day	Tue 4/5/22	Tue 4/5/22		
161	SCE - RFA Abstract Creation Duration	20 days	Tue 4/5/22	Mon 5/2/22		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
162	SCE - RFA Evaluation	14 days	Mon 5/9/22	Thu 5/26/22		
163	SCE - RFA Review with EE PRG	1 day	Tue 5/31/22	Tue 5/31/22		
164	SCE - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/7/22	Tue 6/7/22		
165	SCE - RFP Preparation	62 days	Mon 4/4/22	Tue 6/28/22		
166	SCE - RFP Release	1 day	Wed 6/29/22	Wed 6/29/22		
167	SCE - RFP Proposal Creation Duration	20 days	Wed 6/29/22	Tue 7/26/22		
168	SCE - RFP Evaluation	47 days	Wed 7/27/22	Thu 9/29/22		
169	SCE - RFP Review with EE PRG	1 day?	Tue 10/18/22	Tue 10/18/22		
170	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/1/22	Tue 11/1/22		
171	SCE - Contract Negotiation and Development	108 days	Wed 11/2/22	Fri 3/31/23		
172	SCE - Contract Review with EE PRG	1 day	Tue 4/18/23	Tue 4/18/23		
173	SCE - Final Award and Contract Signed	1 day	Wed 5/31/23	Wed 5/31/23		
174	SCE - Submit Advice Letter	22 days	Mon 6/6/22	Tue 7/5/22		
175	SCE - Advice Letter Approved	24 days	Thu 7/6/23	Tue 8/8/23		
176	SCE - Implementation Plan	45 days	Wed 8/9/23	Tue 10/10/23		
177	SCE - Local Strategic Energy Management Solicitation	372 days?	Thu 12/1/22	Fri 5/3/24		
178	SCE - RFP Preparation	85 days	Thu 12/1/22	Wed 3/29/23		
179	SCE - RFP Release	1 day	Fri 4/7/23	Fri 4/7/23		
180	SCE - RFP Proposal Creation Duration	35 days	Fri 4/7/23	Thu 5/25/23		
181	SCE - RFP Evaluation	22 days	Thu 6/1/23	Fri 6/30/23		
182	SCE - RFP Review with EE PRG	1 day	Tue 7/18/23	Tue 7/18/23		
183	SCE - Contract Negotiation and Development	86 days	Tue 8/1/23	Tue 11/28/23		
184	SCE - Contract Review with EE PRG	1 day	Tue 12/19/23	Tue 12/19/23		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
185	SCE - Final Award and Contract Signed	6 days	Fri 1/19/24	Fri 1/26/24		
186	SCE - Submit Advice Letter	34 days	Wed 1/31/24	Mon 3/18/24		
187	SCE - Advice Letter Approved	40 days	Tue 3/19/24	Mon 5/13/24		
188	SCE - Local Large Commercial Solicitation	488 days?	Mon 6/26/23	Wed 5/7/25		
189	SCE - RFP Preparation	35 days	Mon 6/26/23	Fri 8/11/23		
190	SCE - RFP Release	1 day	Thu 8/17/23	Thu 8/17/23		
191	SCE - RFP Proposal Creation Duration	41 days	Thu 8/17/23	Thu 10/12/23		
192	SCE - RFP Paused	1 day	Fri 10/13/23	Fri 10/13/23		
193	SCE - Residential Multifamily	326 days?	Fri 9/1/23	Fri 11/29/24		
194	SCE - RFP Preparation	47 days	Fri 9/1/23	Mon 11/6/23		
195	SCE - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23		
196	SCE - RFP Proposal Creation Duration	48 days	Mon 11/6/23	Wed 1/10/24		
197	SCE - RFP Evaluation	25 days	Thu 1/11/24	Wed 2/14/24		
198	SCE - RFP Review with EE PRG	1 day	Tue 2/20/24	Tue 2/20/24		
199	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 2/28/24	Wed 2/28/24		
200	SCE - Contract Negotiation and Development	70 days	Mon 3/4/24	Fri 6/7/24		
201	SCE - Contract Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
202	SCE - Final Award and Contract Signed	15 days	Mon 7/29/24	Fri 8/16/24		
203	SCE - Submit Advice Letter	30 days	Mon 8/19/24	Fri 9/27/24		
204	SCE - Advice Letter Approved	1 day	Mon 10/28/24	Mon 10/28/24		
205	SCE - Local Large Industrial	293 days?	Fri 11/3/23	Tue 12/17/24		
206	SCE - RFP Preparation	17 days	Fri 11/3/23	Mon 11/27/23		
207	SCE - RFP Release	1 day	Mon 12/11/23	Mon 12/11/23		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
208	SCE - RFP Proposal Creation Duration	49 days	Mon 12/11/23	Thu 2/15/24		
209	SCE - RFP Evaluation	35 days	Fri 2/16/24	Thu 4/4/24		
210	SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24		
211	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/23/24	Tue 4/23/24		
212	SCE - Contract Negotiation and Development	208 days	Wed 4/24/24	Fri 2/7/25		
213	SCE - Contract Review with EE PRG	1 day	Tue 3/18/25	Tue 3/18/25		
214	SCE - Final Award and Contract Signed	10 days	Mon 3/31/25	Fri 4/11/25		
215	SCE - Submit Advice Letter	25 days	Mon 4/14/25	Fri 5/16/25		
216	SCE - Advice Letter Approved	22 days	Mon 5/19/25	Tue 6/17/25		
217	SCE - MAP - All Sectors	299 days?	Mon 11/20/23	Thu 1/9/25		
218	SCE - RFP Preparation	20 days	Mon 11/20/23	Fri 12/15/23		
219	SCE - RFP Release	1 day	Mon 1/8/24	Mon 1/8/24		
220	SCE - RFP Proposal Creation Duration	40 days	Mon 1/8/24	Fri 3/1/24		
221	SCE - RFP Evaluation	30 days	Mon 3/4/24	Fri 4/12/24		
222	SCE - RFP Review with EE PRG	1 day	Tue 4/16/24	Tue 4/16/24		
223	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/24/24	Wed 4/24/24		
224	SCE - Contract Negotiation and Development	108 days	Wed 5/1/24	Fri 9/27/24		
225	SCE - Contract Review with EE PRG	1 day	Tue 10/15/24	Tue 10/15/24		
226	SCE - Final Award and Contract Signed	12 days	Tue 10/29/24	Wed 11/13/24		
227	SCE - Submit Advice Letter	43 days	Wed 11/13/24	Fri 1/10/25		
228	SCE - Advice Letter Approved	30 days	Mon 1/13/25	Fri 2/21/25		
229	SCE - Residential	360 days?	Mon 11/20/23	Fri 4/4/25		
230	SCE - RFP Preparation	20 days	Tue 1/16/24	Mon 2/12/24		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	H2	H1
231	SCE - RFP Release	1 day	Thu 3/28/24	Thu 3/28/24		
232	SCE - RFP Proposal Creation Duration	41 days	Thu 3/28/24	Thu 5/23/24		
233	SCE - RFP Evaluation	35 days	Fri 5/24/24	Thu 7/11/24		
234	SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
235	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/5/24	Mon 8/5/24		
236	SCE - Contract Negotiation and Development	80 days	Mon 8/19/24	Fri 12/6/24		
237	SCE - Contract Review with EE PRG	1 day	Tue 12/17/24	Tue 12/17/24		
238	SCE - Final Award and Contract Signed	11 days	Mon 1/13/25	Mon 1/27/25		
239	SCE - Submit Advice Letter	23 days	Mon 2/3/25	Wed 3/5/25		
240	SCE - Advice Letter Approved	22 days	Thu 3/6/25	Fri 4/4/25		
241						
242	SCE - Local Comprehensive Commercial Solicitation	431 days?	Mon 11/13/23	Mon 7/7/25		
243	SCE - RFP Preparation	73 days	Mon 11/13/23	Wed 2/21/24		
244	SCE - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24		
245	SCE - RFP Proposal Creation Duration	43 days	Thu 2/29/24	Mon 4/29/24		
246	SCE - RFP Evaluation	54 days	Tue 4/30/24	Fri 7/12/24		
247	SCE - RFP Review with EE PRG	1 day	Tue 7/16/24	Tue 7/16/24		
248	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Pha	1 day	Mon 7/29/24	Mon 7/29/24		
249	SCE - Contract Negotiation and Development - Phase 1	81 days	Tue 7/30/24	Tue 11/19/24		
250	SCE - Contract Review with EE PRG - Phase 1	1 day	Tue 12/17/24	Tue 12/17/24		
251	SCE - Final Award and Contract Signed - Phase 1	1 day	Thu 2/13/25	Thu 2/13/25		
252	SCE - Submit Advice Letter - Phase 1	20 days	Fri 2/14/25	Thu 3/13/25		
253	SCE - Advice Letter Approved - Phase 1	1 day	Mon 4/14/25	Mon 4/14/25		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
254	SCE - RFP Estimated Notification of Successful and Unsuccessful Bidder - Pha	1 day	Mon 9/30/24	Mon 9/30/24		
255	SCE - Contract Negotiation and Development - Phase 2	80 days	Mon 12/2/24	Fri 3/21/25		
256	SCE - Contract Review with EE PRG - Phase 2	1 day	Tue 4/15/25	Tue 4/15/25		
257	SCE - Final Award and Contract Signed - Phase 2	1 day	Wed 5/14/25	Wed 5/14/25		
258	SCE - Submit Advice Letter - Phase 2	5245 days	Thu 5/19/05	Wed 6/25/25		
259	SCE - Advice Letter Approved - Phase 2	1 day	Fri 7/25/25	Fri 7/25/25		
260						
261	SCG - Local Single Family Solicitation	660 days	Sun 7/1/18	Thu 1/7/21		
262	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18		
263	SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18		
264	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19		
265	SCG - RFA Evaluation	39 days	Mon 1/7/19	Thu 2/28/19		
266	SCG - RFA Review with EE PRG	1 day	Tue 3/5/19	Tue 3/5/19		
267	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19		
268	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19		
269	SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19		
270	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19		
271	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19		
272	SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19		
273	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
274	SCG - Contract Negotiation and Development	69 days	Mon 1/27/20	Thu 4/30/20		
275	SCG - Contract Review with EE PRG	14 days	Tue 5/5/20	Fri 5/22/20		
276	SCG - Final Award and Contract Signed	8 days	Mon 5/25/20	Wed 6/3/20		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
277	SCG - Submit Advice Letter	96 days	Mon 6/1/20	Mon 10/12/20		
278	SCG - Advice Letter Approved	1 day	Thu 11/12/20	Thu 11/12/20		
279	SCG - Implementation Plan	41 days	Fri 11/13/20	Fri 1/8/21		
280	SCG - Local Multi-family Solicitation	735 days	Sun 7/1/18	Thu 4/22/21		
281	SCG - RFA Preparation	105 days	Sun 7/1/18	Thu 11/22/18		
282	SCG - RFA Release	1 day	Mon 11/26/18	Mon 11/26/18		
283	SCG - RFA Abstract Creation Duration	30 days	Tue 11/27/18	Mon 1/7/19		
284	SCG - RFA Evaluation	59 days	Mon 1/7/19	Thu 3/28/19		
285	SCG - RFA Review with EE PRG	1 day	Tue 4/2/19	Tue 4/2/19		
286	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/3/19	Mon 6/3/19		
287	SCG - RFP Preparation	146 days	Wed 1/2/19	Wed 7/24/19		
288	SCG - RFP Release	1 day	Wed 7/31/19	Wed 7/31/19		
289	SCG - RFP Proposal Creation Duration	30 days	Thu 8/1/19	Wed 9/11/19		
290	SCG - RFP Evaluation	37 days	Wed 9/11/19	Thu 10/31/19		
291	SCG - RFP Review with EE PRG	1 day	Tue 11/5/19	Tue 11/5/19		
292	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
293	SCG - Contract Negotiation and Development	155 days	Mon 1/27/20	Fri 8/28/20		
294	SCG - Contract Review with EE PRG	99 days	Tue 5/5/20	Fri 9/18/20		
295	SCG - Final Award and Contract Signed	8 days	Mon 9/21/20	Wed 9/30/20		
296	SCG - Submit Advice Letter	37 days	Thu 10/1/20	Fri 11/20/20		
297	SCG - Advice Letter Approved	1 day	Sun 5/2/21	Sun 5/2/21		
298	SCG - Implementation Plan	51 days	Mon 5/3/21	Mon 7/12/21		
299	SCG - Local Small/Medium Commercial Solicitation	641 days	Tue 9/4/18	Tue 2/16/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
300	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19		
301	SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19		
302	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19		
303	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19		
304	SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19		
305	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19		
306	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19		
307	SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19		
308	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19		
309	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19		
310	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19		
311	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
312	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20		
313	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20		
314	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20		
315	SCG - Submit Advice Letter	59 days	Tue 9/1/20	Fri 11/20/20		
316	SCG - Advice Letter Approved	1 day	Fri 12/18/20	Fri 12/18/20		
317	SCG - Implementation Plan	43 days	Sat 12/19/20	Tue 2/16/21		
318	SCG - Local Small/Medium Public Solicitation	631 days	Tue 9/4/18	Tue 2/2/21		
319	SCG - RFA Preparation	104 days	Tue 9/4/18	Fri 1/25/19		
320	SCG - RFA Release	1 day	Thu 1/31/19	Thu 1/31/19		
321	SCG - RFA Abstract Creation Duration	30 days	Fri 2/1/19	Thu 3/14/19		
322	SCG - RFA Evaluation	52 days	Thu 3/14/19	Fri 5/24/19		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
323	SCG - RFA Review with EE PRG	1 day	Tue 6/4/19	Tue 6/4/19		
324	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 8/1/19	Thu 8/1/19		
325	SCG - RFP Preparation	37 days	Wed 7/3/19	Thu 8/22/19		
326	SCG - RFP Release	1 day	Fri 8/23/19	Fri 8/23/19		
327	SCG - RFP Proposal Creation Duration	31 days	Mon 8/26/19	Mon 10/7/19		
328	SCG - RFP Evaluation	36 days	Tue 10/8/19	Tue 11/26/19		
329	SCG - RFP Review with EE PRG	1 day	Tue 12/3/19	Tue 12/3/19		
330	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 1/21/20	Tue 1/21/20		
331	SCG - Contract Negotiation and Development	135 days	Mon 1/27/20	Fri 7/31/20		
332	SCG - Contract Review with EE PRG	14 days	Tue 8/4/20	Fri 8/21/20		
333	SCG - Final Award and Contract Signed	6 days	Mon 8/24/20	Mon 8/31/20		
334	SCG - Submit Advice Letter	49 days	Tue 9/1/20	Fri 11/6/20		
335	SCG - Advice Letter Approved	1 day	Fri 12/4/20	Fri 12/4/20		
336	SCG - Implementation Plan	43 days	Sat 12/5/20	Tue 2/2/21		
337	SCG - Statewide POS Food Service Solicitation	605 days	Mon 1/21/19	Fri 5/14/21		
338	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19		
339	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19		
340	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19		
341	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19		
342	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19		
343	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20		
344	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19		
345	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	H2	H1
346	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20		
347	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20		
348	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20		
349	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20		
350	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20		
351	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20		
352	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20		
353	SCG - Submit Advice Letter	32 days	Mon 11/2/20	Tue 12/15/20		
354	SCG - Advice Letter Approved	1 day	Thu 1/14/21	Thu 1/14/21		
355	SCG - Implementation Plan	42 days	Fri 1/15/21	Mon 3/15/21		
356	SCG - Statewide Midstream Water Heating Solicitation	597 days	Mon 1/21/19	Tue 5/4/21		
357	SCG - RFA Preparation	143 days	Mon 1/21/19	Wed 8/7/19		
358	SCG - RFA Release	0 days	Mon 8/12/19	Mon 8/12/19		
359	SCG - RFA Abstract Creation Duration	34 days	Tue 8/13/19	Fri 9/27/19		
360	SCG - RFA Evaluation	34 days	Mon 9/30/19	Thu 11/14/19		
361	SCG - RFA Review with EE PRG	0 days	Tue 12/3/19	Tue 12/3/19		
362	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 1/24/20	Fri 1/24/20		
363	SCG - RFP Preparation	24 days	Sat 10/26/19	Wed 11/27/19		
364	SCG - RFP Release	0 days	Wed 1/29/20	Wed 1/29/20		
365	SCG - RFP Proposal Creation Duration	35 days	Thu 1/30/20	Wed 3/18/20		
366	SCG - RFP Evaluation	28 days	Thu 3/19/20	Mon 4/27/20		
367	SCG - RFP Review with EE PRG	0 days	Tue 5/5/20	Tue 5/5/20		
368	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 5/15/20	Fri 5/15/20		

Project: IOU Master Task Timeli
Date: Fri 1/31/25




















Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	H2	H1
369	SCG - Contract Negotiation and Development	90 days	Mon 6/1/20	Fri 10/2/20		
370	SCG - Contract Review with EE PRG	14 days	Tue 10/6/20	Fri 10/23/20		
371	SCG - Final Award and Contract Signed	5 days	Mon 10/26/20	Fri 10/30/20		
372	SCG - Submit Advice Letter	25 days	Mon 11/2/20	Fri 12/4/20		
373	SCG - Advice Letter Approved	1 day	Thu 3/18/21	Thu 3/18/21		
374	SCG - Implementation Plan	22 days	Fri 3/19/21	Mon 4/19/21		
375	SCG - Statewide Gas Emerging Technology Solicitation	738 days	Wed 1/2/19	Fri 10/29/21		
376	SCG - RFA Preparation	283 days	Wed 1/2/19	Fri 1/31/20		
377	SCG - RFA Release	1 day	Wed 2/12/20	Wed 2/12/20		
378	SCG - RFA Abstract Creation Duration	30 days	Thu 2/13/20	Wed 3/25/20		
379	SCG - RFA Evaluation	26 days	Thu 3/26/20	Thu 4/30/20		
380	SCG - RFA Review with EE PRG	1 day	Tue 5/5/20	Tue 5/5/20		
381	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 5/15/20	Fri 5/15/20		
382	SCG - RFP Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
383	SCG - RFP Release	1 day	Fri 8/21/20	Fri 8/21/20		
384	SCG - RFP Proposal Creation Duration	30 days	Mon 8/24/20	Fri 10/2/20		
385	SCG - RFP Evaluation	38 days	Mon 10/5/20	Wed 11/25/20		
386	SCG - RFP Review with EE PRG	1 day	Tue 12/1/20	Tue 12/1/20		
387	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 12/7/20	Mon 12/7/20		
388	SCG - Contract Negotiation and Development	85 days	Mon 1/4/21	Fri 4/30/21		
389	SCG - Contract Review with EE PRG	9 days	Tue 5/4/21	Fri 5/14/21		
390	SCG - Final Award and Contract Signed	29 days	Mon 5/17/21	Thu 6/24/21		
391	SCG - Submit Advice Letter	23 days	Sun 6/27/21	Tue 7/27/21		

Project: IOU Master Task Timeli Date: Fri 1/31/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
392	SCG - Advice Letter Approved	1 day	Tue 8/24/21	Tue 8/24/21		2005
393	SCG - Implementation Plan	44 days	Wed 8/25/21	Sat 10/23/21		H1
394	SCG - Local Manufactured Housing Solicitation	341 days	Fri 11/1/19	Fri 2/19/21		
395	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		
396	SCG - RFA Release	0 days	Fri 2/21/20	Fri 2/21/20		
397	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
398	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
399	SCG - RFA Review with EE PRG	0 days	Tue 6/2/20	Tue 6/2/20		
400	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 6/8/20	Mon 6/8/20		
401	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
402	SCG - RFP Release	0 days	Fri 6/12/20	Fri 6/12/20		
403	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
404	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
405	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
406	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
407	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
408	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
409	SCG - Final Award and Contract Signed	9 days	Thu 12/10/20	Tue 12/22/20		
410	SCG - Submit Advice Letter	0 days	N/A	N/A		
411	SCG - Advice Letter Approved	0 days	N/A	N/A		
412	SCG - Implementation Plan	44 days	Tue 12/22/20	Fri 2/19/21		
413	SCG - Local Large Commercial Solicitation	434 days	Fri 11/1/19	Wed 6/30/21		
414	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
415	SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20		2005
416	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		H1
417	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
418	SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20		
419	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20		
420	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		
421	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20		
422	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
423	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
424	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
425	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
426	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
427	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
428	SCG - Final Award and Contract Signed	10 days	Thu 12/10/20	Wed 12/23/20		
429	SCG - Submit Advice Letter	64 days	Fri 1/1/21	Wed 3/31/21		
430	SCG - Advice Letter Approved	1 day	Fri 6/4/21	Fri 6/4/21		
431	SCG - Implementation Plan	43 days	Sat 6/5/21	Tue 8/3/21		
432	SCG - Local Agricultural Solicitation	434 days	Fri 11/1/19	Wed 6/30/21		
433	SCG - RFA Preparation	66 days	Fri 11/1/19	Fri 1/31/20		
434	SCG - RFA Release	1 day	Fri 2/21/20	Fri 2/21/20		
435	SCG - RFA Abstract Creation Duration	30 days	Mon 2/24/20	Fri 4/3/20		
436	SCG - RFA Evaluation	35 days	Mon 4/6/20	Fri 5/22/20		
437	SCG - RFA Review with EE PRG	1 day	Tue 6/2/20	Tue 6/2/20		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
438	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 6/8/20	Mon 6/8/20		2005
439	SCG - RFP Preparation	43 days	Wed 4/1/20	Fri 5/29/20		H1
440	SCG - RFP Release	1 day	Fri 6/12/20	Fri 6/12/20		
441	SCG - RFP Proposal Creation Duration	30 days	Mon 6/15/20	Fri 7/24/20		
442	SCG - RFP Evaluation	50 days	Mon 7/27/20	Fri 10/2/20		
443	SCG - RFP Review with EE PRG	1 day	Tue 10/6/20	Tue 10/6/20		
444	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/13/20	Tue 10/13/20		
445	SCG - Contract Negotiation and Development	28 days	Mon 10/19/20	Wed 11/25/20		
446	SCG - Contract Review with EE PRG	7 days	Tue 12/1/20	Wed 12/9/20		
447	SCG - Final Award and Contract Signed	2 days	Fri 12/11/20	Mon 12/14/20		
448	SCG - Submit Advice Letter	41 days	Fri 1/1/21	Fri 2/26/21		
449	SCG - Advice Letter Approved	1 day	Wed 4/7/21	Wed 4/7/21		
450	SCG - Implementation Plan	43 days	Thu 4/8/21	Mon 6/7/21		
451	SCG - Local Behavioral Solicitation - Residential	413 days?	Fri 5/1/20	Tue 11/30/21		
452	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
453	SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20		
454	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20		
455	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20		
456	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20		
457	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20		
458	SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20		
459	SCG - RFP Release	1 day	Fri 1/15/21	Fri 1/15/21		
460	SCG - RFP Proposal Creation Duration	26 days	Mon 1/18/21	Mon 2/22/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	H2	H1
461	SCG - RFP Evaluation	29 days	Tue 2/23/21	Fri 4/2/21		
462	SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21		
463	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 4/13/21	Tue 4/13/21		
464	SCG - Contract Negotiation and Development	95 days	Mon 4/26/21	Fri 9/3/21		
465	SCG - Contract Review with EE PRG	9 days	Tue 9/7/21	Fri 9/17/21		
466	SCG - Final Award and Contract Signed	30 days	Mon 9/20/21	Fri 10/29/21		
467	SCG - Submit Advice Letter	21 days	Mon 11/1/21	Mon 11/29/21		
468	SCG - Advice Letter Approved	1 day	Wed 12/22/21	Wed 12/22/21		
469	SCG - Implementation Plan	43 days	Thu 12/23/21	Sun 2/20/22		
470	SCG - Local Behavioral Solicitation - Commercial	413 days?	Fri 5/1/20	Tue 11/30/21		
471	SCG - RFA Preparation	66 days	Fri 5/1/20	Fri 7/31/20		
472	SCG - RFA Release	1 day	Fri 8/21/20	Fri 8/21/20		
473	SCG - RFA Abstract Creation Duration	25 days	Mon 8/24/20	Fri 9/25/20		
474	SCG - RFA Evaluation	25 days	Mon 9/28/20	Fri 10/30/20		
475	SCG - RFA Review with EE PRG	1 day	Tue 11/3/20	Tue 11/3/20		
476	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 11/18/20	Wed 11/18/20		
477	SCG - RFP Preparation	66 days	Thu 10/1/20	Thu 12/31/20		
478	SCG - RFP Release	1 day	Fri 1/22/21	Fri 1/22/21		
479	SCG - RFP Proposal Creation Duration	26 days	Mon 1/25/21	Mon 3/1/21		
480	SCG - RFP Evaluation	24 days	Tue 3/2/21	Fri 4/2/21		
481	SCG - RFP Review with EE PRG	1 day	Tue 4/6/21	Tue 4/6/21		
482	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 11/12/21	Fri 11/12/21		
483	SCG - Contract Negotiation and Development	132 days	Mon 11/29/21	Tue 5/31/22		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
484	SCG - Contract Review with EE PRG	8 days	Sun 6/5/22	Tue 6/14/22		
485	SCG - Final Award and Contract Signed	109 days	Fri 7/1/22	Wed 11/30/22		
486	SCG - Submit Advice Letter	23 days	N/A	N/A		
487	SCG - Advice Letter Approved	1 day	N/A	N/A		
488	SCG - Implementation Plan	43 days	Thu 12/1/22	Sun 1/29/23		
489	SCG - Local Industrial Solicitation	434 days?	Tue 12/1/20	Fri 7/29/22		
490	SCG - RFA Preparation	63 days?	Tue 12/1/20	Thu 2/25/21		
491	SCG - RFA Release	1 day?	Fri 3/19/21	Fri 3/19/21		
492	SCG - RFA Abstract Creation Duration	25 days?	Mon 3/22/21	Fri 4/23/21		
493	SCG - RFA Evaluation	25 days?	Mon 4/26/21	Fri 5/28/21		
494	SCG - RFA Review with EE PRG	1 day?	Tue 6/1/21	Tue 6/1/21		
495	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 6/8/21	Tue 6/8/21		
496	SCG - RFP Preparation	67 days?	Thu 4/1/21	Fri 7/2/21		
497	SCG - RFP Release	1 day?	Fri 7/16/21	Fri 7/16/21		
498	SCG - RFP Proposal Creation Duration	30 days?	Mon 7/19/21	Fri 8/27/21		
499	SCG - RFP Evaluation	25 days?	Mon 8/30/21	Fri 10/1/21		
500	SCG - RFP Review with EE PRG	1 day?	Tue 10/5/21	Tue 10/5/21		
501	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day?	Tue 12/14/21	Tue 12/14/21		
502	SCG - Contract Negotiation and Development	127 days?	Thu 2/3/22	Fri 7/29/22		
503	SCG - Contract Review with EE PRG	9 days?	Tue 8/2/22	Fri 8/12/22		
504	SCG - Final Award and Contract Signed	21 days?	Fri 7/29/22	Fri 8/26/22		
505	SCG - Submit Advice Letter	1 day?	Sun 10/30/22	Sun 10/30/22		
506	SCG - Advice Letter Approved	1 day?	Mon 1/30/23	Mon 1/30/23		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
507	SCG - Implementation Plan	45 days?	Tue 1/31/23	Sat 4/1/23		2005
508	SCG - Large Public Sector Solicitation (re-Bid)	412 days	Mon 1/4/21	Tue 8/2/22		H1
509	SCG - RFA Preparation	65 days	Mon 1/4/21	Fri 4/2/21		
510	SCG - RFA Release	1 day	Fri 7/16/21	Fri 7/16/21		
511	SCG - RFA Abstract Creation Duration	20 days	Mon 7/19/21	Fri 8/13/21		
512	SCG - RFA Evaluation	15 days	Mon 8/16/21	Fri 9/3/21		
513	SCG - RFA Review with EE PRG	1 day	Tue 9/7/21	Tue 9/7/21		
514	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/14/21	Tue 9/14/21		
515	SCG - RFP Preparation	35 days	Mon 9/13/21	Fri 10/29/21		
516	SCG - RFP Release	1 day	Mon 11/8/21	Mon 11/8/21		
517	SCG - RFP Proposal Creation Duration	29 days	Tue 11/9/21	Fri 12/17/21		
518	SCG - RFP Evaluation	30 days	Mon 12/20/21	Fri 1/28/22		
519	SCG - RFP Review with EE PRG	1 day	Tue 2/1/22	Tue 2/1/22		
520	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/8/22	Tue 3/8/22		
521	SCG - Contract Negotiation and Development	79 days	Mon 3/14/22	Thu 6/30/22		
522	SCG - Contract Review with EE PRG	9 days	Tue 7/5/22	Fri 7/15/22		
523	SCG - Final Award and Contract Signed	63 days	Mon 7/18/22	Wed 10/12/22		
524	SCG - Submit Advice Letter	23 days	N/A	N/A		
525	SCG - Advice Letter Approved	1 day	N/A	N/A		
526	SCG - Implementation Plan	44 days	Wed 10/12/22	Sat 12/10/22		
527	SCG - Outreach Solicitation	434 days	Mon 2/1/21	Thu 9/29/22		
528	SCG - RFA Preparation	65 days	Mon 2/1/21	Fri 4/30/21		
529	SCG - RFA Release	1 day	Fri 5/21/21	Fri 5/21/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
530	SCG - RFA Abstract Creation Duration	25 days	Mon 5/24/21	Fri 6/25/21		
531	SCG - RFA Evaluation	25 days	Mon 6/28/21	Fri 7/30/21		
532	SCG - RFA Review with EE PRG	1 day	Tue 8/3/21	Tue 8/3/21		
533	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/10/21	Tue 8/10/21		
534	SCG - RFP Preparation	69 days	Tue 6/1/21	Fri 9/3/21		
535	SCG - RFP Release	1 day	Fri 9/17/21	Fri 9/17/21		
536	SCG - RFP Proposal Creation Duration	30 days	Mon 9/20/21	Fri 10/29/21		
537	SCG - RFP Evaluation	25 days	Mon 11/1/21	Fri 12/3/21		
538	SCG - RFP Review with EE PRG	1 day	Tue 12/7/21	Tue 12/7/21		
539	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 12/14/21	Tue 12/14/21		
540	SCG - Contract Negotiation and Development	54 days	Mon 1/17/22	Thu 3/31/22		
541	SCG - Contract Review with EE PRG	9 days	Tue 4/5/22	Fri 4/15/22		
542	SCG - Final Award and Contract Signed	10 days	Mon 4/18/22	Fri 4/29/22		
543	SCG - Submit Advice Letter	21 days	N/A	N/A		
544	SCG - Advice Letter Approved	1 day	N/A	N/A		
545	SCG - Implementation Plan	43 days	Sat 4/30/22	Tue 6/28/22		
546	SCG - Marketplace Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
547	SCG - RFA Preparation	64 days	Sat 5/1/21	Wed 7/28/21		
548	SCG - RFA Release	1 day	Fri 8/20/21	Fri 8/20/21		
549	SCG - RFA Abstract Creation Duration	25 days	Mon 8/23/21	Fri 9/24/21		
550	SCG - RFA Evaluation	25 days	Mon 9/27/21	Fri 10/29/21		
551	SCG - RFA Review with EE PRG	1 day	Tue 11/2/21	Tue 11/2/21		
552	SCG - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/9/21	Tue 11/9/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
553	SCG - RFP Preparation	91 days	Thu 8/26/21	Thu 12/30/21		
554	SCG - RFP Release	1 day	Fri 1/14/22	Fri 1/14/22		
555	SCG - RFP Proposal Creation Duration	30 days	Mon 1/17/22	Fri 2/25/22		
556	SCG - RFP Evaluation	25 days	Mon 2/28/22	Fri 4/1/22		
557	SCG - RFP Review with EE PRG	1 day	Tue 5/3/22	Tue 5/3/22		
558	SCG - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 5/11/22	Wed 5/11/22		
559	SCG - Contract Negotiation and Development	117 days	Wed 6/22/22	Thu 12/1/22		
560	SCG - Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22		
561	SCG - Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22		
562	SCG - Submit Advice Letter	20 days	Tue 1/3/23	Mon 1/30/23		
563	SCG - Advice Letter Approved	1 day	Tue 5/2/23	Tue 5/2/23		
564	SCG - Implementation Plan	44 days	Wed 5/3/23	Sun 7/2/23		
565	SCG - Residential Multi-Family - Whole Building	436 days?	Mon 3/1/21	Mon 10/31/22		
566	RFA Preparation	40 days	Mon 1/10/22	Fri 3/4/22		
567	RFA Release	1 day	Fri 3/25/22	Fri 3/25/22		
568	RFA Abstract Creation Duration	25 days	Mon 3/28/22	Fri 4/29/22		
569	RFA Evaluation	25 days	Mon 5/2/22	Fri 6/3/22		
570	RFA Review with EE PRG	1 day	Tue 6/7/22	Tue 6/7/22		
571	RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/14/22	Tue 6/14/22		
572	RFP Preparation	28 days	Sun 5/1/22	Tue 6/7/22		
573	RFP Release	1 day	Fri 6/24/22	Fri 6/24/22		
574	RFP Proposal Creation Duration	52 days	Mon 6/27/22	Tue 9/6/22		
575	RFP Evaluation	11 days	Fri 9/9/22	Fri 9/23/22		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
576	RFP Review with EE PRG	1 day	Thu 10/6/22	Thu 10/6/22		
577	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/11/22	Tue 10/11/22		
578	Contract Negotiation and Development	39 days	Tue 10/11/22	Fri 12/2/22		
579	Contract Review with EE PRG	1 day	Tue 12/6/22	Tue 12/6/22		
580	Final Award and Contract Signed	10 days	Mon 12/19/22	Fri 12/30/22		
581	Submit Advice Letter	22 days	Mon 1/2/23	Tue 1/31/23		
582	Advice Letter Approved	1 day	Fri 3/31/23	Fri 3/31/23		
583	Implementation Plan	43 days	Sat 4/1/23	Tue 5/30/23		
584	SCG - Youth Education Outreach Solicitation	331 days	Tue 3/1/22	Tue 6/6/23		
585	SCG - HERS Rater Training Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
586	RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22		
587	RFP Release	1 day	Fri 5/13/22	Fri 5/13/22		
588	RFP Proposal Creation Duration	20 days	Mon 5/16/22	Fri 6/10/22		
589	RFP Evaluation	59 days	Mon 6/13/22	Thu 9/1/22		
590	RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22		
591	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 8/31/22	Wed 8/31/22		
592	Contract Negotiation and Development	53 days	Fri 9/16/22	Tue 11/29/22		
593	Contract Review with EE PRG	9 days	Tue 12/6/22	Fri 12/16/22		
594	Final Award and Contract Signed	9 days	Mon 12/19/22	Thu 12/29/22		
595	Submit Advice Letter	N/A	N/A	N/A		
596	Advice Letter Approved	N/A	N/A	N/A		
597	Implementation Plan	42 days	Fri 12/30/22	Mon 2/27/23		
598	SCG - Retail Partnering Solicitation	29 days?	Tue 9/27/22	Fri 11/4/22		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
599	RFP Preparation	43 days	Tue 3/1/22	Thu 4/28/22		
600	RFP Release	1 day	Fri 6/17/22	Fri 6/17/22		
601	RFP Proposal Creation Duration	30 days	Mon 6/20/22	Fri 7/29/22		
602	RFP Evaluation	24 days	Mon 8/1/22	Thu 9/1/22		
603	RFP Review with EE PRG	1 day	Tue 9/6/22	Tue 9/6/22		
604	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/13/22	Tue 9/13/22		
605	Contract Negotiation and Development	29 days	Mon 9/19/22	Thu 10/27/22		
606	Contract Review with EE PRG	9 days	Tue 11/1/22	Fri 11/11/22		
607	Final Award and Contract Signed	13 days	Mon 11/14/22	Wed 11/30/22		
608	Submit Advice Letter	N/A	N/A	N/A		
609	Advice Letter Approved	N/A	N/A	N/A		
610	Implementation Plan	43 days	Sat 10/1/22	Tue 11/29/22		
611	SCG - Non-Residential EE Advisor Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
612	RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22		
613	RFP Release	1 day	Fri 8/26/22	Fri 8/26/22		
614	RFP Proposal Creation Duration	20 days	Mon 8/29/22	Fri 9/23/22		
615	RFP Evaluation	16 days	Sat 9/24/22	Fri 10/14/22		
616	RFP Review with EE PRG	5 days	Mon 10/17/22	Fri 10/21/22		
617	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/25/22	Tue 10/25/22		
618	Contract Negotiation and Development	32 days	Sun 10/30/22	Mon 12/12/22		
619	Contract Review with EE PRG	9 days	Tue 12/13/22	Fri 12/23/22		
620	Final Award and Contract Signed	4 days	Tue 12/27/22	Fri 12/30/22		
621	Submit Advice Letter	N/A	N/A	N/A		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
622	Advice Letter Approved	N/A	N/A	N/A		2005
623	Implementation Plan	44 days	Sun 1/1/23	Wed 3/1/23		H1
624	SCG - Residential EE Kits Solicitation	436 days?	Mon 3/1/21	Mon 10/31/22		
625	RFP Preparation	46 days	Fri 4/1/22	Fri 6/3/22		
626	RFP Release	1 day	Mon 7/25/22	Mon 7/25/22		
627	RFP Proposal Creation Duration	16 days	Tue 7/26/22	Tue 8/16/22		
628	RFP Evaluation	12 days	Wed 8/17/22	Thu 9/1/22		
629	RFP Review with EE PRG	1 day	Tue 8/2/22	Tue 8/2/22		
630	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 8/9/22	Tue 8/9/22		
631	Contract Negotiation and Development	30 days	Mon 8/22/22	Fri 9/30/22		
632	Contract Review with EE PRG	9 days	Tue 10/4/22	Fri 10/14/22		
633	Final Award and Contract Signed	10 days	Mon 10/17/22	Fri 10/28/22		
634	Submit Advice Letter	N/A	N/A	N/A		
635	Advice Letter Approved	N/A	N/A	N/A		
636	Implementation Plan	43 days	Sat 10/29/22	Tue 12/27/22		
637	SCG - IDEEA 365	230 days	Mon 2/13/23	Fri 12/29/23		
638	RFP Preparation	23 days	Mon 2/13/23	Wed 3/15/23		
639	RFP Release	20 days	Thu 4/20/23	Wed 5/17/23		
640	RFP Proposal Creation Duration	43 days	Wed 5/3/23	Fri 6/30/23		
641	RFP Evaluation	12 days	Fri 7/14/23	Mon 7/31/23		
642	RFP Review with EE PRG	1 day	Tue 8/1/23	Tue 8/1/23		
643	RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Tue 8/1/23	Thu 8/31/23		
644	Contract Negotiation and Development	21 days	Fri 9/1/23	Fri 9/29/23		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
645	Contract Review with EE PRG	32 days	Mon 9/18/23	Tue 10/31/23		
646	Final Award and Contract Signed	17 days	Mon 10/9/23	Tue 10/31/23		
647	Submit Advice Letter	10 days	Wed 11/1/23	Tue 11/14/23		
648	Advice Letter Approved	11 days	Wed 11/22/23	Wed 12/6/23		
649	Implementation Plan	9 days	Tue 12/19/23	Fri 12/29/23		
650	SCG - Commercial SEM	110 days?	Tue 8/1/23	Mon 1/1/24		
651	RFP Preparation	22 days	Tue 8/1/23	Wed 8/30/23		
652	RFP Release	13 days	Wed 9/13/23	Fri 9/29/23		
653	RFP Proposal Creation Duration	11 days	Mon 10/2/23	Mon 10/16/23		
654	RFP Evaluation	5 days	Wed 10/25/23	Tue 10/31/23		
655	RFP Review with EE PRG	2 days	Tue 10/31/23	Wed 11/1/23		
656	RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Thu 11/2/23	Wed 11/8/23		
657	Contract Negotiation and Development	16 days	Wed 10/25/23	Wed 11/15/23		
658	Contract Review with EE PRG	1 day	Tue 12/5/23	Tue 12/5/23		
659	Final Award and Contract Signed	6 days	Wed 12/13/23	Wed 12/20/23		
660	Submit Advice Letter	5 days	Mon 12/18/23	Fri 12/22/23		
661	Advice Letter Approved	1 day	Fri 12/29/23	Fri 12/29/23		
662	Implementation Plan	1 day	Mon 1/1/24	Mon 1/1/24		
663	SCG - Market Access Program	333 days?	Sat 3/16/24	Tue 6/24/25		
664	RFP Preparation	75 days	Sat 3/16/24	Thu 6/27/24		
665	RFP Release	1 day	Fri 6/21/24	Fri 6/21/24		
666	RFP Proposal Creation Duration	53 days	Mon 6/24/24	Wed 9/4/24		
667	RFP Evaluation	38 days	Mon 8/19/24	Wed 10/9/24		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
668	RFP Review with EE PRG	1 day	Tue 10/1/24	Tue 10/1/24		
669	RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/8/24	Tue 10/8/24		
670	Contract Negotiation and Development	78 days	Mon 10/14/24	Wed 1/29/25		
671	Contract Review with EE PRG	10 days	Tue 1/7/25	Mon 1/20/25		
672	Final Award and Contract Signed	11 days	Mon 1/20/25	Mon 2/3/25		
673	Submit Advice Letter	N/A	Wed 1/1/25			
674	Advice Letter Approved	N/A	Mon 3/3/25			
675	Implementation Plan	59 days	Thu 4/3/25	Tue 6/24/25		
676	SCG - IDEEA 365 (Round 3)	230 days?	Tue 10/15/24	Mon 9/1/25		
677	RFP Preparation	23 days	Tue 10/15/24	Thu 11/14/24		
678	RFP Release	20 days	Fri 11/15/24	Thu 12/12/24		
679	RFP Proposal Creation Duration	43 days	Fri 12/13/24	Tue 2/11/25		
680	RFP Evaluation	12 days	Wed 2/12/25	Thu 2/27/25		
681	RFP Review with EE PRG	1 day	Fri 2/28/25	Fri 2/28/25		
682	RFP Estimated Notification of Successful and Unsuccessful Bidder	23 days	Mon 3/3/25	Wed 4/2/25		
683	Contract Negotiation and Development	21 days	Thu 4/3/25	Thu 5/1/25		
684	Contract Review with EE PRG	32 days	Fri 5/2/25	Mon 6/16/25		
685	Final Award and Contract Signed	17 days	Tue 6/17/25	Wed 7/9/25		
686	Submit Advice Letter	10 days	Thu 7/10/25	Wed 7/23/25		
687	Advice Letter Approved	11 days	Thu 7/24/25	Thu 8/7/25		
688	Implementation Plan	9 days	Fri 8/8/25	Wed 8/20/25		
689						
690	<i>Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change</i>					

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
691	SDG&E - Small Commercial (<20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20		
692	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18		
693	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18		
694	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18		
695	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19		
696	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19		
697	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19		
698	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19		
699	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19		
700	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19		
701	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19		
702	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20		
703	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20		
704	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20		
705	SDG&E - Contract Review with EE PRG	0 days	Tue 6/9/20	Tue 6/9/20		
706	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20		
707	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
708	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
709	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
710	SDG&E - Large Commercial (>20kW) Solicitation	612 days	Wed 8/1/18	Thu 12/3/20		
711	SDG&E - RFA Preparation	69 days	Wed 8/1/18	Mon 11/5/18		
712	SDG&E - RFA Release	0 days	Mon 11/5/18	Mon 11/5/18		
713	SDG&E - RFA Abstract Creation Duration	25 days	Mon 11/5/18	Fri 12/7/18		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
714	SDG&E - RFA Evaluation	28 days	Fri 12/7/18	Tue 1/15/19		
715	SDG&E - RFA Review with EE PRG	0 days	Sat 2/2/19	Sat 2/2/19		
716	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 4/1/19	Mon 4/1/19		
717	SDG&E - RFP Preparation	55 days	Tue 4/2/19	Mon 6/17/19		
718	SDG&E - RFP Release	0 days	Tue 6/18/19	Tue 6/18/19		
719	SDG&E - RFP Proposal Creation Duration	51 days	Tue 6/18/19	Tue 8/27/19		
720	SDG&E - RFP Evaluation	48 days	Wed 8/28/19	Fri 11/1/19		
721	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 1/1/20	Wed 1/1/20		
722	SDG&E - Selection Review with EE PRG	0 days	Tue 2/11/20	Tue 2/11/20		
723	SDG&E - Contract Negotiation and Development	55 days	Mon 2/17/20	Fri 5/1/20		
724	SDG&E - Contract Review with EE PRG	0 days	Tue 5/12/20	Tue 5/12/20		
725	SDG&E - Final Award and Contract Signed	0 days	Tue 6/30/20	Tue 6/30/20		
726	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
727	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
728	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
729	SDG&E - Residential Multi-Family Solicitation	586 days	Thu 9/6/18	Thu 12/3/20		
730	SDG&E - RFA Preparation	64 days	Thu 9/6/18	Tue 12/4/18		
731	SDG&E - RFA Release	23 days	Tue 12/4/18	Thu 1/3/19		
732	SDG&E - RFA Abstract Creation Duration	49 days	Tue 9/11/18	Fri 11/16/18		
733	SDG&E - RFA Evaluation	21 days	Mon 1/7/19	Mon 2/4/19		
734	SDG&E - RFA Review with EE PRG	0 days	Tue 11/13/18	Tue 11/13/18		
735	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 3/20/19	Wed 3/20/19		
736	SDG&E - RFP Preparation	63 days	Fri 3/22/19	Tue 6/18/19		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	H2	H1
737	SDG&E - RFP Release	52 days	Tue 6/18/19	Wed 8/28/19		
738	SDG&E - RFP Proposal Creation Duration	36 days	Mon 3/25/19	Mon 5/13/19		
739	SDG&E - RFP Evaluation	30 days	Thu 8/29/19	Wed 10/9/19		
740	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Thu 12/12/19	Thu 12/19/19		
741	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
742	SDG&E - Contract Negotiation and Development	35 days	Mon 4/13/20	Fri 5/29/20		
743	SDG&E - Contract Review with EE PRG	10 days	Thu 6/4/20	Wed 6/17/20		
744	SDG&E - Final Award and Contract Signed	0 days	Mon 6/22/20	Mon 6/22/20		
745	SDG&E - Submit Advice Letter	0 days	Wed 8/12/20	Wed 8/12/20		
746	SDG&E - Advice Letter Approved	23 days	Wed 8/12/20	Fri 9/11/20		
747	SDG&E - Implementation Plan	60 days	Fri 9/11/20	Thu 12/3/20		
748	SDG&E - SW HVAC Solicitation	593 days	Thu 11/1/18	Tue 2/9/21		
749	SDG&E - RFA Preparation	48 days	Thu 11/1/18	Mon 1/7/19		
750	SDG&E - RFA Release	0 days	Mon 1/7/19	Mon 1/7/19		
751	SDG&E - RFA Abstract Creation Duration	24 days	Mon 1/7/19	Thu 2/7/19		
752	SDG&E - RFA Evaluation	37 days	Fri 2/8/19	Sun 3/31/19		
753	SDG&E - RFA Review with EE PRG	0 days	Tue 4/9/19	Tue 4/9/19		
754	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 4/17/19	Wed 4/17/19		
755	SDG&E - RFP Preparation	73 days	Thu 4/18/19	Mon 7/29/19		
756	SDG&E - RFP Release	0 days	Tue 9/3/19	Tue 9/3/19		
757	SDG&E - RFP Proposal Creation Duration	30 days	Tue 9/3/19	Mon 10/14/19		
758	SDG&E - RFP Evaluation	33 days	Mon 10/14/19	Wed 11/27/19		
759	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 1/21/20	Tue 1/21/20		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
760	SDG&E - Selection Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
761	SDG&E - Contract Negotiation and Development	88 days	Wed 3/25/20	Fri 7/24/20		
762	SDG&E - Contract Review with EE PRG	0 days	Tue 9/8/20	Tue 9/8/20		
763	SDG&E - Final Award and Contract Signed	0 days	Fri 10/30/20	Fri 10/30/20		
764	SDG&E - Submit Advice Letter	0 days	Thu 11/12/20	Thu 11/12/20		
765	SDG&E - Advice Letter Approved	0 days	Fri 12/11/20	Fri 12/11/20		
766	SDG&E - Implementation Plan	0 days	Tue 2/9/21	Tue 2/9/21		
767	SDG&E - SW PLA Solicitation	853 days	Mon 1/28/19	Wed 5/4/22		
768	SDG&E - RFA Preparation	75 days	Mon 1/28/19	Fri 5/10/19		
769	SDG&E - RFA Release	0 days	Fri 5/10/19	Fri 5/10/19		
770	SDG&E - RFA Abstract Creation Duration	31 days	Fri 5/10/19	Fri 6/21/19		
771	SDG&E - RFA Evaluation	65 days	Mon 6/24/19	Fri 9/20/19		
772	SDG&E - RFA Review with EE PRG	0 days	Tue 9/10/19	Tue 9/10/19		
773	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Fri 9/20/19	Fri 9/20/19		
774	SDG&E - RFP Preparation	52 days	Fri 9/20/19	Mon 12/2/19		
775	SDG&E - RFP Release	0 days	Mon 1/27/20	Mon 1/27/20		
776	SDG&E - RFP Proposal Creation Duration	31 days	Mon 1/27/20	Mon 3/9/20		
777	SDG&E - RFP Evaluation	82 days	Mon 3/9/20	Tue 6/30/20		
778	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 8/17/20	Mon 8/17/20		
779	SDG&E - Selection Review with EE PRG	66 days	Tue 10/13/20	Tue 1/12/21		
780	SDG&E - Contract Negotiation and Development	197 days	Fri 1/29/21	Mon 11/1/21		
781	SDG&E - Contract Review with EE PRG	0 days	Tue 11/9/21	Tue 11/9/21		
782	SDG&E - Final Award and Contract Signed	0 days	Fri 1/7/22	Fri 1/7/22		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
783	SDG&E - Submit Advice Letter	0 days	Mon 1/10/22	Mon 1/10/22		
784	SDG&E - Advice Letter Approved	0 days	Thu 2/10/22	Thu 2/10/22		
785	SDG&E - Implementation Plan	60 days	Thu 2/10/22	Wed 5/4/22		
786	SDG&E - Residential Single-Family 2.0 Solicitation	467 days	Tue 1/19/21	Wed 11/2/22		
787	SDG&E - RFA Preparation	43 days	Tue 1/19/21	Thu 3/18/21		
788	SDG&E - RFA Release	0 days	Mon 3/22/21	Mon 3/22/21		
789	SDG&E - RFA Abstract Creation Duration	22 days	Mon 3/22/21	Tue 4/20/21		
790	SDG&E - RFA Evaluation	38 days	Wed 4/21/21	Fri 6/11/21		
791	SDG&E - RFA Review with EE PRG	7 days	Thu 6/3/21	Fri 6/11/21		
792	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 6/15/21	Tue 6/15/21		
793	SDG&E - RFP Preparation	43 days	Wed 6/16/21	Fri 8/13/21		
794	SDG&E - RFP Release	0 days	Wed 8/18/21	Wed 8/18/21		
795	SDG&E - RFP Proposal Creation Duration	32 days	Wed 8/18/21	Thu 9/30/21		
796	SDG&E - RFP Evaluation	44 days	Fri 10/1/21	Wed 12/1/21		
797	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 12/14/21	Tue 12/14/21		
798	SDG&E - Selection Review with EE PRG	7 days	Thu 12/2/21	Fri 12/10/21		
799	SDG&E - Contract Negotiation and Development	96 days	Mon 12/20/21	Mon 5/2/22		
800	SDG&E - Contract Review with EE PRG	7 days	Thu 5/5/22	Fri 5/13/22		
801	SDG&E - Final Award and Contract Signed	0 days	Tue 5/31/22	Tue 5/31/22		
802	SDG&E - Submit Advice Letter	0 days	Fri 6/24/22	Fri 6/24/22		
803	SDG&E - Advice Letter Approved	0 days	Thu 8/11/22	Thu 8/11/22		
804	SDG&E - Implementation Plan	60 days	Thu 8/11/22	Wed 11/2/22		
805	SDG&E - Residential Single-Family Solicitation	501 days	Mon 7/1/19	Tue 6/1/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
806	SDG&E - RFA Preparation	80 days	Mon 7/1/19	Fri 10/18/19		
807	SDG&E - RFA Release	35 days	Fri 10/18/19	Thu 12/5/19		
808	SDG&E - RFA Abstract Creation Duration	53 days	Mon 7/22/19	Wed 10/2/19		
809	SDG&E - RFA Evaluation	29 days	Fri 12/6/19	Wed 1/15/20		
810	SDG&E - RFA Review with EE PRG	0 days	Tue 10/8/19	Tue 10/8/19		
811	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Thu 2/27/20	Thu 2/27/20		
812	SDG&E - RFP Preparation	48 days	Fri 2/28/20	Tue 5/5/20		
813	SDG&E - RFP Release	0 days	Mon 4/27/20	Mon 4/27/20		
814	SDG&E - RFP Proposal Creation Duration	32 days	Mon 4/27/20	Tue 6/9/20		
815	SDG&E - RFP Evaluation	16 days	Wed 6/10/20	Wed 7/1/20		
816	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	2 days	Thu 7/23/20	Fri 7/24/20		
817	SDG&E - Selection Review with EE PRG	7 days	Thu 8/6/20	Fri 8/14/20		
818	SDG&E - Contract Negotiation and Development	60 days	Mon 8/17/20	Fri 11/6/20		
819	SDG&E - Contract Review with EE PRG	10 days	Tue 12/8/20	Mon 12/21/20		
820	SDG&E - Final Award and Contract Signed	0 days	Fri 1/29/21	Fri 1/29/21		
821	SDG&E - Submit Advice Letter	0 days	Mon 3/1/21	Mon 3/1/21		
822	SDG&E - Advice Letter Approved					
823	SDG&E - Implementation Plan	0 days	Tue 6/1/21	Tue 6/1/21		
824	SDG&E - Public Sector: Federal Solicitation	625 days	Mon 7/1/19	Fri 11/19/21		
825	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19		
826	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19		
827	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19		
828	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
829	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
830	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20		
831	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20		
832	SDG&E - RFP Release	0 days	Fri 5/22/20	Fri 5/22/20		
833	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20		
834	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20		
835	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20		
836	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20		
837	SDG&E - Contract Negotiation and Development	53 days	Wed 2/17/21	Fri 4/30/21		
838	SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21		
839	SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21		
840	SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21		
841	SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21		
842	SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21		
843	SDG&E - Public Sector: K-12 Solicitation	625 days	Mon 7/1/19	Fri 11/19/21		
844	SDG&E - RFA Preparation	78 days	Mon 7/1/19	Wed 10/16/19		
845	SDG&E - RFA Release	0 days	Wed 10/16/19	Wed 10/16/19		
846	SDG&E - RFA Abstract Creation Duration	31 days	Wed 10/16/19	Wed 11/27/19		
847	SDG&E - RFA Evaluation	39 days	Tue 12/3/19	Fri 1/24/20		
848	SDG&E - RFA Review with EE PRG	0 days	Tue 3/10/20	Tue 3/10/20		
849	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Mon 3/23/20	Mon 3/23/20		
850	SDG&E - RFP Preparation	22 days	Thu 3/26/20	Fri 4/24/20		
851	SDG&E - RFP Release	1 day	Fri 5/22/20	Fri 5/22/20		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
852	SDG&E - RFP Proposal Creation Duration	40 days	Fri 5/22/20	Thu 7/16/20		
853	SDG&E - RFP Evaluation	30 days	Fri 7/17/20	Thu 8/27/20		
854	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Wed 11/18/20	Wed 11/18/20		
855	SDG&E - Selection Review with EE PRG	0 days	Tue 11/10/20	Tue 11/10/20		
856	SDG&E - Contract Negotiation and Development	117 days	Thu 11/19/20	Fri 4/30/21		
857	SDG&E - Contract Review with EE PRG	0 days	Tue 5/11/21	Tue 5/11/21		
858	SDG&E - Final Award and Contract Signed	0 days	Thu 7/1/21	Thu 7/1/21		
859	SDG&E - Submit Advice Letter	0 days	Wed 7/21/21	Wed 7/21/21		
860	SDG&E - Advice Letter Approved	0 days	Fri 8/27/21	Fri 8/27/21		
861	SDG&E - Implementation Plan	60 days	Mon 8/30/21	Fri 11/19/21		
862	SDG&E - Public Sector: Local Government Solicitation	338 days	Tue 10/13/20	Thu 1/27/22		
863	SDG&E - RFA Preparation	10 days	Fri 10/23/20	Thu 11/5/20		
864	SDG&E - RFA Release	1 day	Wed 1/27/21	Wed 1/27/21		
865	SDG&E - RFA Abstract Creation Duration	20 days	Thu 1/28/21	Wed 2/24/21		
866	SDG&E - RFA Evaluation	18 days	Fri 2/26/21	Tue 3/23/21		
867	SDG&E - RFA Review with EE PRG	7 days	Thu 4/8/21	Fri 4/16/21		
868	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 4/21/21	Wed 4/21/21		
869	SDG&E - RFP Preparation	51 days	Fri 3/19/21	Fri 5/28/21		
870	SDG&E - RFP Release	1 day	Tue 6/1/21	Tue 6/1/21		
871	SDG&E - RFP Proposal Creation Duration	26 days	Wed 6/2/21	Wed 7/7/21		
872	SDG&E - RFP Evaluation	26 days	Thu 7/8/21	Thu 8/12/21		
873	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/25/21	Mon 10/25/21		
874	SDG&E - Selection Review with EE PRG	7 days	Tue 10/12/21	Wed 10/20/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
875	SDG&E - Contract Negotiation and Development	41 days	Fri 11/5/21	Fri 12/31/21		2005
876	SDG&E - Contract Review with EE PRG	7 days	Thu 1/6/22	Fri 1/14/22		H1
877	SDG&E - Final Award and Contract Signed	9 days	Mon 1/17/22	Thu 1/27/22		
878	SDG&E - Submit Advice Letter	13 days	Wed 6/1/22	Fri 6/17/22		
879	SDG&E - Advice Letter Approved	40 days	Fri 6/17/22	Thu 8/11/22		
880	SDG&E - Implementation Plan	42 days	Mon 8/15/22	Tue 10/11/22		
881	SDG&E - Agricultural Sector: Local Agriculture Solicitation	447 days	Mon 3/1/21	Tue 11/15/22		
882	SDG&E - RFA Preparation	56 days	Mon 3/1/21	Mon 5/17/21		
883	SDG&E - RFA Release	0 days	Mon 4/26/21	Mon 4/26/21		
884	SDG&E - RFA Abstract Creation Duration	20 days	Tue 4/27/21	Mon 5/24/21		
885	SDG&E - RFA Evaluation	36 days	Tue 6/1/21	Tue 7/20/21		
886	SDG&E - RFA Review with EE PRG	0 days	Thu 7/8/21	Thu 7/8/21		
887	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 7/20/21	Tue 7/20/21		
888	SDG&E - RFP Preparation	48 days	Tue 7/20/21	Thu 9/23/21		
889	SDG&E - RFP Release	0 days	Thu 9/23/21	Thu 9/23/21		
890	SDG&E - RFP Proposal Creation Duration	25 days	Fri 9/24/21	Thu 10/28/21		
891	SDG&E - RFP Evaluation	23 days	Thu 10/28/21	Mon 11/29/21		
892	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	0 days	Tue 2/1/22	Tue 2/1/22		
893	SDG&E - Selection Review with EE PRG	0 days	Tue 2/8/22	Tue 2/8/22		
894	SDG&E - Contract Negotiation and Development	83 days	Tue 2/1/22	Thu 5/26/22		
895	SDG&E - Contract Review with EE PRG	0 days	Tue 6/14/22	Tue 6/14/22		
896	SDG&E - Final Award and Contract Signed	10 days	Fri 6/18/21	Thu 7/1/21		
897	SDG&E - Submit Advice Letter	0 days	Fri 7/22/22	Fri 7/22/22		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
898	SDG&E - Advice Letter Approved	0 days	Tue 8/30/22	Tue 8/30/22		
899	SDG&E - Implementation Plan	44 days	Wed 8/31/22	Sat 10/29/22		
900	*SDG&E - Industrial Solicitation	426 days	Thu 4/1/21	Thu 11/17/22		
901	SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21		
902	SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21		
903	SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21		
904	SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21		
905	SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21		
906	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21		
907	SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21		
908	SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21		
909	SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22		
910	SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22		
911	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22		
912	SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22		
913	SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22		
914	SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22		
915	SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22		
916	SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22		
917	SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22		
918	SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23		
919	*SDG&E - Industrial-Port Tenants Solicitation	426 days	Thu 4/1/21	Thu 11/17/22		
920	SDG&E - RFA Preparation	56 days	Thu 4/1/21	Thu 6/17/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
921	SDG&E - RFA Release	1 day	Fri 6/18/21	Fri 6/18/21		
922	SDG&E - RFA Abstract Creation Duration	24 days	Mon 6/21/21	Thu 7/22/21		
923	SDG&E - RFA Evaluation	29 days	Fri 7/23/21	Wed 9/1/21		
924	SDG&E - RFA Review with EE PRG	7 days	Thu 9/2/21	Fri 9/10/21		
925	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/21/21	Tue 9/21/21		
926	SDG&E - RFP Preparation	41 days	Wed 9/22/21	Wed 11/17/21		
927	SDG&E - RFP Release	1 day	Thu 11/18/21	Thu 11/18/21		
928	SDG&E - RFP Proposal Creation Duration	37 days	Thu 11/18/21	Fri 1/7/22		
929	SDG&E - RFP Evaluation	26 days	Mon 1/10/22	Mon 2/14/22		
930	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Fri 3/25/22	Fri 3/25/22		
931	SDG&E - Selection Review with EE PRG	7 days	Thu 3/17/22	Fri 3/25/22		
932	SDG&E - Contract Negotiation and Development	87 days	Mon 3/28/22	Tue 7/26/22		
933	SDG&E - Contract Review with EE PRG	1 day	Wed 7/27/22	Wed 7/27/22		
934	SDG&E - Final Award and Contract Signed	18 days	Mon 8/8/22	Wed 8/31/22		
935	SDG&E - Submit Advice Letter	1 day	Wed 9/21/22	Wed 9/21/22		
936	SDG&E - Advice Letter Approved	1 day	Fri 12/9/22	Fri 12/9/22		
937	SDG&E - Implementation Plan	60 days	Fri 12/9/22	Thu 3/2/23		
938	*SDG&E - SW Residential HVAC QI/QM Solicitation	377 days	Mon 7/5/21	Tue 12/13/22		
939	SDG&E - RFA Preparation	48 days	Mon 7/5/21	Wed 9/8/21		
940	SDG&E - RFA Release	1 day	Wed 9/29/21	Wed 9/29/21		
941	SDG&E - RFA Abstract Creation Duration	22 days	Wed 9/29/21	Thu 10/28/21		
942	SDG&E - RFA Evaluation	21 days	Fri 10/29/21	Fri 11/26/21		
943	SDG&E - RFA Review with EE PRG	6 days	Fri 12/10/21	Fri 12/17/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
944	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 12/22/21	Wed 12/22/21		
945	SDG&E - RFP Preparation	56 days	Tue 1/4/22	Tue 3/22/22		
946	SDG&E - RFP Release	1 day	Tue 3/22/22	Tue 3/22/22		
947	SDG&E - RFP Proposal Creation Duration	23 days	Wed 3/23/22	Fri 4/22/22		
948	SDG&E - RFP Evaluation	20 days	Mon 4/25/22	Fri 5/20/22		
949	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/21/22	Tue 6/21/22		
950	SDG&E - Selection Review with EE PRG	0 days	Fri 6/17/22	Fri 6/17/22		
951	SDG&E - Contract Negotiation and Development	83 days	Wed 7/20/22	Fri 11/11/22		
952	SDG&E - Contract Review with EE PRG	6 days	Mon 11/14/22	Mon 11/21/22		
953	SDG&E - Final Award and Contract Signed	1 day	Mon 1/10/22	Mon 1/10/22		
954	SDG&E - Submit Advice Letter	22 days	Sun 1/15/23	Mon 2/13/23		
955	SDG&E - Advice Letter Approved	1 day	Fri 4/28/23	Fri 4/28/23		
956	SDG&E - Implementation Plan	60 days	Fri 4/28/23	Thu 7/20/23		
957	*SDG&E - Local/Residential Behavioral Solicitation	472 days	Mon 4/19/21	Tue 2/7/23		
958	SDG&E - RFA Preparation	53 days	Mon 4/19/21	Wed 6/30/21		
959	SDG&E - RFA Release	1 day	Mon 7/26/21	Mon 7/26/21		
960	SDG&E - RFA Abstract Creation Duration	21 days	Mon 7/26/21	Mon 8/23/21		
961	SDG&E - RFA Evaluation	30 days	Tue 8/24/21	Mon 10/4/21		
962	SDG&E - RFA Review with EE PRG	7 days	Thu 10/7/21	Fri 10/15/21		
963	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 10/19/21	Tue 10/19/21		
964	SDG&E - RFP Preparation	28 days	Thu 10/21/21	Mon 11/29/21		
965	SDG&E - RFP Release	1 day	Wed 12/22/21	Wed 12/22/21		
966	SDG&E - RFP Proposal Creation Duration	20 days	Wed 12/22/21	Tue 1/18/22		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
967	SDG&E - RFP Evaluation	28 days	Wed 1/19/22	Fri 2/25/22		
968	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/15/22	Tue 3/15/22		
969	SDG&E - Selection Review with EE PRG	7 days	Thu 3/3/22	Fri 3/11/22		
970	SDG&E - Contract Negotiation and Development	119 days	Fri 3/18/22	Wed 8/31/22		
971	SDG&E - Contract Review with EE PRG	7 days	Thu 9/8/22	Fri 9/16/22		
972	SDG&E - Final Award and Contract Signed	1 day	Fri 10/21/22	Fri 10/21/22		
973	SDG&E - Submit Advice Letter	1 day	Wed 11/16/22	Wed 11/16/22		
974	SDG&E - Advice Letter Approved	1 day	Fri 12/16/22	Fri 12/16/22		
975	SDG&E - Implementation Plan	60 days	Wed 11/16/22	Tue 2/7/23		
976	*SDG&E - Small Business Outreach Solicitation	298 days?	Wed 4/13/22	Fri 6/2/23		
977	SDG&E - RFA Preparation	53 days	Wed 4/13/22	Fri 6/24/22		
978	SDG&E - RFA Release	1 day	Thu 7/7/22	Thu 7/7/22		
979	SDG&E - RFA Abstract Creation Duration	21 days	Fri 7/8/22	Fri 8/5/22		
980	SDG&E - RFA Evaluation	30 days	Mon 8/8/22	Fri 9/16/22		
981	SDG&E - RFA Review with EE PRG	5 days	Mon 9/19/22	Fri 9/23/22		
982	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/27/22	Tue 9/27/22		
983	SDG&E - RFP Preparation	28 days	Mon 8/8/22	Wed 9/14/22		
984	SDG&E - RFP Release	1 day	Tue 10/18/22	Tue 10/18/22		
985	SDG&E - RFP Proposal Creation Duration	31 days	Tue 10/18/22	Tue 11/29/22		
986	SDG&E - RFP Evaluation	38 days	Wed 11/30/22	Fri 1/20/23		
987	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 2/28/23	Tue 2/28/23		
988	SDG&E - Selection Review with EE PRG	7 days	Thu 2/16/23	Fri 2/24/23		
989	SDG&E - Contract Negotiation and Development	79 days	Tue 2/28/23	Fri 6/16/23		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
990	SDG&E - Contract Review with EE PRG	4 days	Wed 6/21/23	Mon 6/26/23		
991	SDG&E - Final Award and Contract Signed	1 day	Tue 8/29/23	Tue 8/29/23		
992	SDG&E - Submit Advice Letter	1 day	Fri 9/15/23	Fri 9/15/23		
993	SDG&E - Advice Letter Approved	1 day	Mon 10/16/23	Mon 10/16/23		
994	SDG&E - Implementation Plan	46 days	Mon 10/16/23	Mon 12/18/23		
995	*SDG&E - Workforce Education & Training /Integrated Energy Education Solicitatio	353 days?	Mon 1/16/23	Wed 5/22/24		
996	SDG&E - RFP Release	1 day?	Thu 2/2/23	Thu 2/2/23		
997	SDG&E - RFP Evaluation	25 days	Fri 3/17/23	Thu 4/20/23		
998	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/16/23	Tue 5/16/23		
999	SDG&E - Selection Review with EE PRG	5 days	Tue 5/9/23	Mon 5/15/23		
1000	SDG&E - Contract Negotiation and Development	94 days	Fri 5/5/23	Wed 9/13/23		
1001	SDG&E - Contract Review with EE PRG	7 days	Tue 10/10/23	Wed 10/18/23		
1002	SDG&E - Final Award and Contract Signed	1 day	Tue 11/14/23	Tue 11/14/23		
1003	SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24		
1004	SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24		
1005	SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24		
1006	*SDG&E - Residential Equity Education & Outreach Solicitation	331 days?	Fri 1/13/23	Fri 4/19/24		
1007	SDG&E - RFA Release	1 day	Thu 3/2/23	Thu 3/2/23		
1008	SDG&E - RFA Evaluation	21 days	Wed 4/12/23	Wed 5/10/23		
1009	SDG&E - RFA Review with EE PRG	7 days	Fri 5/19/23	Mon 5/29/23		
1010	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 5/30/23	Tue 5/30/23		
1011	SDG&E - RFP Release	1 day	Thu 6/1/23	Thu 6/1/23		
1012	SDG&E - RFP Evaluation	27 days	Mon 7/17/23	Tue 8/22/23		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1013	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 8/28/23	Mon 8/28/23		
1014	SDG&E - Selection Review with EE PRG	7 days	Wed 8/30/23	Thu 9/7/23		
1015	SDG&E - Contract Negotiation and Development	32 days	Thu 11/2/23	Fri 12/15/23		
1016	SDG&E - Contract Review with EE PRG	7 days	Tue 1/9/24	Wed 1/17/24		
1017	SDG&E - Final Award and Contract Signed	1 day	Mon 2/12/24	Mon 2/12/24		
1018	SDG&E - Submit Advice Letter	1 day	Mon 2/26/24	Mon 2/26/24		
1019	SDG&E - Advice Letter Approved	1 day	Mon 4/8/24	Mon 4/8/24		
1020	SDG&E - Implementation Plan	60 days	Tue 4/9/24	Mon 7/1/24		
1021	*SDG&E - Non-Residential Behavioral Solicitation	398 days	Mon 8/15/22	Wed 2/21/24		
1022	SDG&E - RFA Preparation	67 days	Mon 8/15/22	Tue 11/15/22		
1023	SDG&E - RFA Release	1 day	Mon 10/24/22	Mon 10/24/22		
1024	SDG&E - RFA Abstract Creation Duration	27 days	Tue 8/23/22	Wed 9/28/22		
1025	SDG&E - RFA Evaluation	16 days	Tue 11/29/22	Tue 12/20/22		
1026	SDG&E - RFA Review with EE PRG	7 days	Thu 1/5/23	Fri 1/13/23		
1027	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Wed 1/18/23	Wed 1/18/23		
1028	SDG&E - RFP Preparation	26 days	Mon 11/14/22	Mon 12/19/22		
1029	SDG&E - RFP Release	1 day	Mon 1/23/23	Mon 1/23/23		
1030	SDG&E - RFP Proposal Creation Duration	26 days	Mon 1/23/23	Mon 2/27/23		
1031	SDG&E - RFP Evaluation	58 days	Tue 2/28/23	Thu 5/18/23		
1032	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/20/23	Tue 6/20/23		
1033	SDG&E - Selection Review with EE PRG	7 days	Thu 6/8/23	Fri 6/16/23		
1034	SDG&E - Contract Negotiation and Development	60 days	Wed 6/21/23	Tue 9/12/23		
1035	SDG&E - Contract Review with EE PRG	7 days	Thu 10/5/23	Fri 10/13/23		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1036	SDG&E - Final Award and Contract Signed	1 day	Thu 12/21/23	Thu 12/21/23		
1037	SDG&E - Submit Advice Letter	1 day	Fri 1/12/24	Fri 1/12/24		
1038	SDG&E - Advice Letter Approved	1 day	Mon 2/12/24	Mon 2/12/24		
1039	SDG&E - Implementation Plan	60 days	Mon 2/12/24	Fri 5/3/24		
1040	*SDG&E - Retail Offices and Wholesale Solicitation	398 days	Wed 5/10/23	Fri 11/15/24		
1041	SDG&E - RFA Preparation	33 days	Wed 5/10/23	Fri 6/23/23		
1042	SDG&E - RFA Release	1 day	Mon 7/3/23	Mon 7/3/23		
1043	SDG&E - RFA Abstract Creation Duration	31 days	Tue 7/4/23	Tue 8/15/23		
1044	SDG&E - RFA Evaluation	19 days	Wed 8/16/23	Mon 9/11/23		
1045	SDG&E - RFA Review with EE PRG	3 days	Mon 9/18/23	Wed 9/20/23		
1046	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 9/25/23	Mon 9/25/23		
1047	SDG&E - RFP Preparation	33 days	Wed 7/5/23	Fri 8/18/23		
1048	SDG&E - RFP Release	1 day	Fri 9/29/23	Fri 9/29/23		
1049	SDG&E - RFP Proposal Creation Duration	33 days	Mon 10/2/23	Wed 11/15/23		
1050	SDG&E - RFP Evaluation	25 days	Thu 11/16/23	Wed 12/20/23		
1051	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 2/19/24	Mon 2/19/24		
1052	SDG&E - Selection Review with EE PRG	7 days	Thu 2/8/24	Fri 2/16/24		
1053	SDG&E - Contract Negotiation and Development	96 days	Mon 2/26/24	Mon 7/8/24		
1054	SDG&E - Contract Review with EE PRG	6 days	Wed 7/17/24	Wed 7/24/24		
1055	SDG&E - Final Award and Contract Signed	1 day	Tue 8/27/24	Tue 8/27/24		
1056	SDG&E - Submit Advice Letter	1 day	Mon 9/16/24	Mon 9/16/24		
1057	SDG&E - Advice Letter Approved	1 day	Mon 10/14/24	Mon 10/14/24		
1058	SDG&E - Implementation Plan	46 days	Mon 10/14/24	Mon 12/16/24		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1059	*SDG&E - Groceries, Restaurants and Food Storage Solicitation	398 days	Wed 6/14/23	Fri 12/20/24		
1060	SDG&E - RFA Preparation	33 days	Wed 6/14/23	Fri 7/28/23		
1061	SDG&E - RFA Release	1 day	Tue 8/15/23	Tue 8/15/23		
1062	SDG&E - RFA Abstract Creation Duration	21 days	Wed 8/16/23	Wed 9/13/23		
1063	SDG&E - RFA Evaluation	15 days	Thu 9/14/23	Wed 10/4/23		
1064	SDG&E - RFA Review with EE PRG	5 days	Wed 10/18/23	Tue 10/24/23		
1065	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 10/30/23	Mon 10/30/23		
1066	SDG&E - RFP Preparation	16 days	Mon 10/9/23	Mon 10/30/23		
1067	SDG&E - RFP Release	1 day	Mon 11/6/23	Mon 11/6/23		
1068	SDG&E - RFP Proposal Creation Duration	33 days	Mon 11/6/23	Wed 12/20/23		
1069	SDG&E - RFP Evaluation	34 days	Thu 12/21/23	Tue 2/6/24		
1070	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Thu 2/22/24	Thu 2/22/24		
1071	SDG&E - Selection Review with EE PRG	7 days	Thu 2/29/24	Fri 3/8/24		
1072	SDG&E - Contract Negotiation and Development	60 days	Tue 2/27/24	Mon 5/20/24		
1073	SDG&E - Contract Review with EE PRG	9 days	Thu 6/27/24	Tue 7/9/24		
1074	SDG&E - Final Award and Contract Signed	1 day	Mon 7/15/24	Mon 7/15/24		
1075	SDG&E - Submit Advice Letter	1 day	Mon 7/22/24	Mon 7/22/24		
1076	SDG&E - Advice Letter Approved	1 day	Tue 9/3/24	Tue 9/3/24		
1077	SDG&E - Implementation Plan	60 days	Wed 9/4/24	Tue 11/26/24		
1078	*SDG&E - Private Institutions and Healthcare Solicitation	398 days	Thu 10/5/23	Mon 4/14/25		
1079	SDG&E - RFA Preparation	33 days	Thu 10/5/23	Mon 11/20/23		
1080	SDG&E - RFA Release	1 day	Mon 11/27/23	Mon 11/27/23		
1081	SDG&E - RFA Abstract Creation Duration	35 days	Mon 11/27/23	Fri 1/12/24		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1082	SDG&E - RFA Evaluation	30 days	Mon 1/15/24	Fri 2/23/24		
1083	SDG&E - RFA Review with EE PRG	5 days	Mon 2/26/24	Fri 3/1/24		
1084	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Mon 3/4/24	Mon 3/4/24		
1085	SDG&E - RFP Preparation	54 days	Mon 11/27/23	Thu 2/8/24		
1086	SDG&E - RFP Release	1 day	Fri 3/8/24	Fri 3/8/24		
1087	SDG&E - RFP Proposal Creation Duration	34 days	Fri 3/8/24	Wed 4/24/24		
1088	SDG&E - RFP Evaluation	42 days	Thu 4/25/24	Fri 6/21/24		
1089	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 7/2/24	Tue 7/2/24		
1090	SDG&E - Selection Review with EE PRG	7 days	Fri 6/21/24	Mon 7/1/24		
1091	SDG&E - Contract Negotiation and Development	62 days	Mon 7/15/24	Tue 10/8/24		
1092	SDG&E - Contract Review with EE PRG	7 days	Mon 10/21/24	Tue 10/29/24		
1093	SDG&E - Final Award and Contract Signed	1 day	Fri 12/6/24	Fri 12/6/24		
1094	SDG&E - Submit Advice Letter	1 day	Fri 12/13/24	Fri 12/13/24		
1095	SDG&E - Advice Letter Approved	1 day	Tue 1/14/25	Tue 1/14/25		
1096	SDG&E - Implementation Plan	46 days	Wed 1/15/25	Wed 3/19/25		
1097	*SDG&E - Lodging: Hotels/Motels Solicitation	398 days	Tue 10/10/23	Thu 4/17/25		
1098	SDG&E - RFA Preparation	33 days	Tue 10/10/23	Thu 11/23/23		
1099	SDG&E - RFA Release	1 day	Fri 12/8/23	Fri 12/8/23		
1100	SDG&E - RFA Abstract Creation Duration	35 days	Fri 12/8/23	Thu 1/25/24		
1101	SDG&E - RFA Evaluation	22 days	Mon 1/22/24	Tue 2/20/24		
1102	SDG&E - RFA Review with EE PRG	7 days	Tue 3/12/24	Wed 3/20/24		
1103	SDG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 3/19/24	Tue 3/19/24		
1104	SDG&E - RFP Preparation	48 days	Tue 1/23/24	Thu 3/28/24		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1105	SDG&E - RFP Release	1 day	Thu 3/21/24	Thu 3/21/24		
1106	SDG&E - RFP Proposal Creation Duration	29 days	Thu 3/21/24	Tue 4/30/24		
1107	SDG&E - RFP Evaluation	23 days	Mon 5/6/24	Wed 6/5/24		
1108	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 6/18/24	Tue 6/18/24		
1109	SDG&E - Selection Review with EE PRG	7 days	Thu 6/20/24	Fri 6/28/24		
1110	SDG&E - Contract Negotiation and Development	60 days	Wed 7/17/24	Tue 10/8/24		
1111	SDG&E - Contract Review with EE PRG	9 days	Thu 10/24/24	Tue 11/5/24		
1112	SDG&E - Final Award and Contract Signed	1 day	Tue 12/10/24	Tue 12/10/24		
1113	SDG&E - Submit Advice Letter	1 day	Tue 12/17/24	Tue 12/17/24		
1114	SDG&E - Advice Letter Approved	1 day	Tue 1/14/25	Tue 1/14/25		
1115	SDG&E - Implementation Plan	46 days	Mon 1/20/25	Mon 3/24/25		
1116	*SDG&E - Market Access Program (MAP)	317 days	Wed 3/13/24	Thu 5/29/25		
1117	SDG&E - RFP Preparation	38 days	Wed 3/13/24	Fri 5/3/24		
1118	SDG&E - RFP Release	1 day	Tue 5/7/24	Tue 5/7/24		
1119	SDG&E - RFP Proposal Creation Duration	31 days	Tue 5/7/24	Tue 6/18/24		
1120	SDG&E - RFP Evaluation	43 days	Wed 6/19/24	Fri 8/16/24		
1121	SDG&E - Selection Review with EE PRG	7 days	Thu 9/5/24	Fri 9/13/24		
1122	SDG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 9/17/24	Tue 9/17/24		
1123	SDG&E - Contract Negotiation and Development	60 days	Fri 9/27/24	Thu 12/19/24		
1124	SDG&E - Contract Review with EE PRG	7 days	Thu 1/9/25	Fri 1/17/25		
1125	SDG&E - Final Award and Contract Signed	1 day	Fri 1/31/25	Fri 1/31/25		
1126	SDG&E - Submit Advice Letter	1 day	Fri 2/14/25	Fri 2/14/25		
1127	SDG&E - Advice Letter Approved	1 day	Mon 3/31/25	Mon 3/31/25		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	2005 H1
1128	SDG&E - Implementation Plan	44 days	Mon 3/31/25	Thu 5/29/25		
1129	Please note the SDG&E Solicitations marked with an * are estimated dates and are subject to change					
1130						
1131	PG&E - Local Government Partnerships (non-resource programs) Solicitation	376 days?	Fri 3/22/19	Fri 8/28/20		
1132	PG&E - RFA Preparation	42 days	Fri 3/22/19	Mon 5/20/19		
1133	PG&E - RFA Release	1 day	Thu 5/23/19	Thu 5/23/19		
1134	PG&E - RFA Abstract Creation Duration	22 days	Thu 5/23/19	Fri 6/21/19		
1135	PG&E - RFA Evaluation	15 days	Mon 6/24/19	Fri 7/12/19		
1136	PG&E - RFA Review with EE PRG	4 days	Tue 7/23/19	Fri 7/26/19		
1137	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/5/19	Fri 8/9/19		
1138	PG&E - RFP Preparation	45 days	Tue 8/27/19	Mon 10/28/19		
1139	PG&E - RFP Release	1 day	Mon 11/4/19	Mon 11/4/19		
1140	PG&E - RFP Proposal Creation Duration	33 days	Mon 11/4/19	Wed 12/18/19		
1141	PG&E - RFP Evaluation	18 days	Mon 1/6/20	Wed 1/29/20		
1142	PG&E - RFP Review with EE PRG	4 days	Tue 2/25/20	Fri 2/28/20		
1143	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 3/2/20	Fri 3/6/20		
1144	PG&E - Contract Negotiation and Development	58 days	Fri 2/28/20	Tue 5/19/20		
1145	PG&E - Contract Review with EE PRG	7 days	Tue 5/26/20	Wed 6/3/20		
1146	PG&E - Final Award and Contract Signed	22 days	Fri 5/29/20	Mon 6/29/20		
1147	PG&E - Submit Advice Letter		N/A	N/A		
1148	PG&E - Advice Letter Approved					
1149	PG&E - Implementation Plan	24 days	Tue 7/28/20	Fri 8/28/20		
1150	PG&E - Statewide Codes & Standards (RFP only) Solicitation	221 days?	Mon 7/8/19	Mon 5/11/20		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	2005 H1
1151	PG&E - RFA Preparation		N/A	N/A		
1152	PG&E - RFA Release		N/A	N/A		
1153	PG&E - RFA Abstract Creation Duration		N/A	N/A		
1154	PG&E - RFA Evaluation		N/A	N/A		
1155	PG&E - RFA Review with EE PRG		N/A	N/A		
1156	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A		
1157	PG&E - RFP Preparation	36 days	Mon 7/8/19	Mon 8/26/19		
1158	PG&E - RFP Release	1 day	Tue 9/10/19	Tue 9/10/19		
1159	PG&E - RFP Proposal Creation Duration	24 days	Tue 9/10/19	Fri 10/11/19		
1160	PG&E - RFP Evaluation	10 days	Mon 10/14/19	Fri 10/25/19		
1161	PG&E - RFP Review with EE PRG	4 days	Thu 11/21/19	Tue 11/26/19		
1162	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 11/27/19	Fri 11/29/19		
1163	PG&E - Contract Negotiation and Development	35 days	Mon 12/2/19	Fri 1/17/20		
1164	PG&E - Contract Review with EE PRG	4 days	Tue 1/21/20	Fri 1/24/20		
1165	PG&E - Final Award and Contract Signed	32 days	Wed 1/29/20	Thu 3/12/20		
1166	PG&E - Submit Advice Letter		N/A	N/A		
1167	PG&E - Advice Letter Approved					
1168	PG&E - Implementation Plan	32 days	Fri 3/27/20	Mon 5/11/20		
1169	PG&E - Local Multi-Sector (40% outsource) Solicitation	251 days?	Tue 4/28/20	Tue 4/13/21		
1170	PG&E - RFA Preparation		N/A	N/A		
1171	PG&E - RFA Release		N/A	N/A		
1172	PG&E - RFA Abstract Creation Duration		N/A	N/A		
1173	PG&E - RFA Evaluation		N/A	N/A		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1174	PG&E - RFA Review with EE PRG		N/A	N/A		
1175	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder		N/A	N/A		
1176	PG&E - RFP Preparation		N/A	N/A		
1177	PG&E - RFP Release		N/A	N/A		
1178	PG&E - RFP Proposal Creation Duration		N/A	N/A		
1179	PG&E - RFP Evaluation		N/A	N/A		
1180	PG&E - RFP Review with EE PRG	4 days	Tue 4/28/20	Fri 5/1/20		
1181	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder					
1182	PG&E - Contract Negotiation and Development	81 days	Thu 7/2/20	Thu 10/22/20		
1183	PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20		
1184	PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20		
1185	PG&E - Submit Advice Letter	1 day	Wed 1/13/21	Wed 1/13/21		
1186	PG&E - Advice Letter Approved	1 day?	Fri 2/12/21	Fri 2/12/21		
1187	PG&E - Implementation Plan	43 days	Sat 2/13/21	Tue 4/13/21		
1188	PG&E - Statewide New Constructions (Non-Residential) Solicitation	591 days	Mon 3/25/19	Sun 6/27/21		
1189	PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19		
1190	PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19		
1191	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19		
1192	PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19		
1193	PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19		
1194	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19		
1195	PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20		
1196	PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1197	PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20		
1198	PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20		
1199	PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20		
1200	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20		
1201	PG&E - Contract Negotiation and Development	49 days	Mon 8/17/20	Thu 10/22/20		
1202	PG&E - Contract Review with EE PRG	24 days	Thu 10/22/20	Tue 11/24/20		
1203	PG&E - Final Award and Contract Signed	23 days	Mon 11/30/20	Wed 12/30/20		
1204	PG&E - Submit Advice Letter	1 day	Fri 2/19/21	Fri 2/19/21		
1205	PG&E - Advice Letter Approved	1 day	Wed 4/28/21	Wed 4/28/21		
1206	PG&E - Implementation Plan	43 days	Thu 4/29/21	Sun 6/27/21		
1207	PG&E - Statewide New Construction (Residential) Solicitation	640 days?	Mon 3/25/19	Fri 9/3/21		
1208	PG&E - RFA Preparation	45 days	Mon 3/25/19	Fri 5/24/19		
1209	PG&E - RFA Release	1 day	Tue 5/28/19	Tue 5/28/19		
1210	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/28/19	Fri 6/28/19		
1211	PG&E - RFA Evaluation	19 days	Tue 7/2/19	Fri 7/26/19		
1212	PG&E - RFA Review with EE PRG	4 days	Tue 8/20/19	Fri 8/23/19		
1213	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Tue 8/27/19	Fri 8/30/19		
1214	PG&E - RFP Preparation	45 days	Fri 12/27/19	Thu 2/27/20		
1215	PG&E - RFP Release	1 day	Mon 3/16/20	Mon 3/16/20		
1216	PG&E - RFP Proposal Creation Duration	40 days	Tue 3/17/20	Mon 5/11/20		
1217	PG&E - RFP Evaluation	52 days	Tue 5/12/20	Wed 7/22/20		
1218	PG&E - RFP Review with EE PRG	8 days	Fri 7/24/20	Tue 8/4/20		
1219	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	6 days	Wed 8/5/20	Wed 8/12/20		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1220	PG&E - Contract Negotiation and Development	177 days	Mon 8/17/20	Tue 4/20/21		
1221	PG&E - Contract Review with EE PRG	16 days	Thu 4/22/21	Thu 5/13/21		
1222	PG&E - Final Award and Contract Signed	32 days	Sat 5/15/21	Mon 6/28/21		
1223	PG&E - Submit Advice Letter	1 day	Mon 7/12/21	Mon 7/12/21		
1224	PG&E - Advice Letter Approved (all electric)	1 day	Wed 8/11/21	Wed 8/11/21		
1225	PG&E - Advice Letter Approved (mixed fuel)	1 day	Wed 9/15/21	Wed 9/15/21		
1226	PG&E - Implementation Plan (all electric)	43 days	Thu 8/12/21	Mon 10/11/21		
1227	PG&E - Implementation Plan (mixed fuel)	43 days	Thu 9/16/21	Sun 11/14/21		
1228	PG&E - Statewide WE&T Career Connections Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21		
1229	PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20		
1230	PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20		
1231	PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20		
1232	PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20		
1233	PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20		
1234	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20		
1235	PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20		
1236	PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20		
1237	PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20		
1238	PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20		
1239	PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20		
1240	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20		
1241	PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21		
1242	PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1243	PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21		
1244	PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21		
1245	PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21		
1246	PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21		
1247	PG&E - Statewide WE&T Career and Workforce Readiness Solicitation	410 days?	Tue 1/7/20	Mon 8/2/21		
1248	PG&E - RFA Preparation	54 days	Tue 1/7/20	Fri 3/20/20		
1249	PG&E - RFA Release	1 day	Mon 4/6/20	Mon 4/6/20		
1250	PG&E - RFA Abstract Creation Duration	29 days	Tue 4/7/20	Fri 5/15/20		
1251	PG&E - RFA Evaluation	20 days	Mon 5/18/20	Fri 6/12/20		
1252	PG&E - RFA Review with EE PRG	8 days	Fri 6/19/20	Tue 6/30/20		
1253	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	4 days	Fri 7/3/20	Wed 7/8/20		
1254	PG&E - RFP Preparation	45 days	Mon 6/15/20	Fri 8/14/20		
1255	PG&E - RFP Release	1 day	Fri 9/4/20	Fri 9/4/20		
1256	PG&E - RFP Proposal Creation Duration	20 days	Mon 9/7/20	Fri 10/2/20		
1257	PG&E - RFP Evaluation	14 days	Tue 10/6/20	Fri 10/23/20		
1258	PG&E - RFP Review with EE PRG	8 days	Fri 10/23/20	Tue 11/3/20		
1259	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	1 day	Tue 11/10/20	Tue 11/10/20		
1260	PG&E - Contract Negotiation and Development	71 days	Mon 12/7/20	Mon 3/15/21		
1261	PG&E - Contract Review with EE PRG	6 days	Tue 3/23/21	Tue 3/30/21		
1262	PG&E - Final Award and Contract Signed	22 days	Thu 4/1/21	Fri 4/30/21		
1263	PG&E - Submit Advice Letter	1 day	Fri 5/28/21	Fri 5/28/21		
1264	PG&E - Advice Letter Approved	1 day	Fri 6/25/21	Fri 6/25/21		
1265	PG&E - Implementation Plan	43 days	Sat 6/26/21	Tue 8/24/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1266	PG&E - Statewide State of CA (Dept. of Corrections) Solicitation	348 days?	Sun 3/1/20	Tue 6/29/21		
1267	PG&E - RFA Preparation	46 days	Sun 3/1/20	Fri 5/1/20		
1268	PG&E - RFA Release	1 day	Wed 5/13/20	Wed 5/13/20		
1269	PG&E - RFA Abstract Creation Duration	31 days	Wed 5/13/20	Wed 6/24/20		
1270	PG&E - RFA Evaluation	15 days	Mon 6/29/20	Fri 7/17/20		
1271	PG&E - RFA Review with EE PRG	5 days	Tue 7/28/20	Mon 8/3/20		
1272	PG&E - RFA Estimated Notification of Successful and Unsuccessful Bidder	5 days	Mon 8/3/20	Fri 8/7/20		
1273	PG&E - RFP Preparation	20 days	Mon 8/3/20	Fri 8/28/20		
1274	PG&E - RFP Release	1 day	Wed 9/9/20	Wed 9/9/20		
1275	PG&E - RFP Proposal Creation Duration	31 days	Wed 9/9/20	Wed 10/21/20		
1276	PG&E - RFP Evaluation	31 days	Fri 10/23/20	Fri 12/4/20		
1277	PG&E - RFP Review with EE PRG	6 days	Tue 12/22/20	Tue 12/29/20		
1278	PG&E - RFP Estimated Notification of Successful and Unsuccessful Bidder	3 days	Wed 1/6/21	Fri 1/8/21		
1279	PG&E - Contract Negotiation and Development	65 days	Wed 1/20/21	Tue 4/20/21		
1280	PG&E - Contract Review with EE PRG	7 days	Thu 4/22/21	Fri 4/30/21		
1281	PG&E - Final Award and Contract Signed	22 days	Sat 5/1/21	Mon 5/31/21		
1282	PG&E - Submit Advice Letter	1 day	Thu 6/24/21	Thu 6/24/21		
1283	PG&E - Advice Letter Approved	1 day	Wed 7/28/21	Wed 7/28/21		
1284	PG&E - Implementation Plan	43 days	Thu 7/29/21	Sun 9/26/21		
1285	PG&E - Local (Micro and Small Business Equity Program) Solicitation	403 days?	Tue 6/1/21	Thu 12/15/22		
1286	PG&E - RFA Preparation	38 days	Tue 6/1/21	Thu 7/22/21		
1287	PG&E - RFA Release	1 day	Tue 9/7/21	Tue 9/7/21		
1288	PG&E - RFA Abstract Creation Duration	34 days	Wed 9/8/21	Mon 10/25/21		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	H2	H1
1289	PG&E - RFA Evaluation	18 days	Tue 10/26/21	Thu 11/18/21		
1290	PG&E - RFP Release	1 day	Wed 12/8/21	Wed 12/8/21		
1291	PG&E - RFP Proposal Creation Duration	46 days	Wed 12/8/21	Wed 2/9/22		
1292	PG&E - RFP Evaluation	21 days	Thu 2/10/22	Thu 3/10/22		
1293	PG&E - RFP Review with EE PRG	6 days	Thu 3/17/22	Thu 3/24/22		
1294	PG&E - RFP Estimated Bidder Notification	1 day	Wed 3/30/22	Wed 3/30/22		
1295	PG&E - Contract Negotiation and Development	71 days	Thu 4/7/22	Thu 7/14/22		
1296	PG&E - Contract Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22		
1297	PG&E - Final Award and Contract Signed	45 days	Mon 8/8/22	Fri 10/7/22		
1298	PG&E - Submit Advice Letter	1 day	Wed 10/12/22	Wed 10/12/22		
1299	PG&E - Advice Letter Approved	1 day	Fri 11/11/22	Fri 11/11/22		
1300	PG&E - Implementation Plan	31 days	Fri 11/11/22	Fri 12/23/22		
1301	PG&E - Local (C&S Compliance Improvement) Solicitation	436 days	Tue 3/1/22	Tue 10/31/23		
1302	PG&E - RFA Preparation	34 days	Tue 3/1/22	Fri 4/15/22		
1303	PG&E - RFA Release	1 day	Mon 5/16/22	Mon 5/16/22		
1304	PG&E - RFA Abstract Creation Duration	25 days	Tue 5/17/22	Mon 6/20/22		
1305	PG&E - RFA Evaluation	28 days	Tue 6/21/22	Thu 7/28/22		
1306	PG&E - RFA Review with EE PRG	1 day	Tue 8/9/22	Tue 8/9/22		
1307	PG&E - RFA Estimated Bidder Notification	1 day	Wed 8/31/22	Wed 8/31/22		
1308	PG&E - RFP Preparation	24 days	Mon 8/1/22	Thu 9/1/22		
1309	PG&E - RFP Release	1 day	Tue 9/13/22	Tue 9/13/22		
1310	PG&E - RFP Proposal Creation Duration	26 days	Tue 9/13/22	Tue 10/18/22		
1311	PG&E - RFP Evaluation	45 days	Wed 10/19/22	Tue 12/20/22		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	H2	H1
1312	PG&E - RFP Review with EE PRG	1 day	Tue 1/24/23	Tue 1/24/23		
1313	PG&E - RFP Estimated Bidder Notification	1 day	Fri 2/10/23	Fri 2/10/23		
1314	PG&E - Contract Negotiation and Development	47 days	Mon 2/13/23	Tue 4/18/23		
1315	PG&E - Contract Review with EE PRG	26 days	Tue 5/23/23	Tue 6/27/23		
1316	PG&E - Final Award and Contract Signed	48 days	Wed 6/28/23	Fri 9/1/23		
1317	PG&E - Submit Advice Letter		N/A			
1318	PG&E - Advice Letter Approved		N/A			
1319	PG&E - Implementation Plan	1 day	Tue 10/31/23	Tue 10/31/23		
1320	PG&E - Residential Electrification Equity Program Solicitation	595 days	Mon 8/1/22	Fri 11/8/24		
1321	PG&E - RFA Preparation	59 days	Mon 8/1/22	Thu 10/20/22		
1322	PG&E - RFA Release	1 day	Tue 11/29/22	Tue 11/29/22		
1323	PG&E - RFA Abstract Creation Duration	46 days	Tue 11/29/22	Tue 1/31/23		
1324	PG&E - RFA Evaluation	17 days	Sun 2/5/23	Sun 2/26/23		
1325	PG&E - RFA Review with EE PRG	6 days	Mon 2/27/23	Mon 3/6/23		
1326	PG&E - RFA Estimated Bidder Notification	3 days	Mon 3/6/23	Wed 3/8/23		
1327	PG&E - RFP Preparation	46 days	Mon 1/9/23	Mon 3/13/23		
1328	PG&E - RFP Release	1 day	Tue 4/11/23	Tue 4/11/23		
1329	PG&E - RFP Proposal Creation Duration	26 days	Tue 4/11/23	Tue 5/16/23		
1330	PG&E - RFP Evaluation	18 days	Fri 5/19/23	Tue 6/13/23		
1331	PG&E - RFP Review with EE PRG	1 day	Tue 6/27/23	Tue 6/27/23		
1332	PG&E - RFP Estimated Bidder Notification	1 day	Tue 7/11/23	Tue 7/11/23		
1333	PG&E - Contract Negotiation and Development	233 days	Tue 8/1/23	Thu 6/20/24		
1334	PG&E - Contract Review with EE PRG	8 days	Fri 6/21/24	Tue 7/2/24		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1335	PG&E - Final Award and Contract Signed	21 days	Fri 7/5/24	Fri 8/2/24		
1336	PG&E - Submit Advice Letter	1 day	Fri 8/9/24	Fri 8/9/24		
1337	PG&E - Advice Letter Approved	1 day	Mon 9/9/24	Mon 9/9/24		
1338	PG&E - Implementation Plan	1 day	Fri 11/8/24	Fri 11/8/24		
1339	PG&E - Statewide C&S Advocacy Solicitation	641 days	Tue 2/1/22	Tue 7/16/24		
1340	PG&E - RFA Preparation	54 days	Tue 2/1/22	Fri 4/15/22		
1341	PG&E - RFA Release	1 day	Mon 5/30/22	Mon 5/30/22		
1342	PG&E - RFA Abstract Creation Duration	24 days	Tue 5/31/22	Fri 7/1/22		
1343	PG&E - RFA Evaluation	14 days	Fri 7/1/22	Wed 7/20/22		
1344	PG&E - RFA Review with EE PRG	6 days	Fri 7/22/22	Fri 7/29/22		
1345	PG&E - RFA Estimated Bidder Notification	1 day	Mon 8/1/22	Mon 8/1/22		
1346	PG&E - RFP Preparation	36 days	Fri 4/1/22	Fri 5/20/22		
1347	PG&E - RFP Release	1 day	Tue 6/7/22	Tue 6/7/22		
1348	PG&E - RFP Proposal Creation Duration	31 days	Tue 6/7/22	Tue 7/19/22		
1349	PG&E - RFP Evaluation	50 days	Wed 7/20/22	Tue 9/27/22		
1350	PG&E - RFP Review with EE PRG	1 day	Wed 10/5/22	Wed 10/5/22		
1351	PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/24/22	Mon 10/24/22		
1352	PG&E - Contract Negotiation and Development	73 days	Mon 11/14/22	Wed 2/22/23		
1353	PG&E - Contract Review with EE PRG - Wave 1	1 day	Tue 4/25/23	Tue 4/25/23		
1354	PG&E - Final Award and Contract Signed	18 days	Mon 7/17/23	Wed 8/9/23		
1355	PG&E - Submit Advice Letter (wave 1)	1 day	Thu 9/21/23	Thu 9/21/23		
1356	PG&E - Advice Letter Approved	1 day	Wed 10/25/23	Wed 10/25/23		
1357	PG&E - Implementation Plan	1 day	Thu 12/7/23	Thu 12/7/23		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	H2	H1
1358	PG&E - Contract Review with EE PRG - Wave 2	1 day	Wed 12/20/23	Wed 12/20/23		
1359	PG&E - Final Award and Contract Signed	1 day	Fri 3/29/24	Fri 3/29/24		
1360	PG&E - Submit Advice Letter	1 day	Wed 4/17/24	Wed 4/17/24		
1361	PG&E - Advice Letter Approved	1 day	Fri 5/17/24	Fri 5/17/24		
1362	PG&E - Implementation Plan	1 day	Tue 7/16/24	Tue 7/16/24		
1363	PG&E - Zonal Electrification Solicitation	495 days	Thu 12/1/22	Wed 10/23/24		
1364	PG&E - RFP Preparation	88 days	Thu 12/1/22	Mon 4/3/23		
1365	PG&E - RFP Release	1 day	Tue 4/18/23	Tue 4/18/23		
1366	PG&E - RFP Proposal Creation Duration	53 days	Tue 4/18/23	Thu 6/29/23		
1367	PG&E - RFP Evaluation (including interviews)	40 days	Mon 7/10/23	Fri 9/1/23		
1368	PG&E - RFP Review with EE PRG	1 day	Tue 9/26/23	Tue 9/26/23		
1369	PG&E - RFP Estimated Bidder Notification	1 day	Mon 10/2/23	Mon 10/2/23		
1370	PG&E - Contract Negotiation and Development	135 days	Mon 10/9/23	Fri 4/12/24		
1371	PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24		
1372	PG&E - Final Award and Contract Signed	43 days	Wed 5/1/24	Fri 6/28/24		
1373	PG&E - Submit Advice Letter	1 day	Wed 7/3/24	Wed 7/3/24		
1374	PG&E - Advice Letter Approved	1 day	Wed 8/28/24	Wed 8/28/24		
1375	PG&E - Implementation Plan	1 day	Wed 10/23/24	Wed 10/23/24		
1376	PG&E - Residential Whole Home Load Management RFP	453 days	Tue 8/15/23	Thu 5/8/25		
1377	PG&E - RFP Preparation	1 day	Tue 8/15/23	Tue 8/15/23		
1378	PG&E - RFP Release	1 day	Tue 8/15/23	Tue 8/15/23		
1379	PG&E - RFP Proposal Creation Duration	51 days	Tue 8/15/23	Tue 10/24/23		
1380	PG&E - RFP Evaluation	36 days	Thu 10/26/23	Thu 12/14/23		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1381	PG&E - RFP Review with EE PRG	1 day	Fri 2/16/24	Fri 2/16/24		
1382	PG&E - RFP Estimated Bidder Notification	1 day	Tue 2/27/24	Tue 2/27/24		
1383	PG&E - Contract Negotiation and Development	155 days	Wed 3/13/24	Tue 10/15/24		
1384	PG&E - Contract Review with EE PRG	8 days	Tue 11/5/24	Thu 11/14/24		
1385	PG&E - Final Award and Contract Signed	53 days	Thu 11/14/24	Mon 1/27/25		
1386	PG&E - Submit Advice Letter	1 day	Fri 2/7/25	Fri 2/7/25		
1387	PG&E - Advice Letter Approved	1 day	Sat 3/9/24	Sat 3/9/24		
1388	PG&E - Implementation Plan	1 day	Wed 5/8/24	Wed 5/8/24		
1389	PG&E - 2024 Summer Reliability Platform Administrator RFP	337 days?	Tue 4/18/23	Wed 7/31/24		
1390	PG&E - RFP Preparation	30 days	Mon 5/1/23	Fri 6/9/23		
1391	PG&E - RFP Release	1 day	Fri 9/1/23	Fri 9/1/23		
1392	PG&E - RFP Proposal Creation Duration	31 days	Fri 9/1/23	Fri 10/13/23		
1393	PG&E - RFP Evaluation	22 days	Tue 10/17/23	Wed 11/15/23		
1394	PG&E - RFP Review with EE PRG	1 day	Tue 11/28/23	Tue 11/28/23		
1395	PG&E - RFP Estimated Bidder Notification	1 day	Tue 12/5/23	Tue 12/5/23		
1396	PG&E - Contract Negotiation and Development	68 days	Mon 1/8/24	Wed 4/10/24		
1397	PG&E - Contract Review with EE PRG	1 day	Tue 4/23/24	Tue 4/23/24		
1398	PG&E - Final Award and Contract Signed	22 days	Wed 5/1/24	Thu 5/30/24		
1399	PG&E - Submit Advice Letter	1 day	Fri 5/31/24	Fri 5/31/24		
1400	PG&E - Advice Letter Approved	1 day	Mon 7/1/24	Mon 7/1/24		
1401	PG&E - Implementation Plan	1 day	Wed 7/31/24	Wed 7/31/24		
1402	PG&E - C&S Code Readiness RFP	393 days?	Wed 2/1/23	Fri 8/2/24		
1403	PG&E - RFP Preparation	113 days	Wed 2/1/23	Fri 7/7/23		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	2005 H1
1404	PG&E - RFP Release	1 day	Wed 7/12/23	Wed 7/12/23		
1405	PG&E - RFP Proposal Creation Duration	30 days	Thu 7/13/23	Wed 8/23/23		
1406	PG&E - RFP Evaluation	36 days	Mon 8/28/23	Mon 10/16/23		
1407	PG&E - RFP Review with EE PRG	1 day	Tue 10/24/23	Tue 10/24/23		
1408	PG&E - RFP Estimated Bidder Notification	1 day	Mon 11/6/23	Mon 11/6/23		
1409	PG&E - Contract Negotiation and Development	65 days	Wed 11/15/23	Tue 2/13/24		
1410	PG&E - Contract Review with EE PRG	1 day	Tue 2/27/24	Tue 2/27/24		
1411	PG&E - Final Award and Contract Signed	1 day	Fri 4/12/24	Fri 4/12/24		
1412	PG&E - Submit Advice Letter	1 day	Tue 5/7/24	Tue 5/7/24		
1413	PG&E - Advice Letter Approved	1 day	Thu 6/6/24	Thu 6/6/24		
1414	PG&E - Implementation Plan	1 day	Fri 8/2/24	Fri 8/2/24		
1415	PG&E - Residential Electrification - Single Point of Contact	414 days	Tue 8/1/23	Fri 2/28/25		
1416	PG&E - RFP Preparation	133 days	Tue 8/1/23	Thu 2/1/24		
1417	PG&E - RFP Release	1 day	Wed 2/28/24	Wed 2/28/24		
1418	PG&E - RFP Proposal Creation Duration	33 days	Wed 2/28/24	Fri 4/12/24		
1419	PG&E - RFP Evaluation	66 days	Mon 4/15/24	Mon 7/15/24		
1420	PG&E - RFP Review with EE PRG	6 days	Fri 7/19/24	Fri 7/26/24		
1421	PG&E - RFP Estimated Bidder Notification	1 day	Wed 8/7/24	Wed 8/7/24		
1422	PG&E - Contract Negotiation and Development	62 days				
1423	PG&E - Contract Review with EE PRG	6 days				
1424	PG&E - Final Award and Contract Signed	25 days				
1425	PG&E - Submit Advice Letter	1 day				
1426	PG&E - Advice Letter Approved	1 day				

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	H1
1427	PG&E - Implementation Plan	1 day				
1428	PG&E - Commercial SEM FP	433 days	Thu 8/3/23	Mon 3/31/25		
1429	PG&E - RFP Preparation	16 days	Thu 8/3/23	Thu 8/24/23		
1430	PG&E - RFP Release	1 day	Fri 11/3/23	Fri 11/3/23		
1431	PG&E - RFP Proposal Creation Duration	55 days	Fri 11/3/23	Thu 1/18/24		
1432	PG&E - RFP Evaluation	58 days	Tue 1/23/24	Thu 4/11/24		
1433	PG&E - RFP Review with EE PRG	1 day	Wed 4/17/24	Wed 4/17/24		
1434	PG&E - RFP Estimated Bidder Notification	4 days	Tue 4/23/24	Fri 4/26/24		
1435	PG&E - Contract Negotiation and Development	90 days	Thu 5/2/24	Wed 9/4/24		
1436	PG&E - Contract Review with EE PRG	8 days	Mon 9/16/24	Wed 9/25/24		
1437	PG&E - Final Award and Contract Signed	58 days	Thu 9/26/24	Mon 12/16/24		
1438	PG&E - Submit Advice Letter	1 day	Thu 12/19/24	Thu 12/19/24		
1439	PG&E - Advice Letter Approved	1 day	Mon 3/31/25	Mon 3/31/25		
1440	PG&E - Implementation Plan	1 day	Mon 3/31/25	Mon 3/31/25		
1441	PG&E - SW WE&T Career & Workforce Readiness	370 days	Tue 10/8/24	Sun 3/8/26		
1442	PG&E - RFP Preparation	118 days	Tue 10/8/24	Thu 3/20/25		
1443	PG&E - RFP Release	1 day	Tue 4/8/25	Tue 4/8/25		
1444	PG&E - RFP Proposal Creation Duration	31 days	Tue 4/8/25	Tue 5/20/25		
1445	PG&E - RFP Evaluation	19 days	Thu 5/22/25	Tue 6/17/25		
1446	PG&E - RFP Review with EE PRG	6 days	Tue 7/1/25	Tue 7/8/25		
1447	PG&E - RFP Estimated Bidder Notification	1 day	Wed 7/9/25	Wed 7/9/25		
1448	PG&E - Contract Negotiation and Development	42 days	Tue 7/22/25	Wed 9/17/25		
1449	PG&E - Contract Review with EE PRG	5 days	Thu 9/26/24	Wed 10/2/24		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Name	Duration	Start	Finish	H2	2005 H1
1450	PG&E - Final Award and Contract Signed	298 days	Thu 10/10/24	Mon 12/1/25		
1451	PG&E - Submit Advice Letter	1 day	Mon 12/8/25	Mon 12/8/25		
1452	PG&E - Advice Letter Approved	1 day	Wed 1/7/26	Wed 1/7/26		
1453	PG&E - Implementation Plan	1 day	Sun 3/8/26	Sun 3/8/26		

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

2005	H1	H2	2006	H1	H2	2007	H1	H2	2008	H1	H2	2009	H1	H2	2010	H1	H2	2011	H1	H2	2012	H1	H2	2013	H1	H2	2014	H1	H2	2015	H1	H2

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

2005	H1	H2	2006	H1	H2	2007	H1	H2	2008	H1	H2	2009	H1	H2	2010	H1	H2	2011	H1	H2	2012	H1	H2	2013	H1	H2	2014	H1	H2	2015	H1	H2

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

2005	H1	H2	2006	H1	H2	2007	H1	H2	2008	H1	H2	2009	H1	H2	2010	H1	H2	2011	H1	H2	2012	H1	H2	2013	H1	H2	2014	H1	H2	2015	H1	H2

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

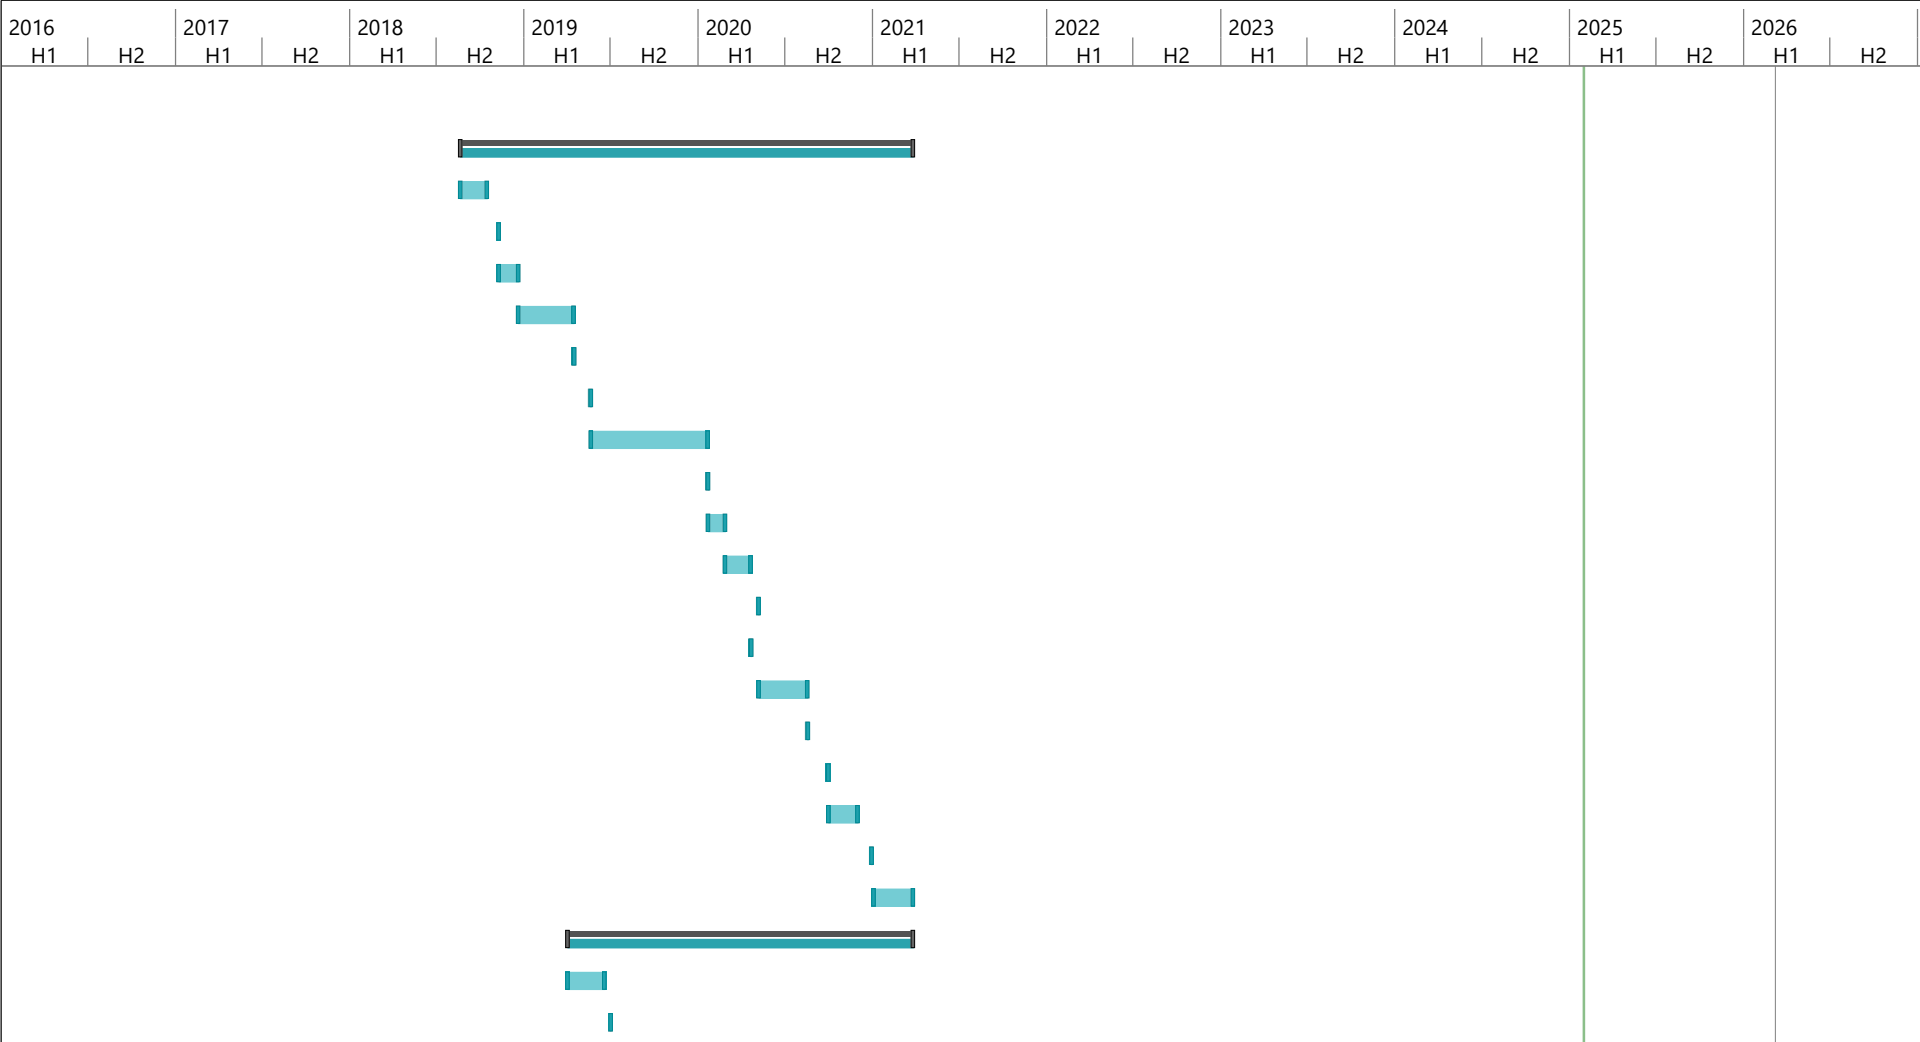


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

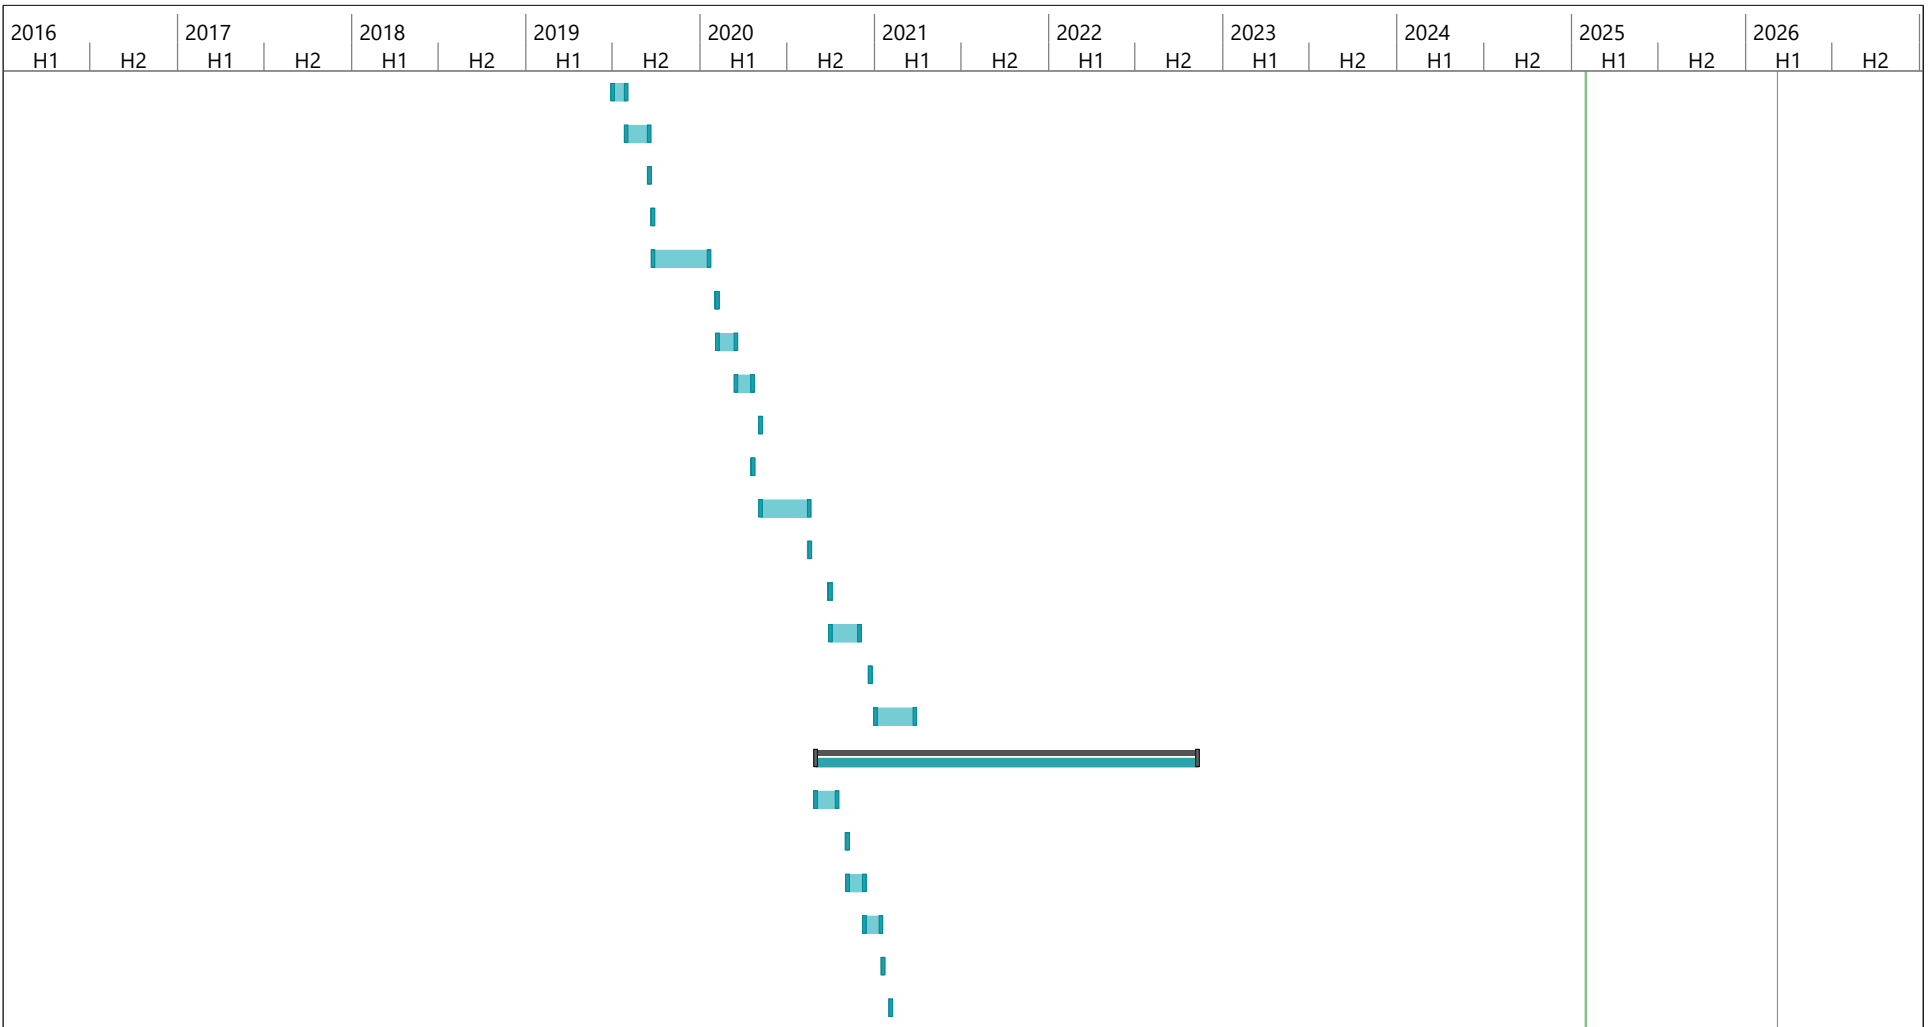


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

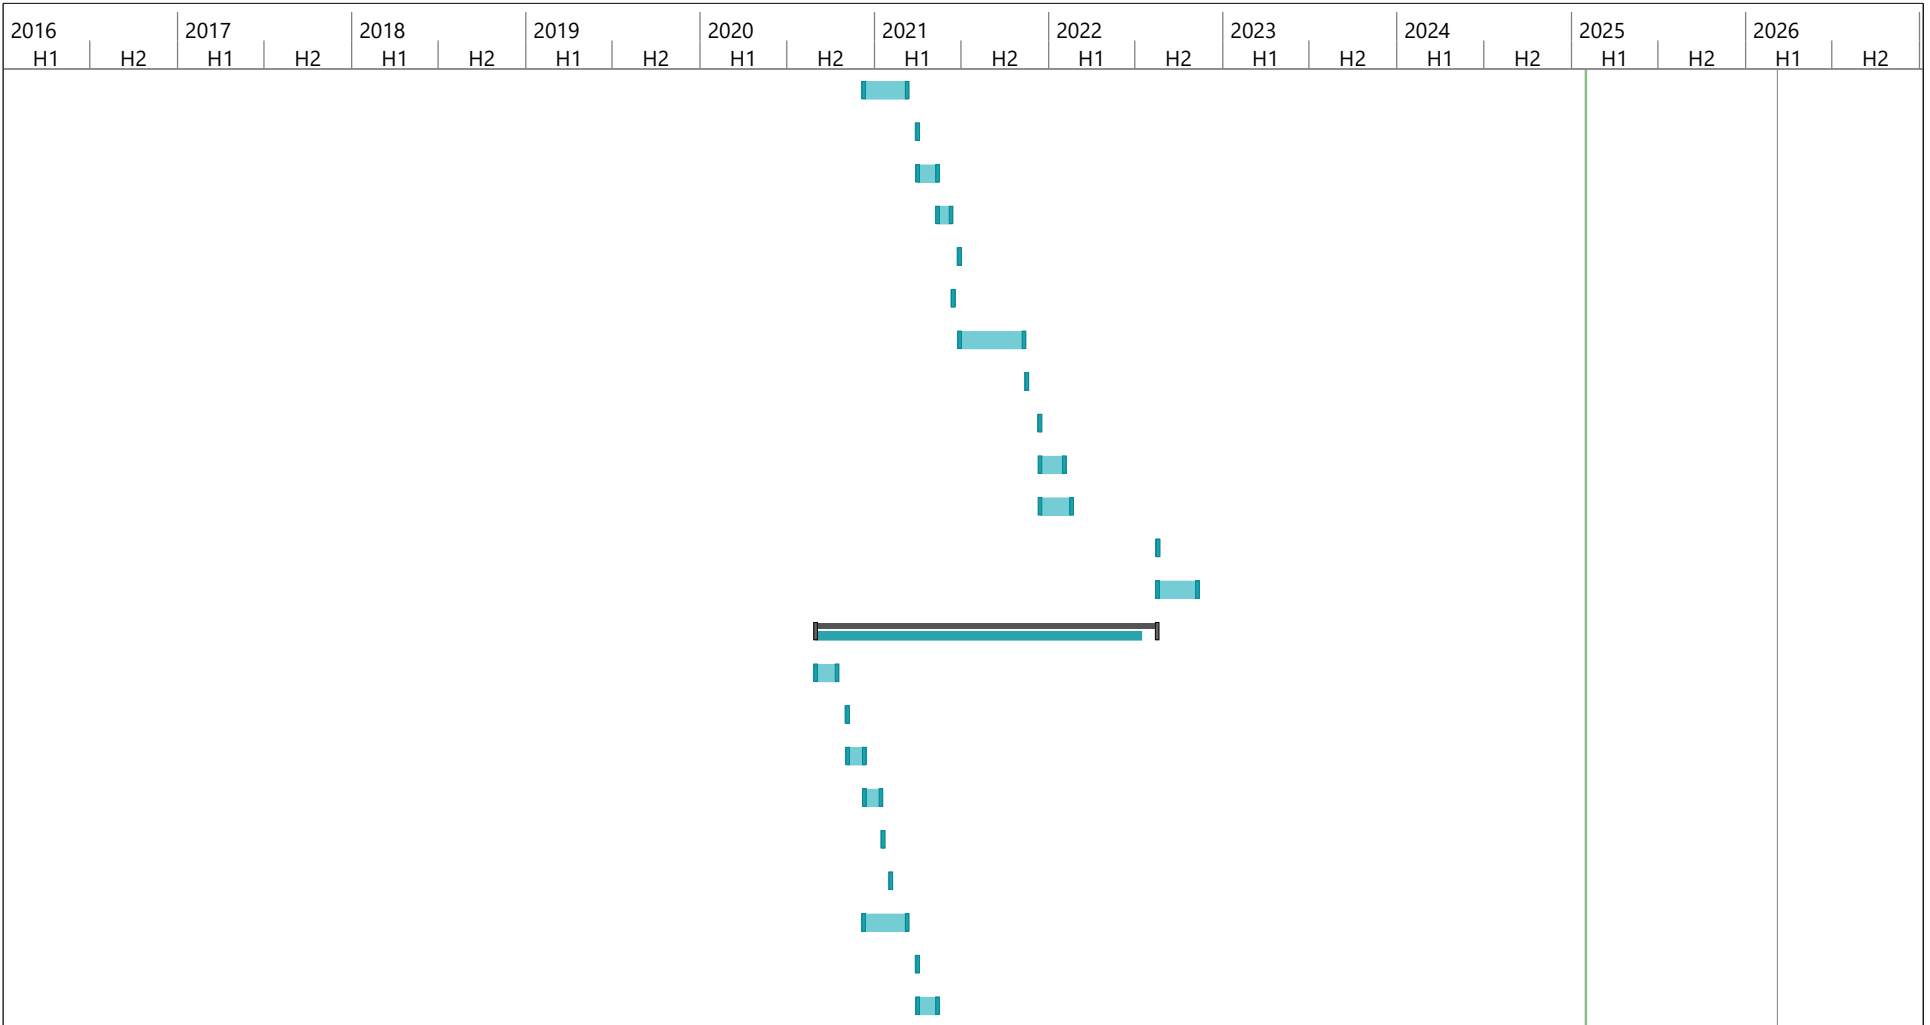


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

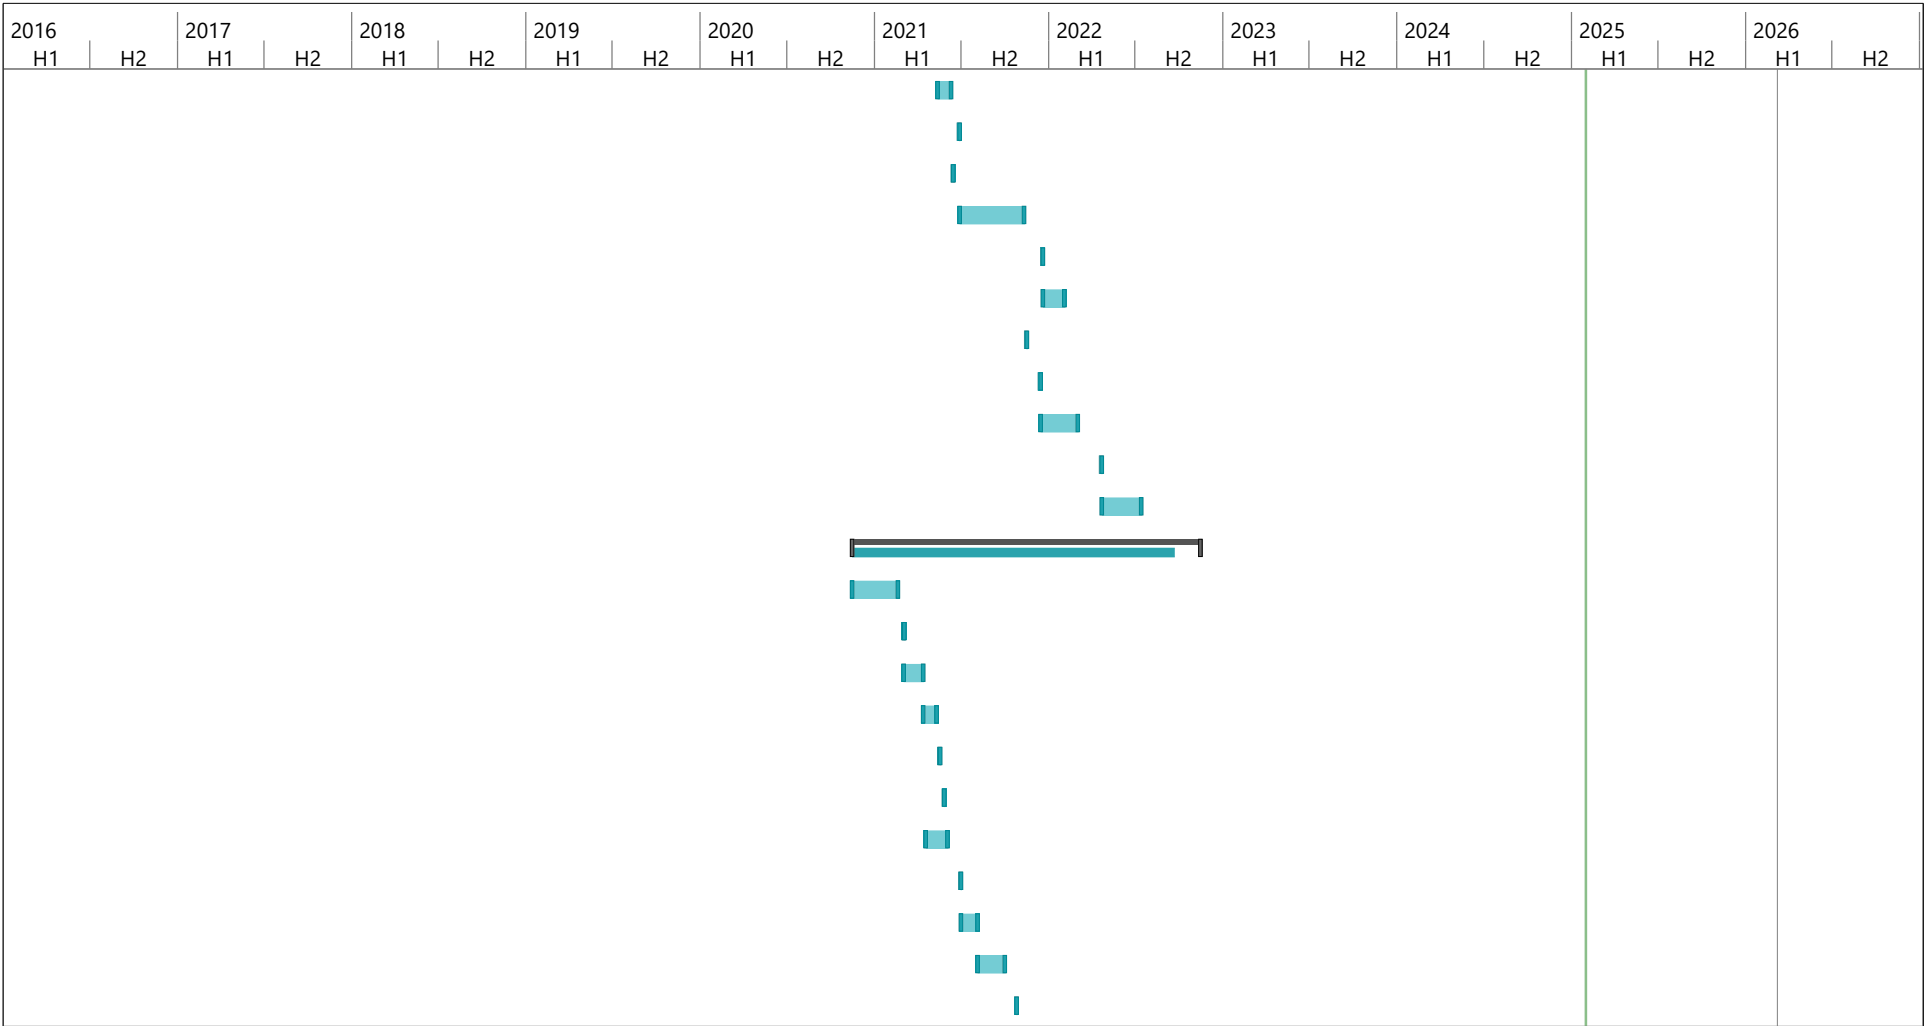


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

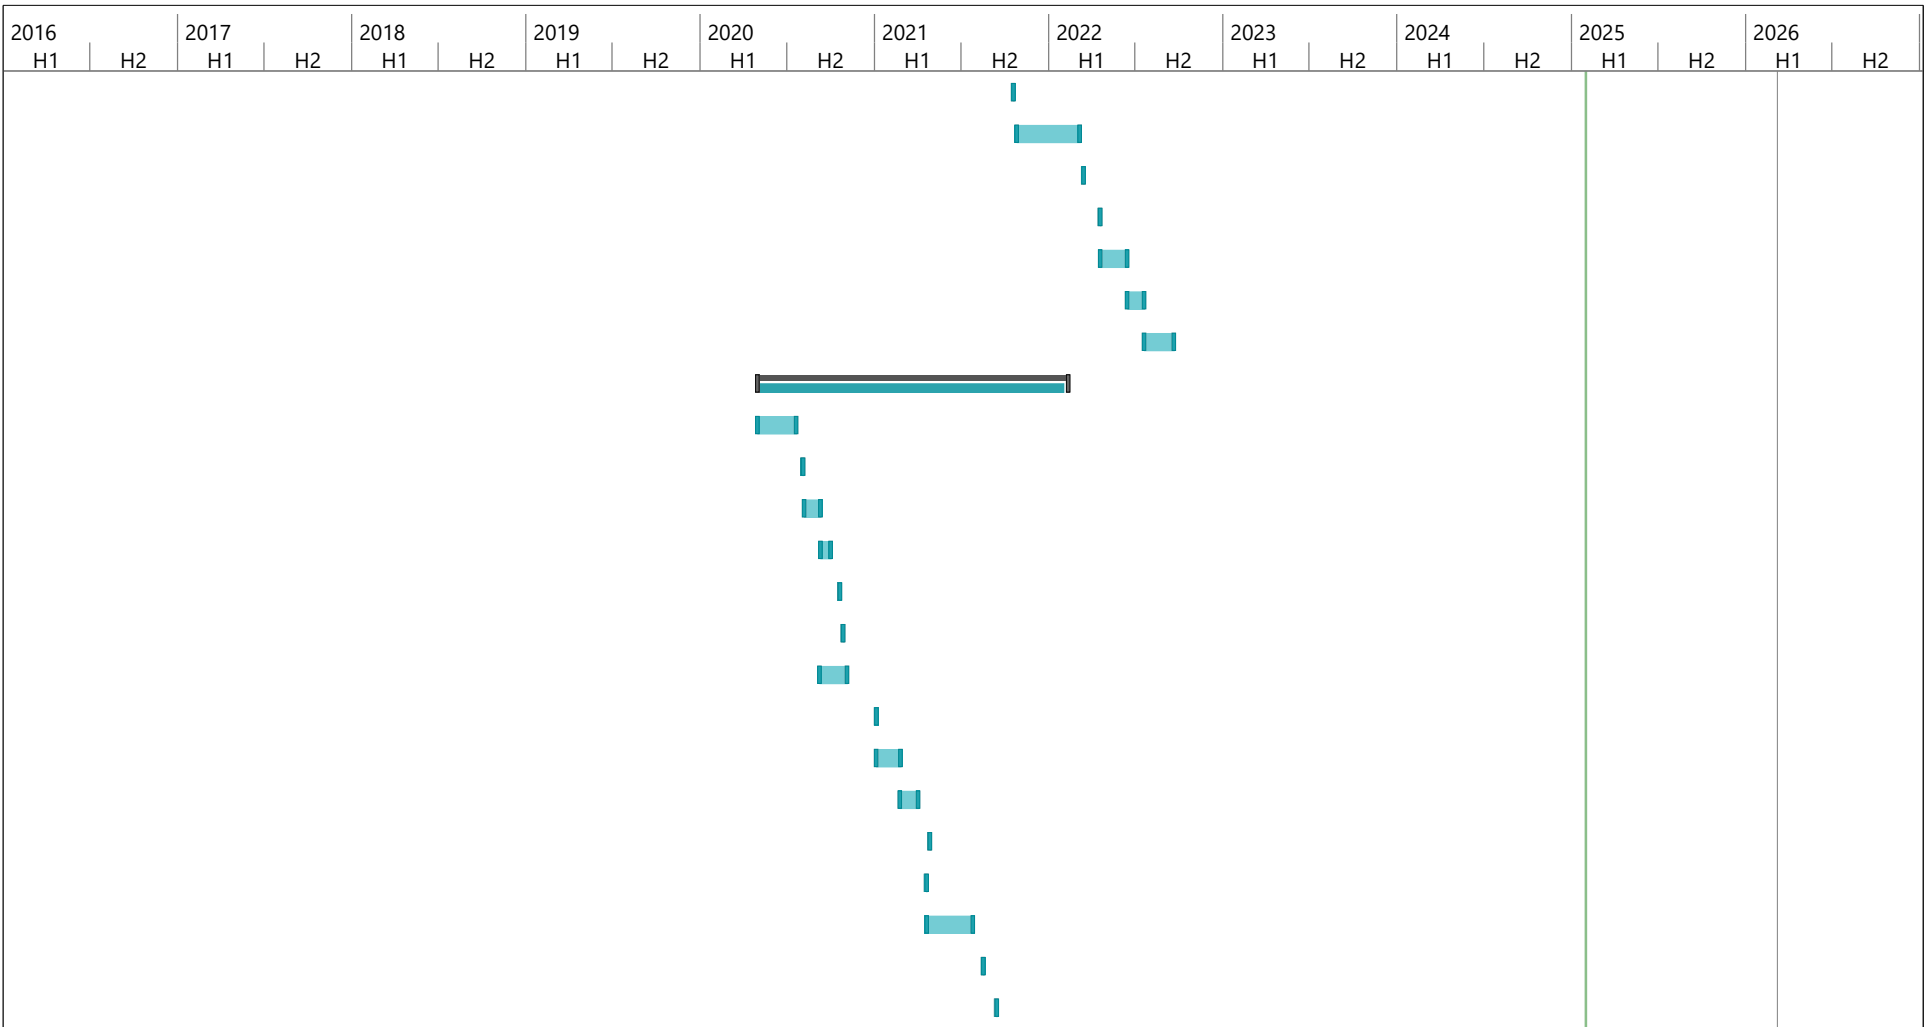


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

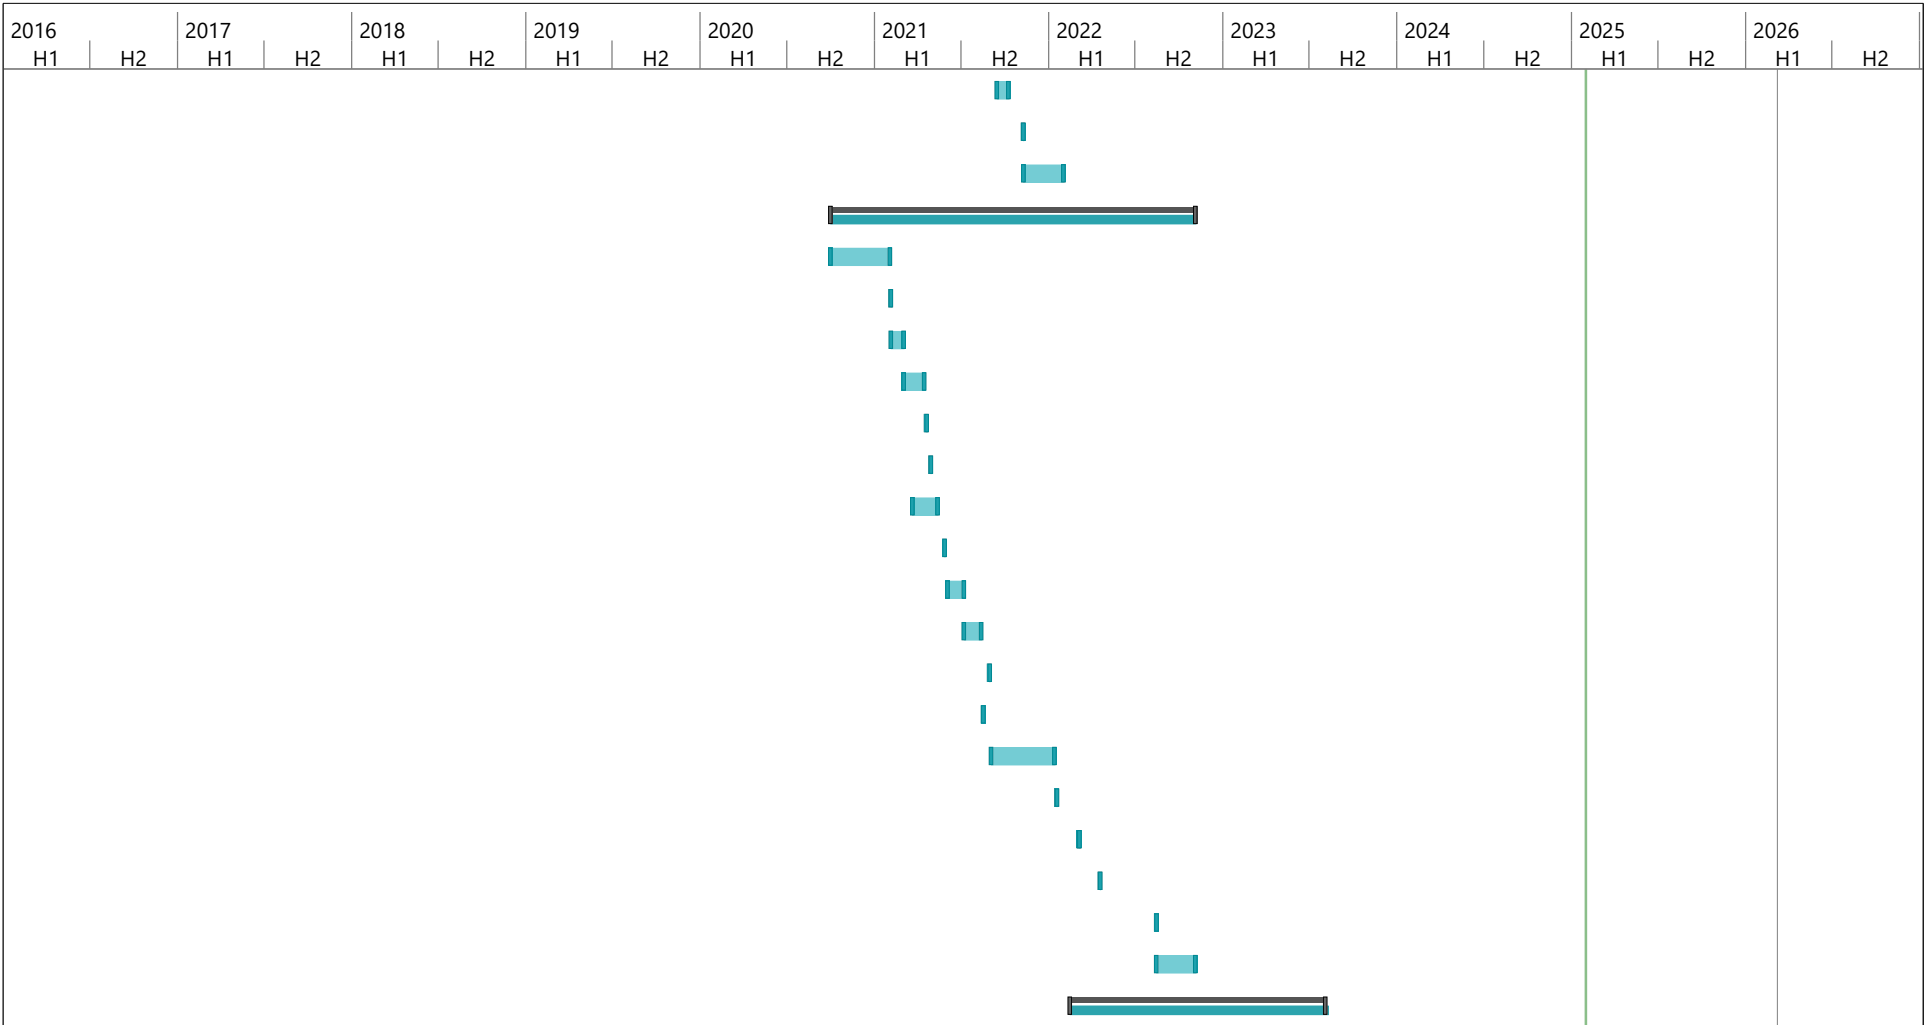


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

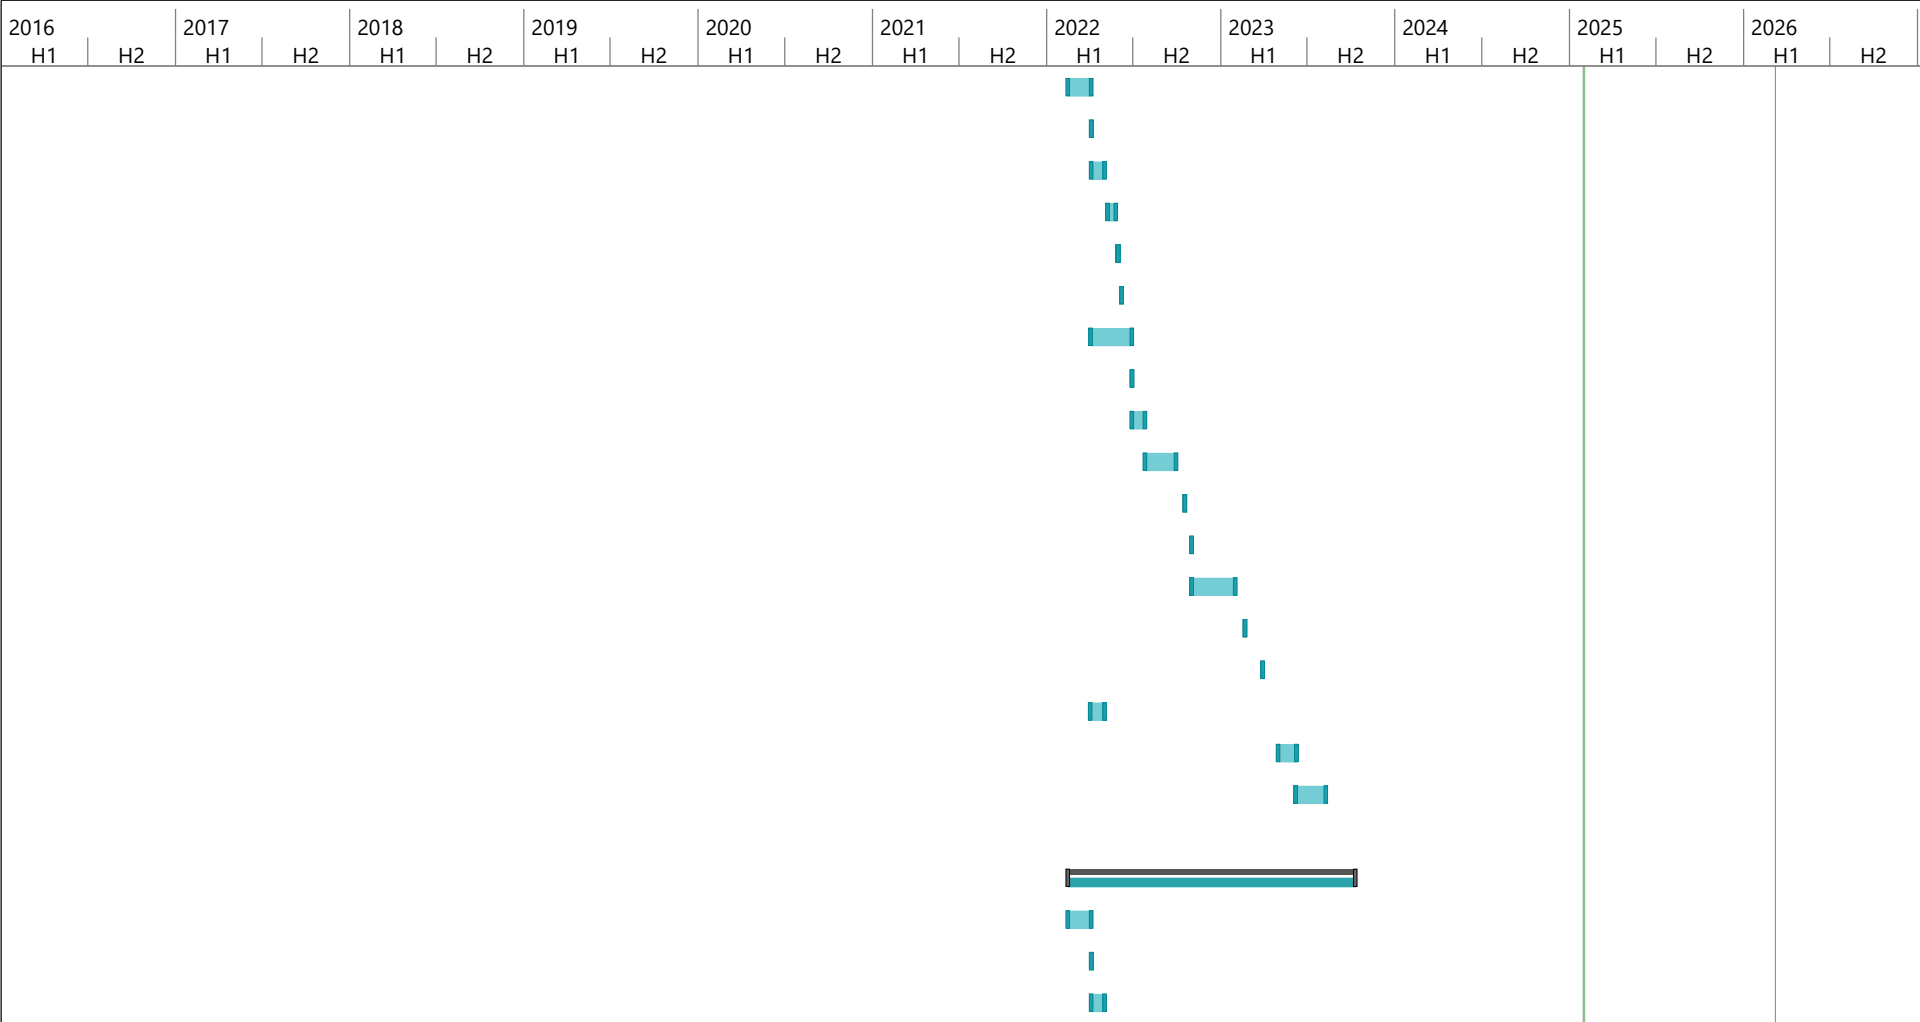


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

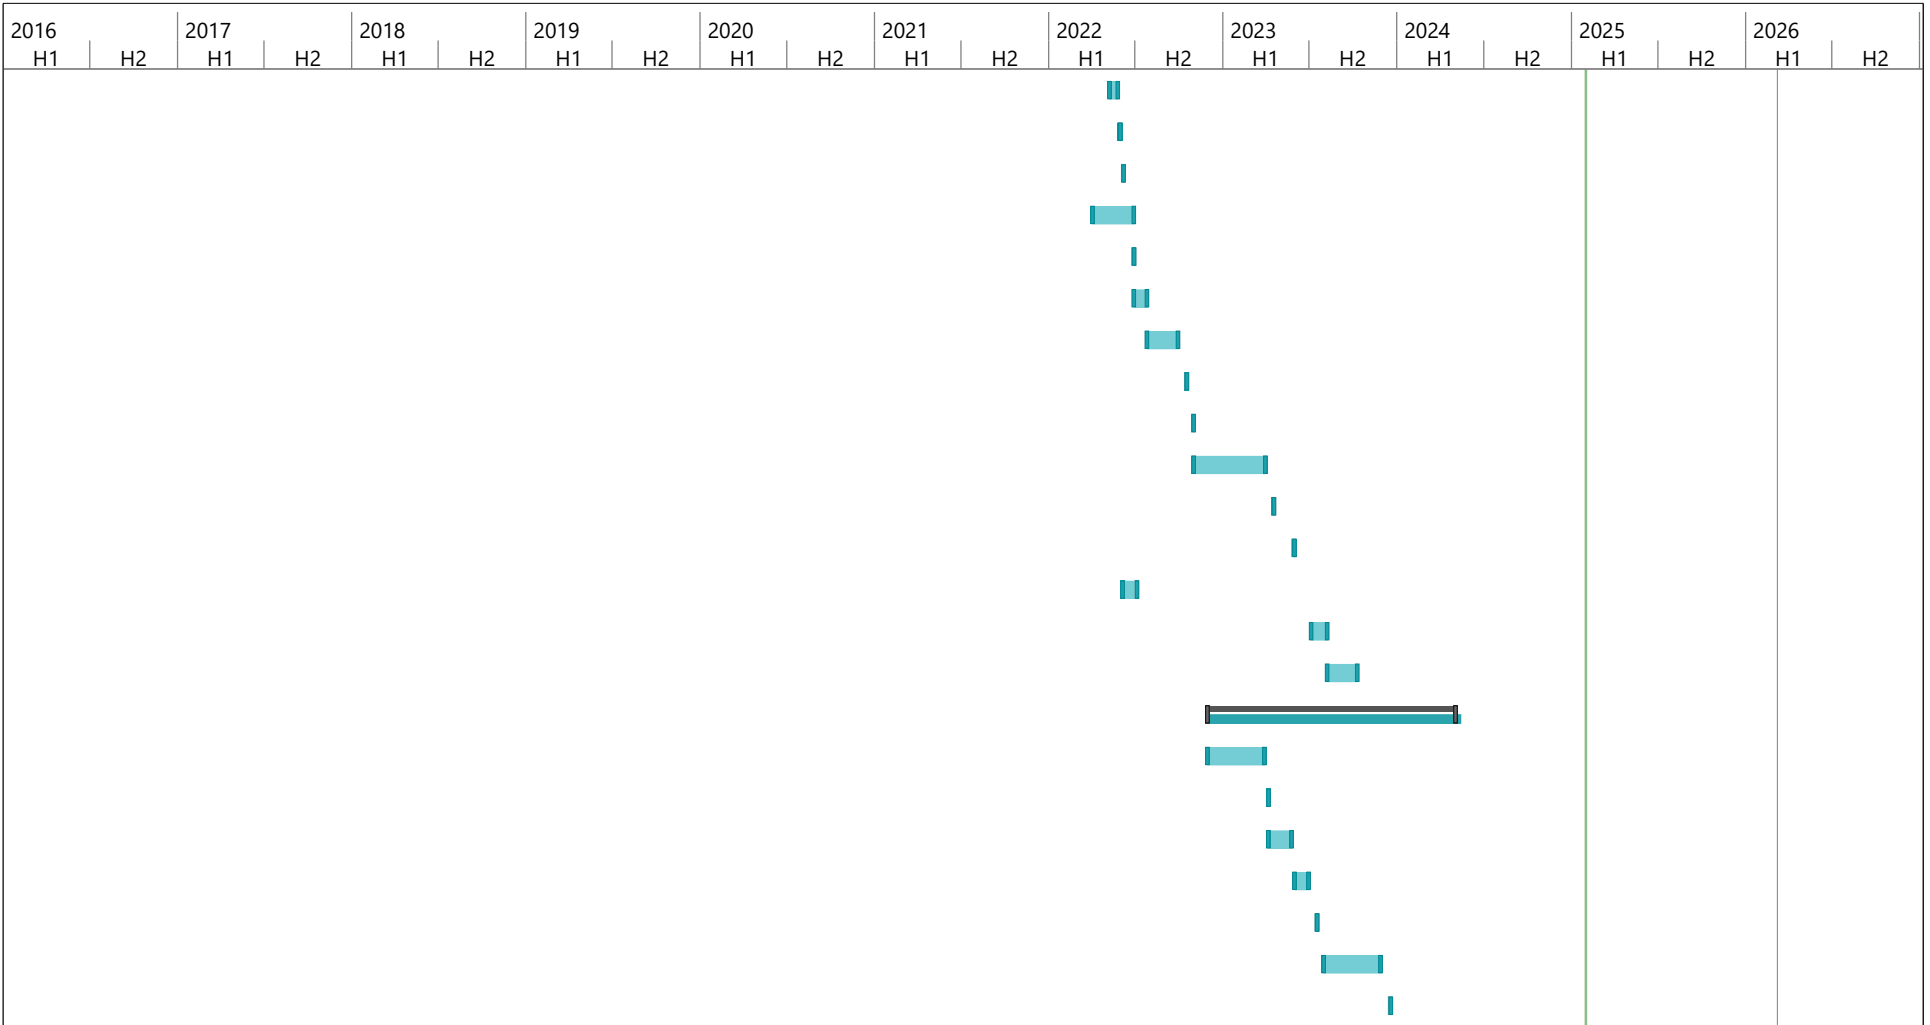


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

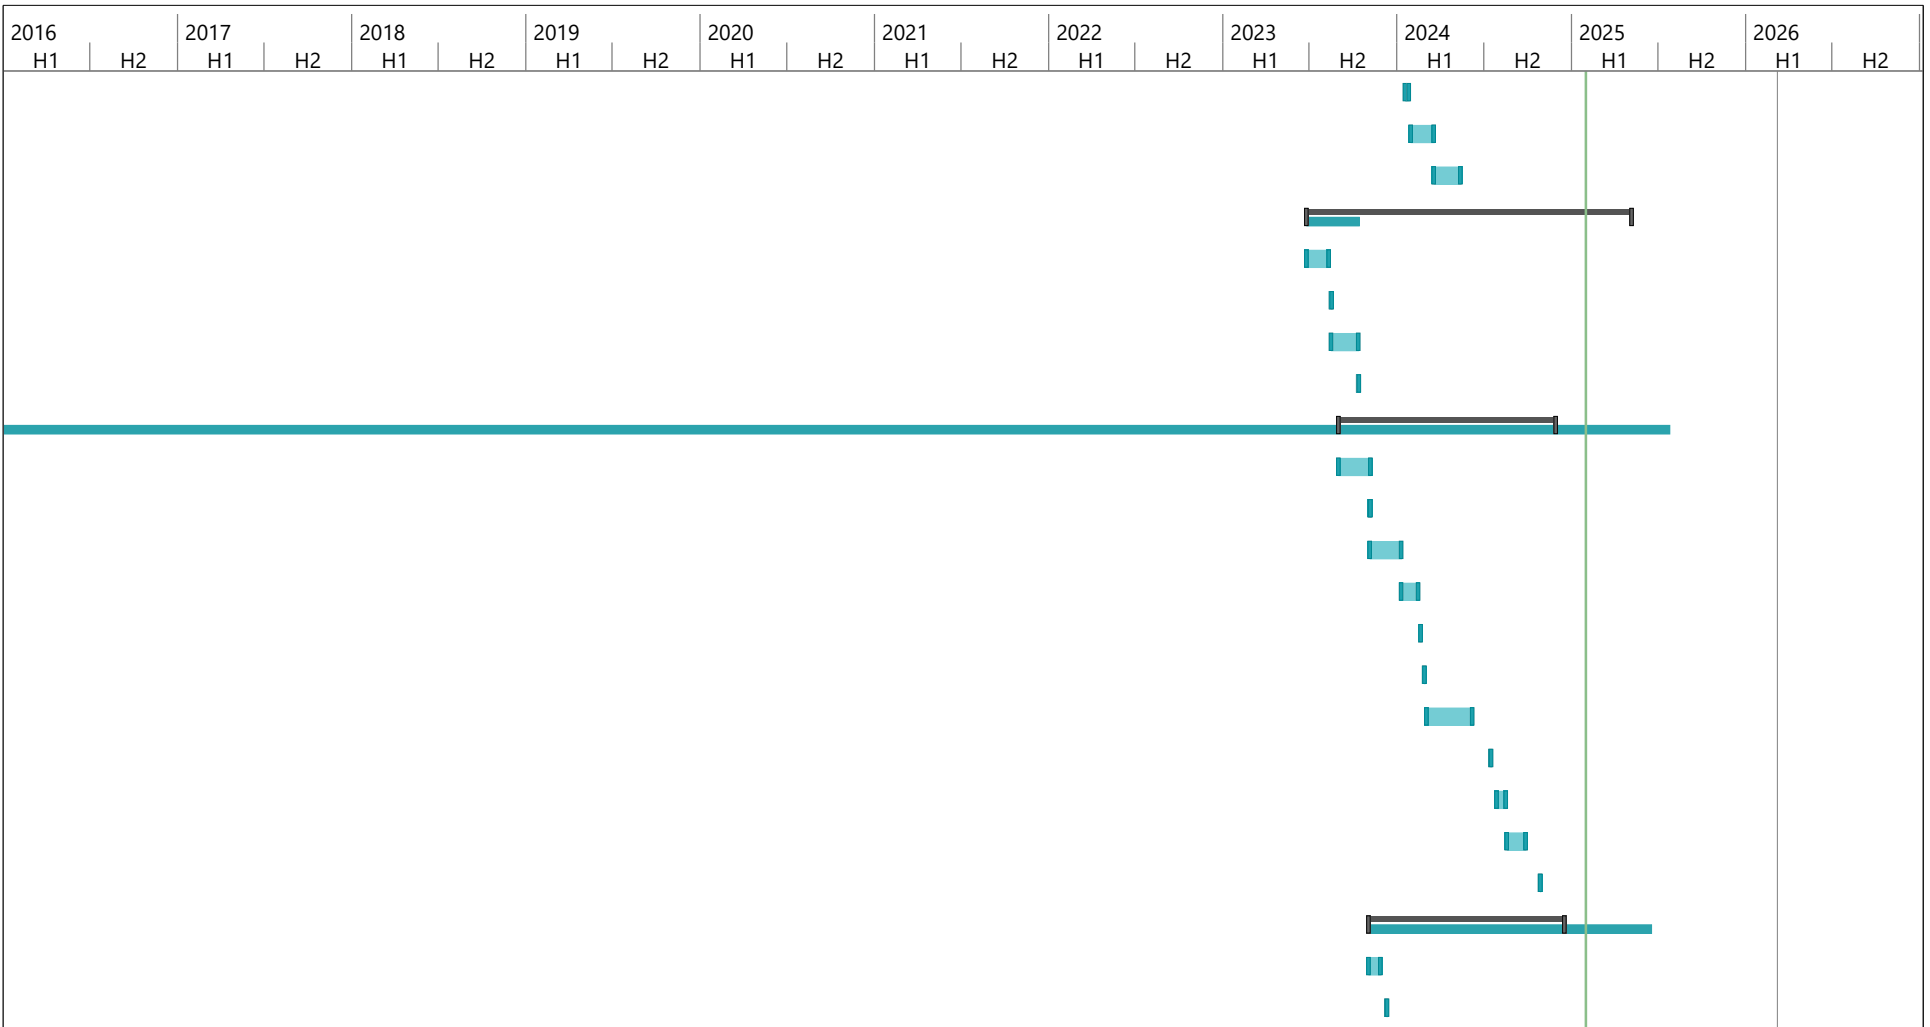


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

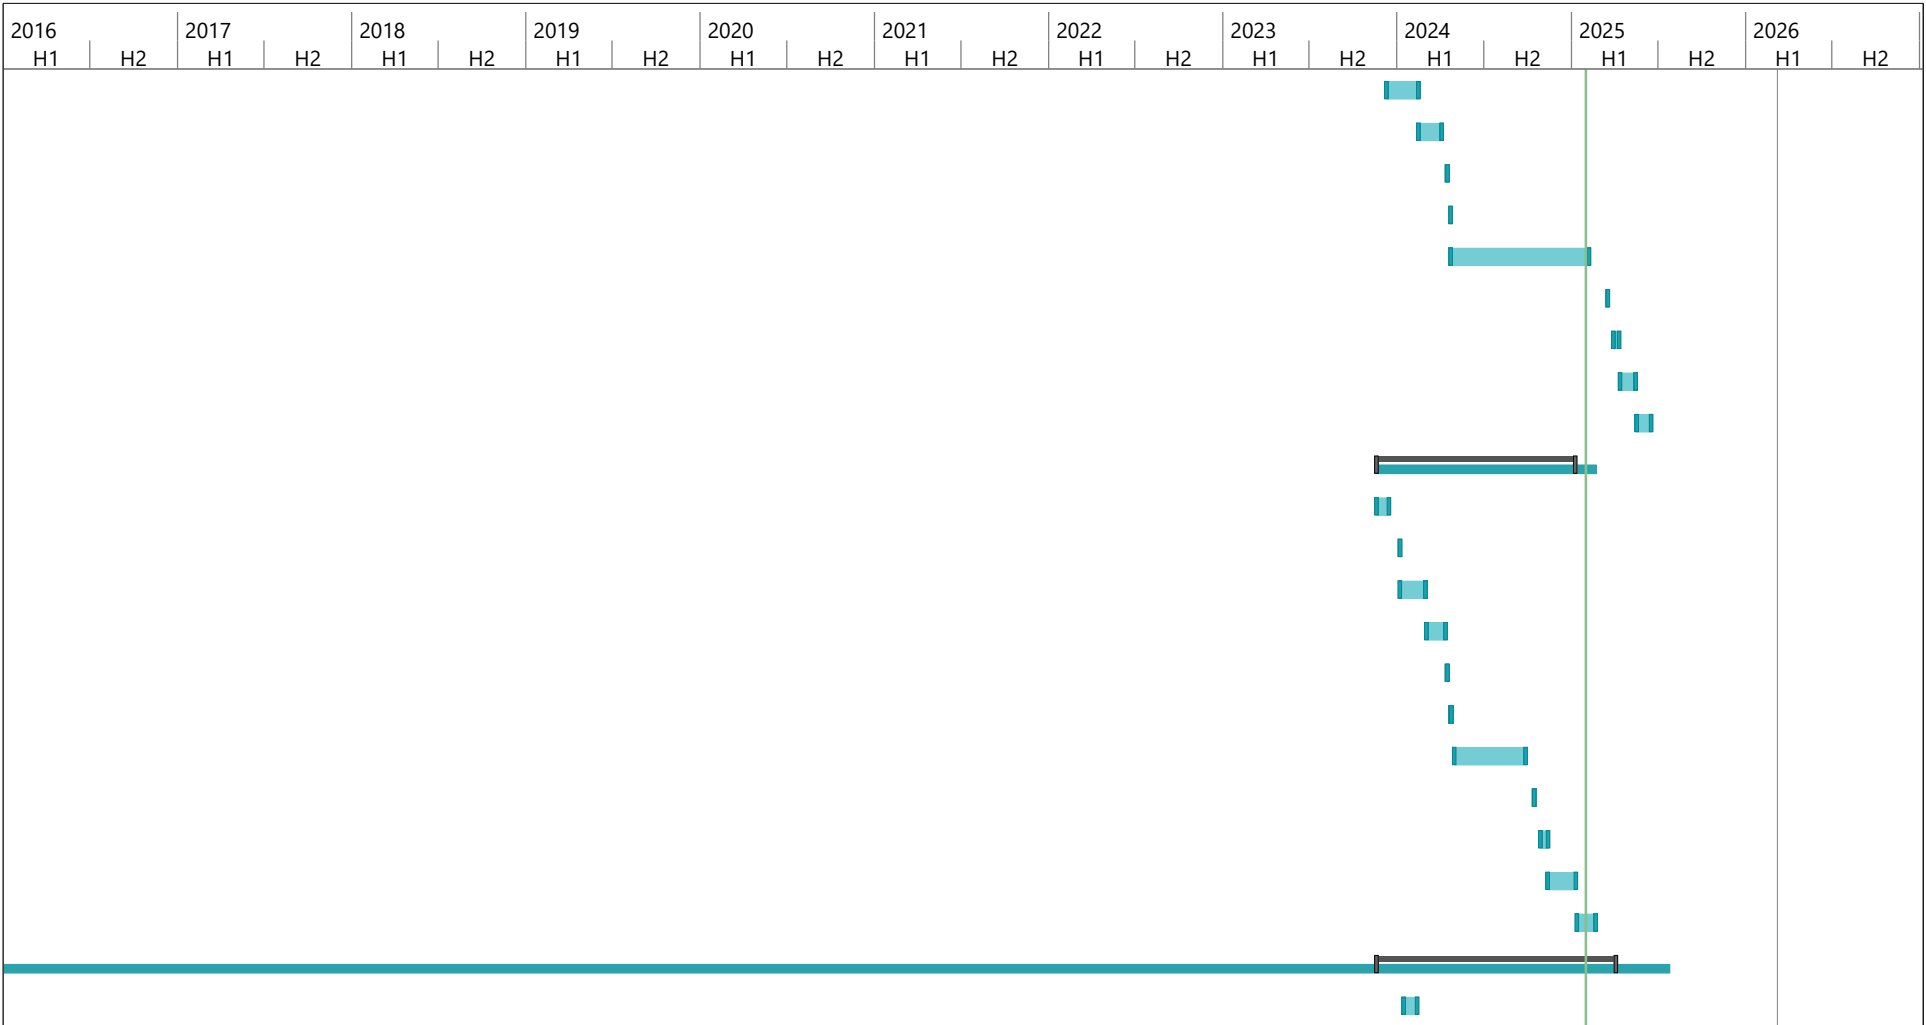


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

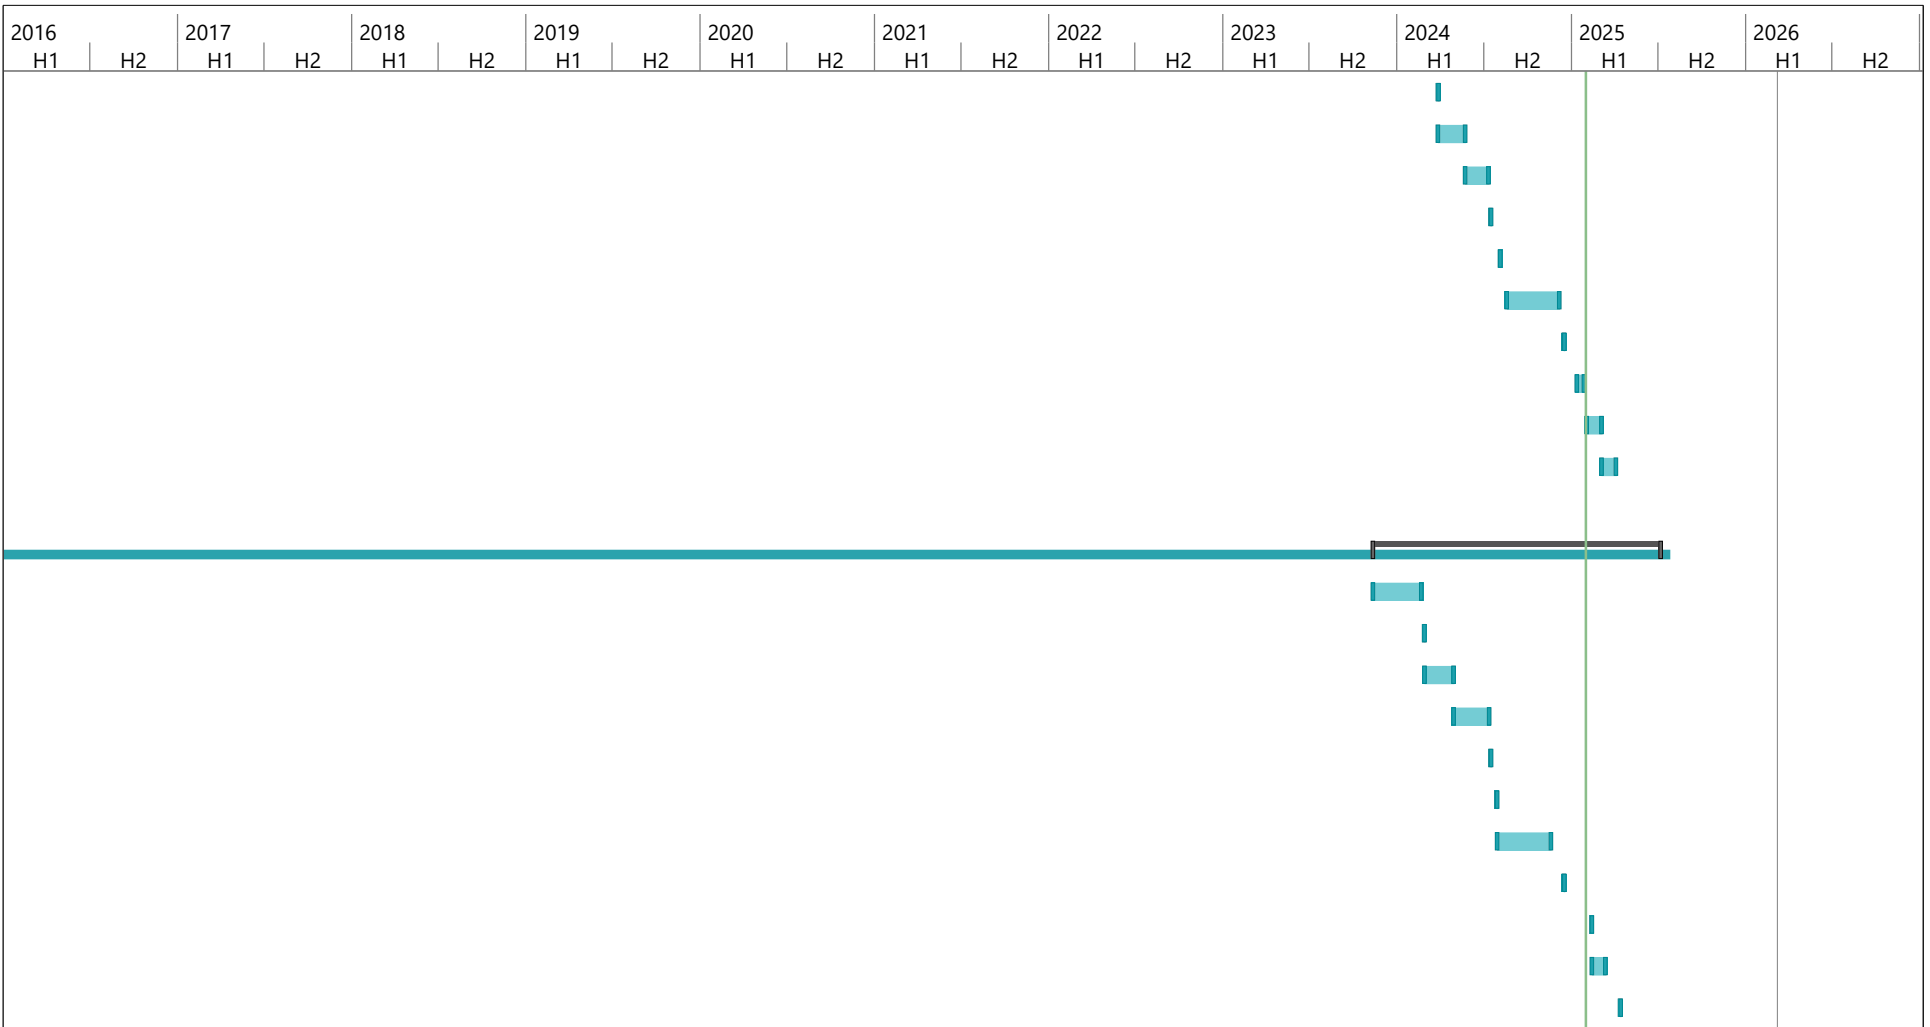


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

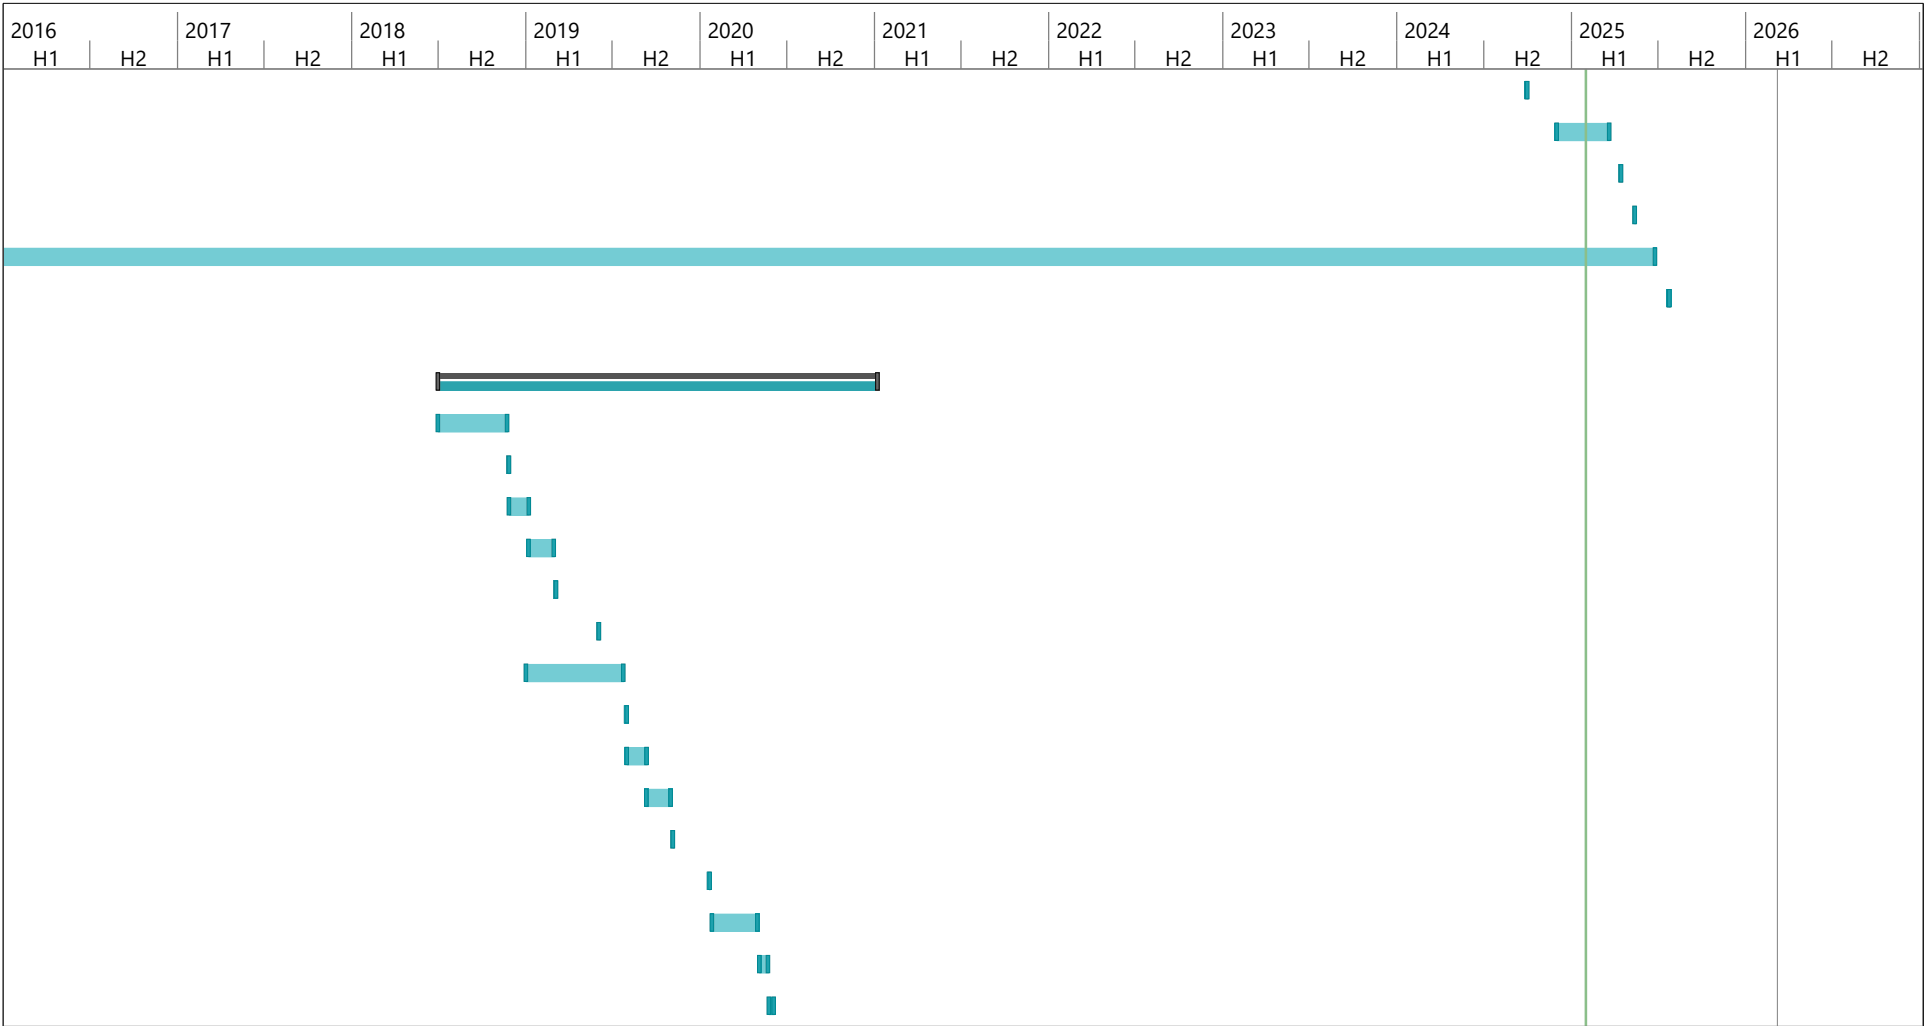


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

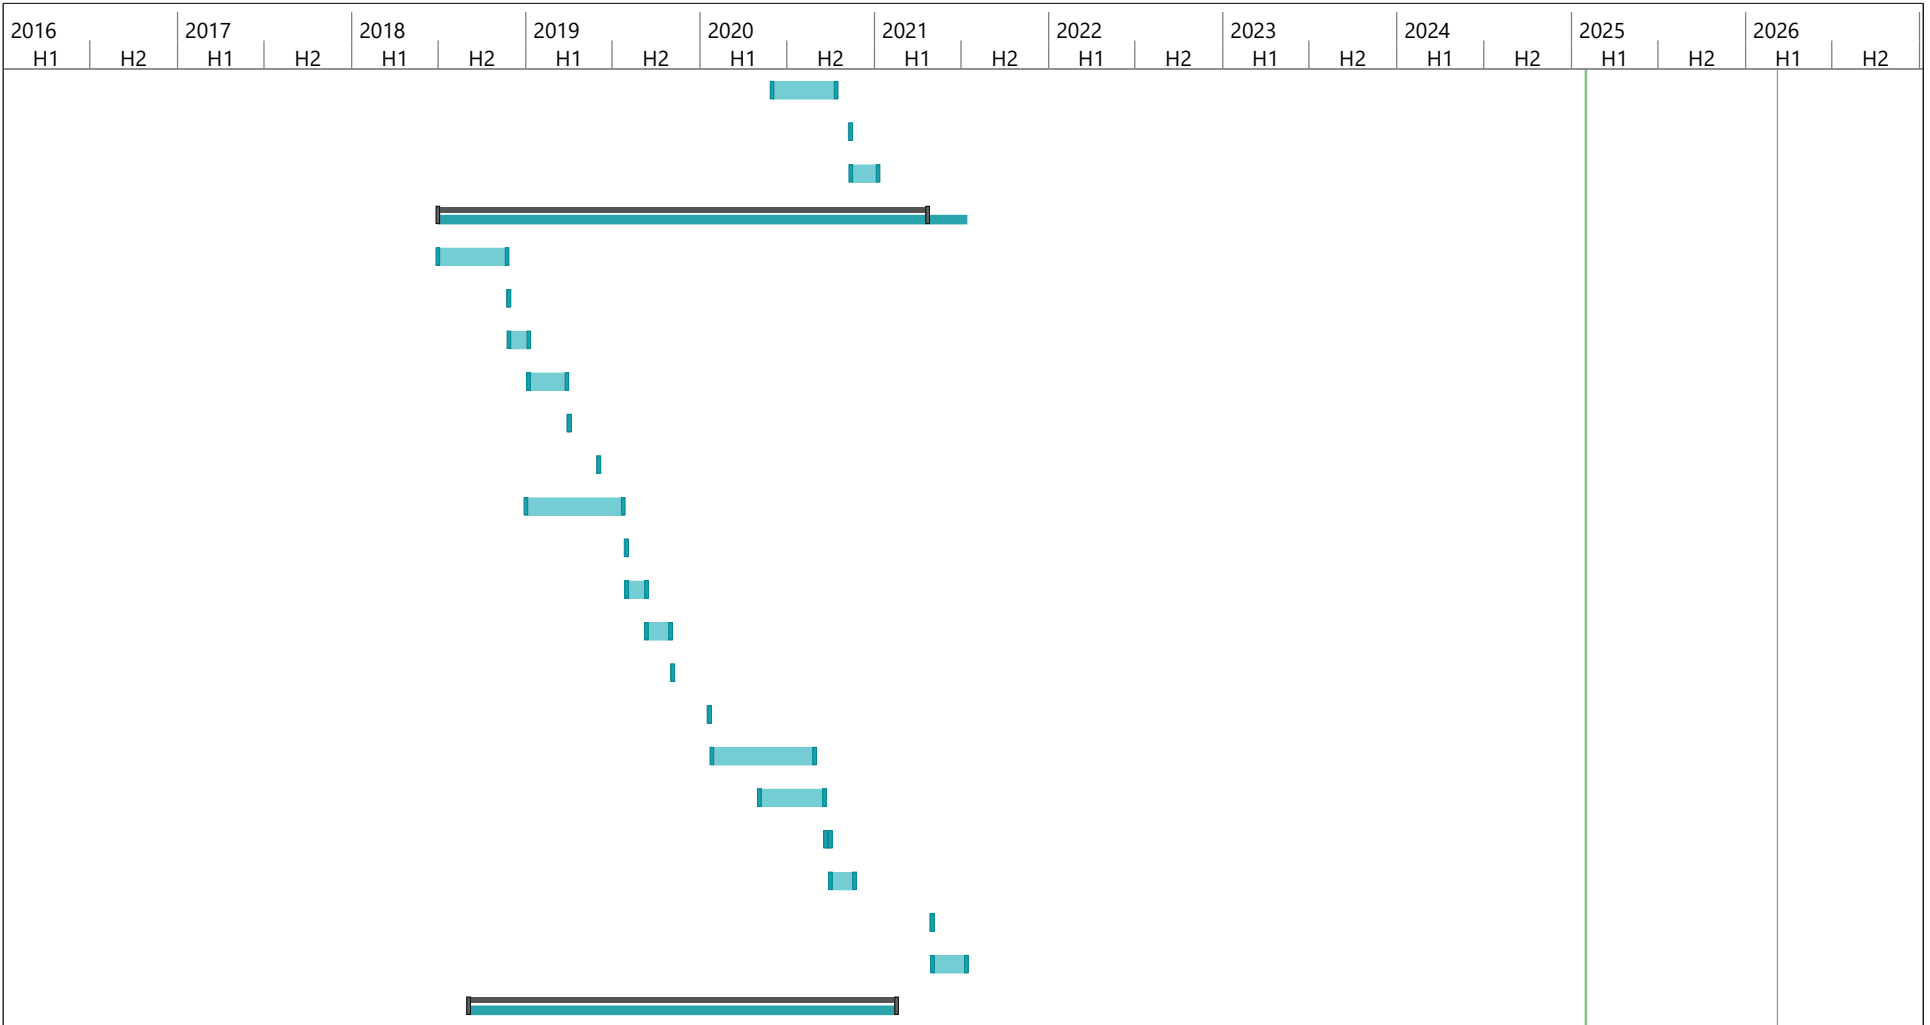


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

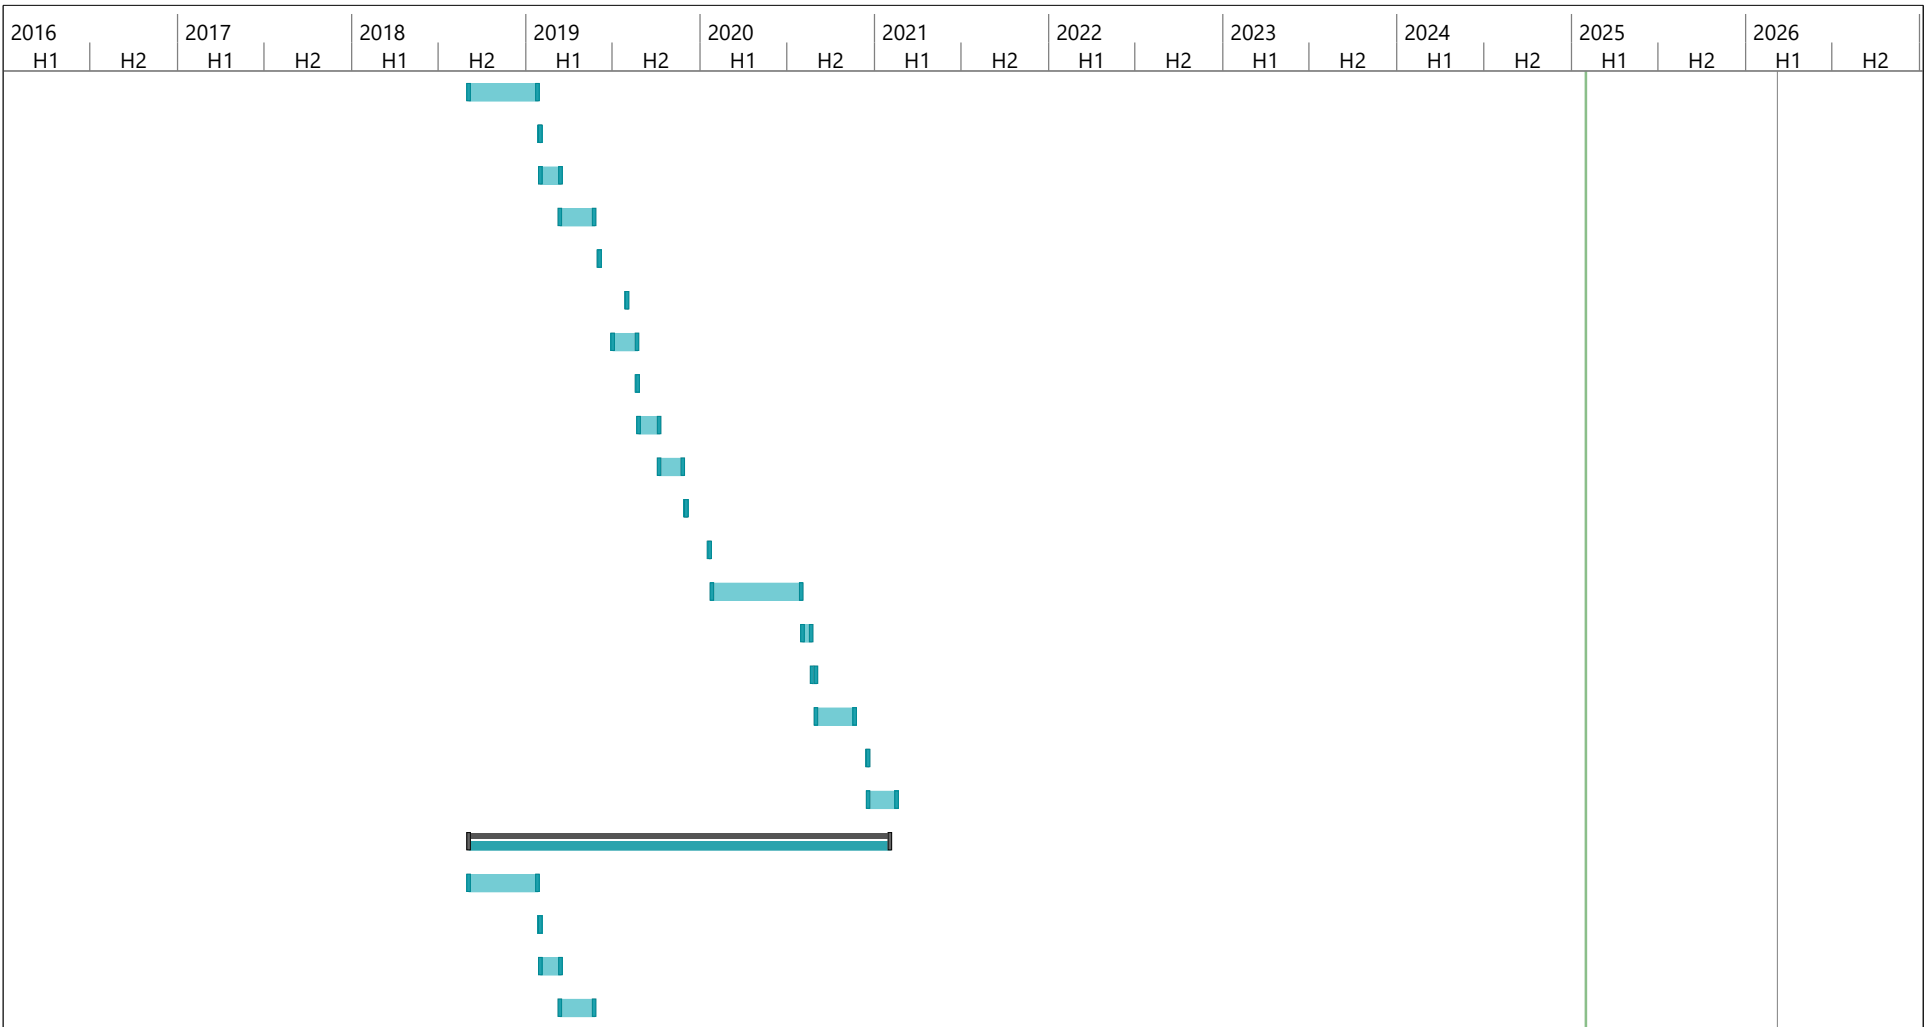


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

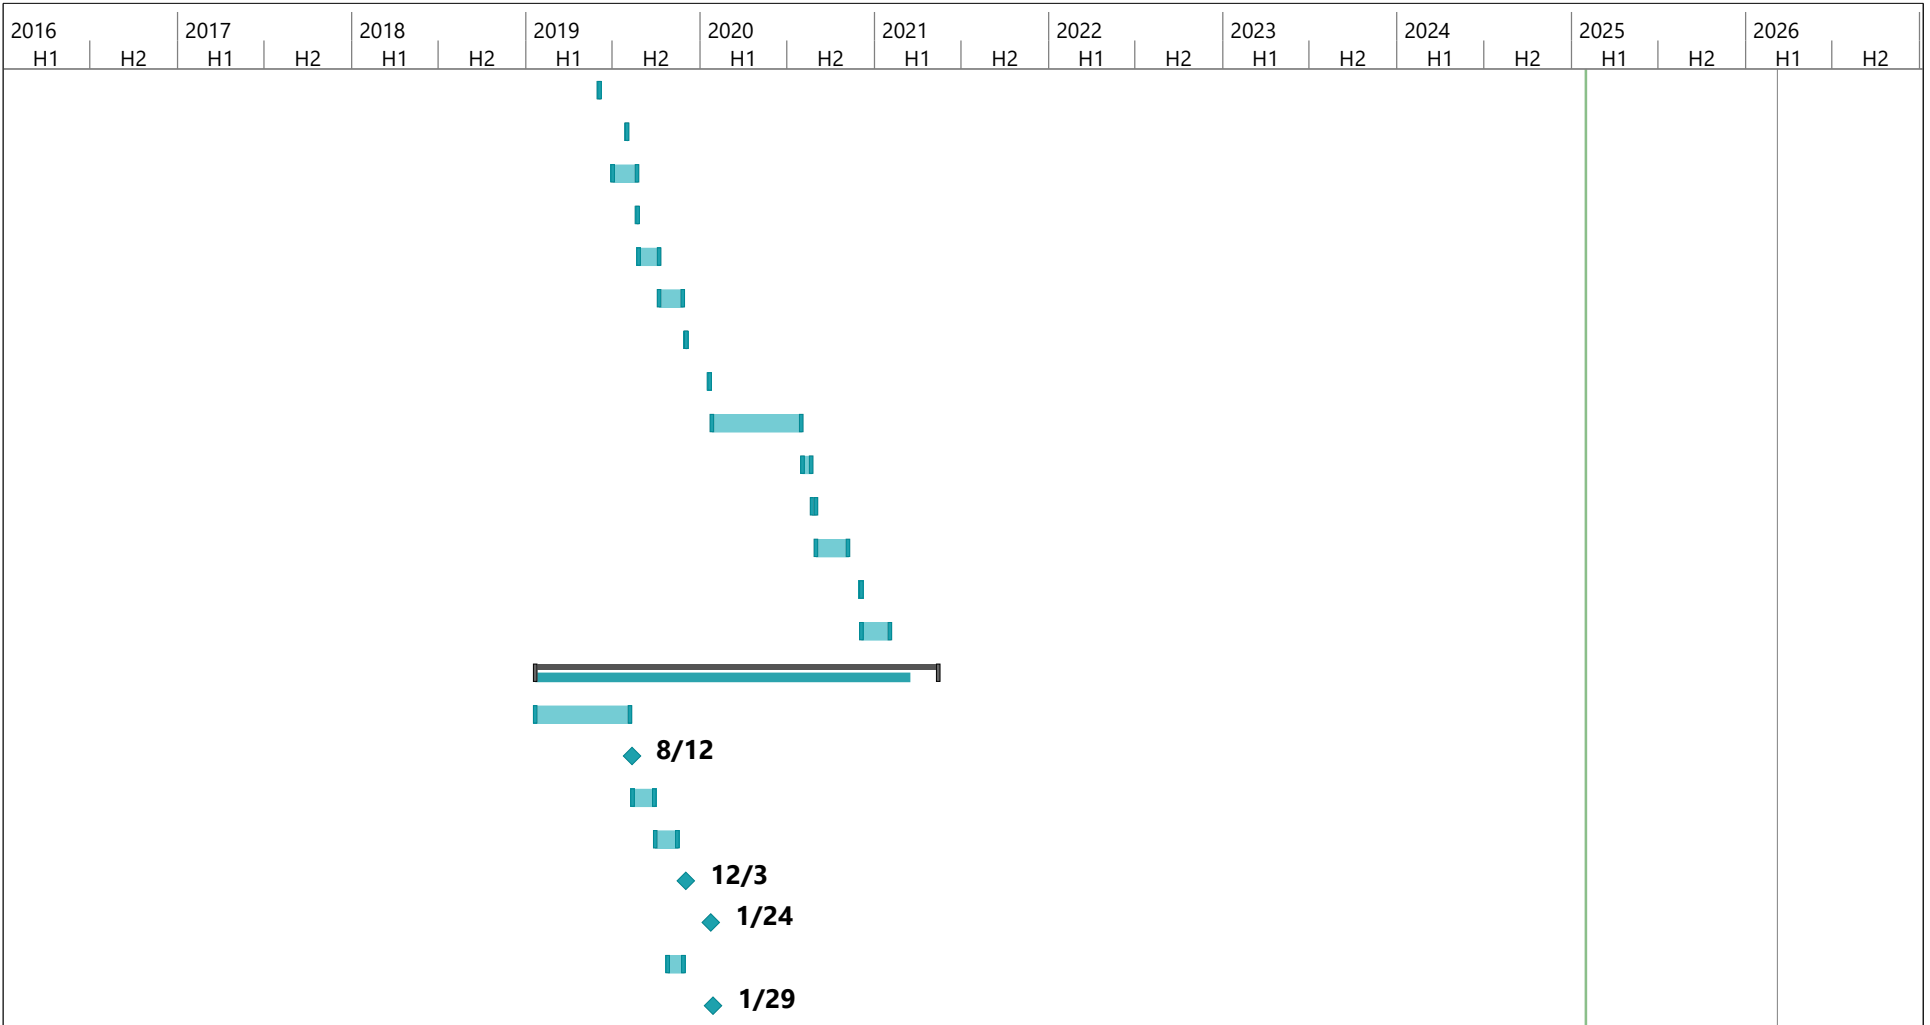


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

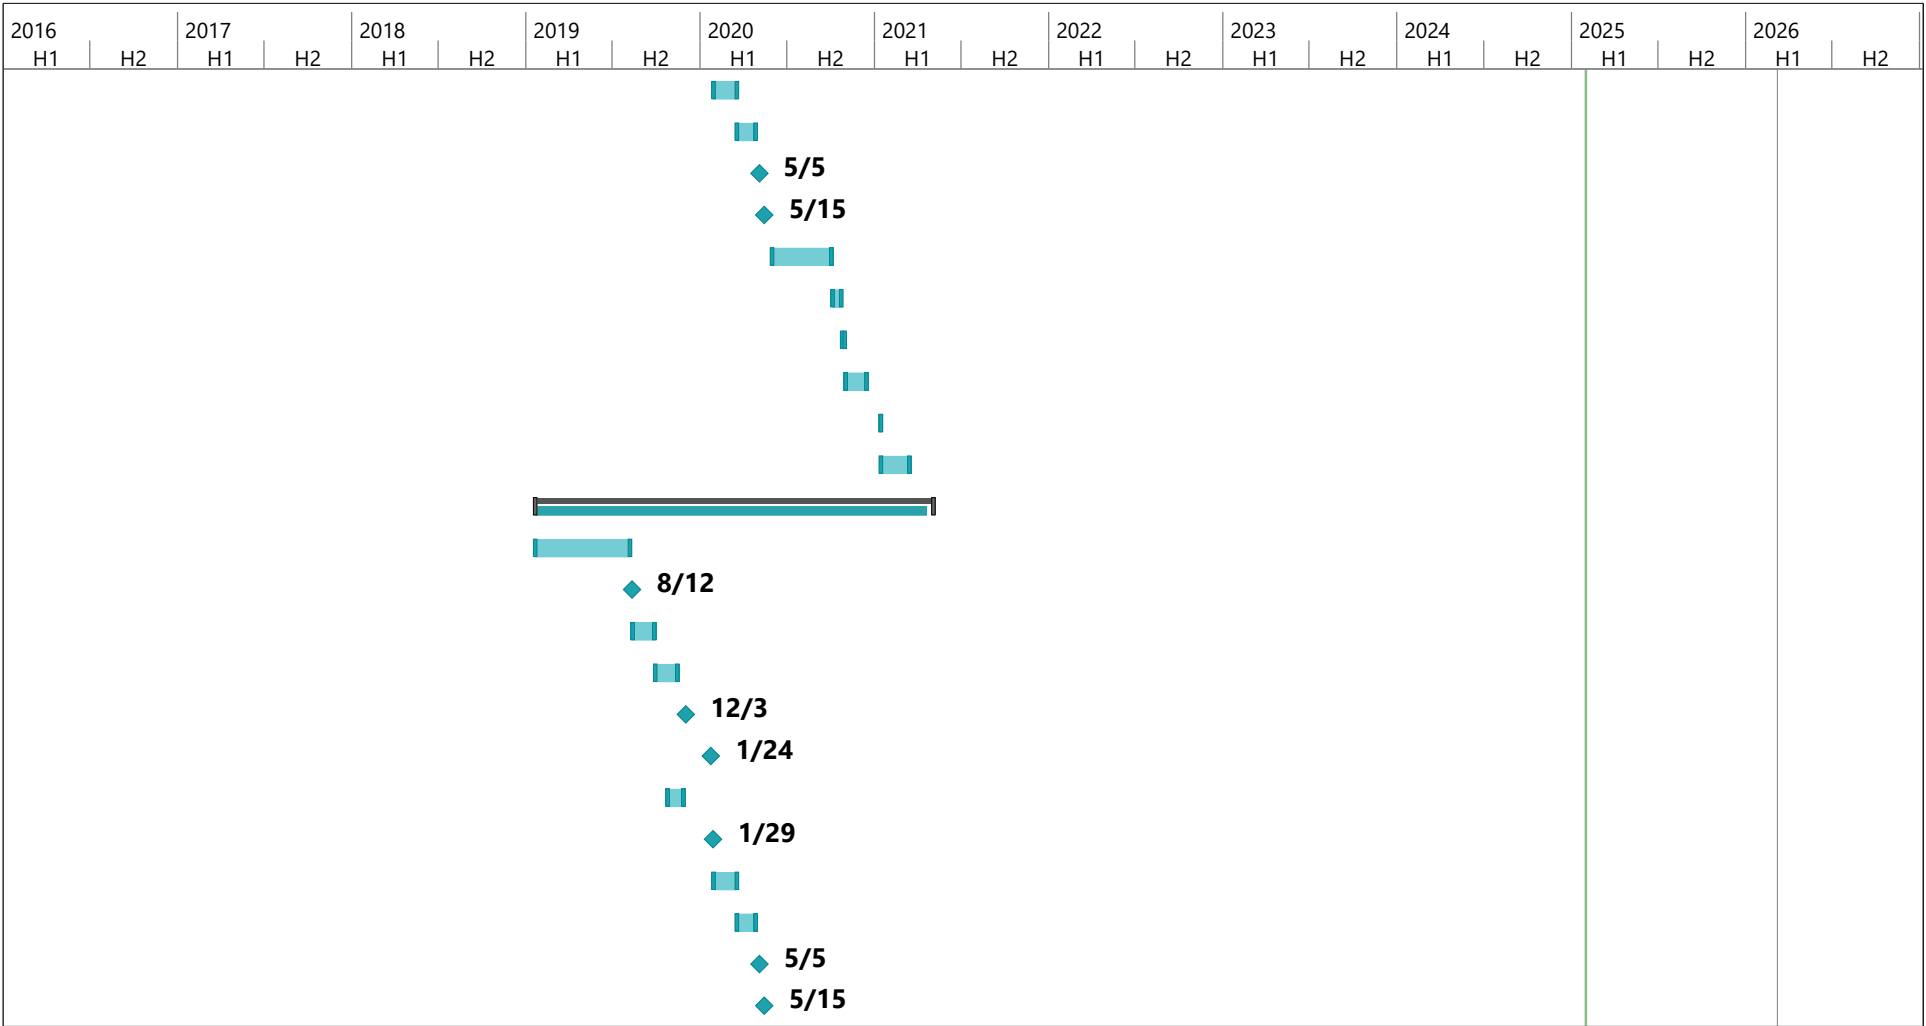


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

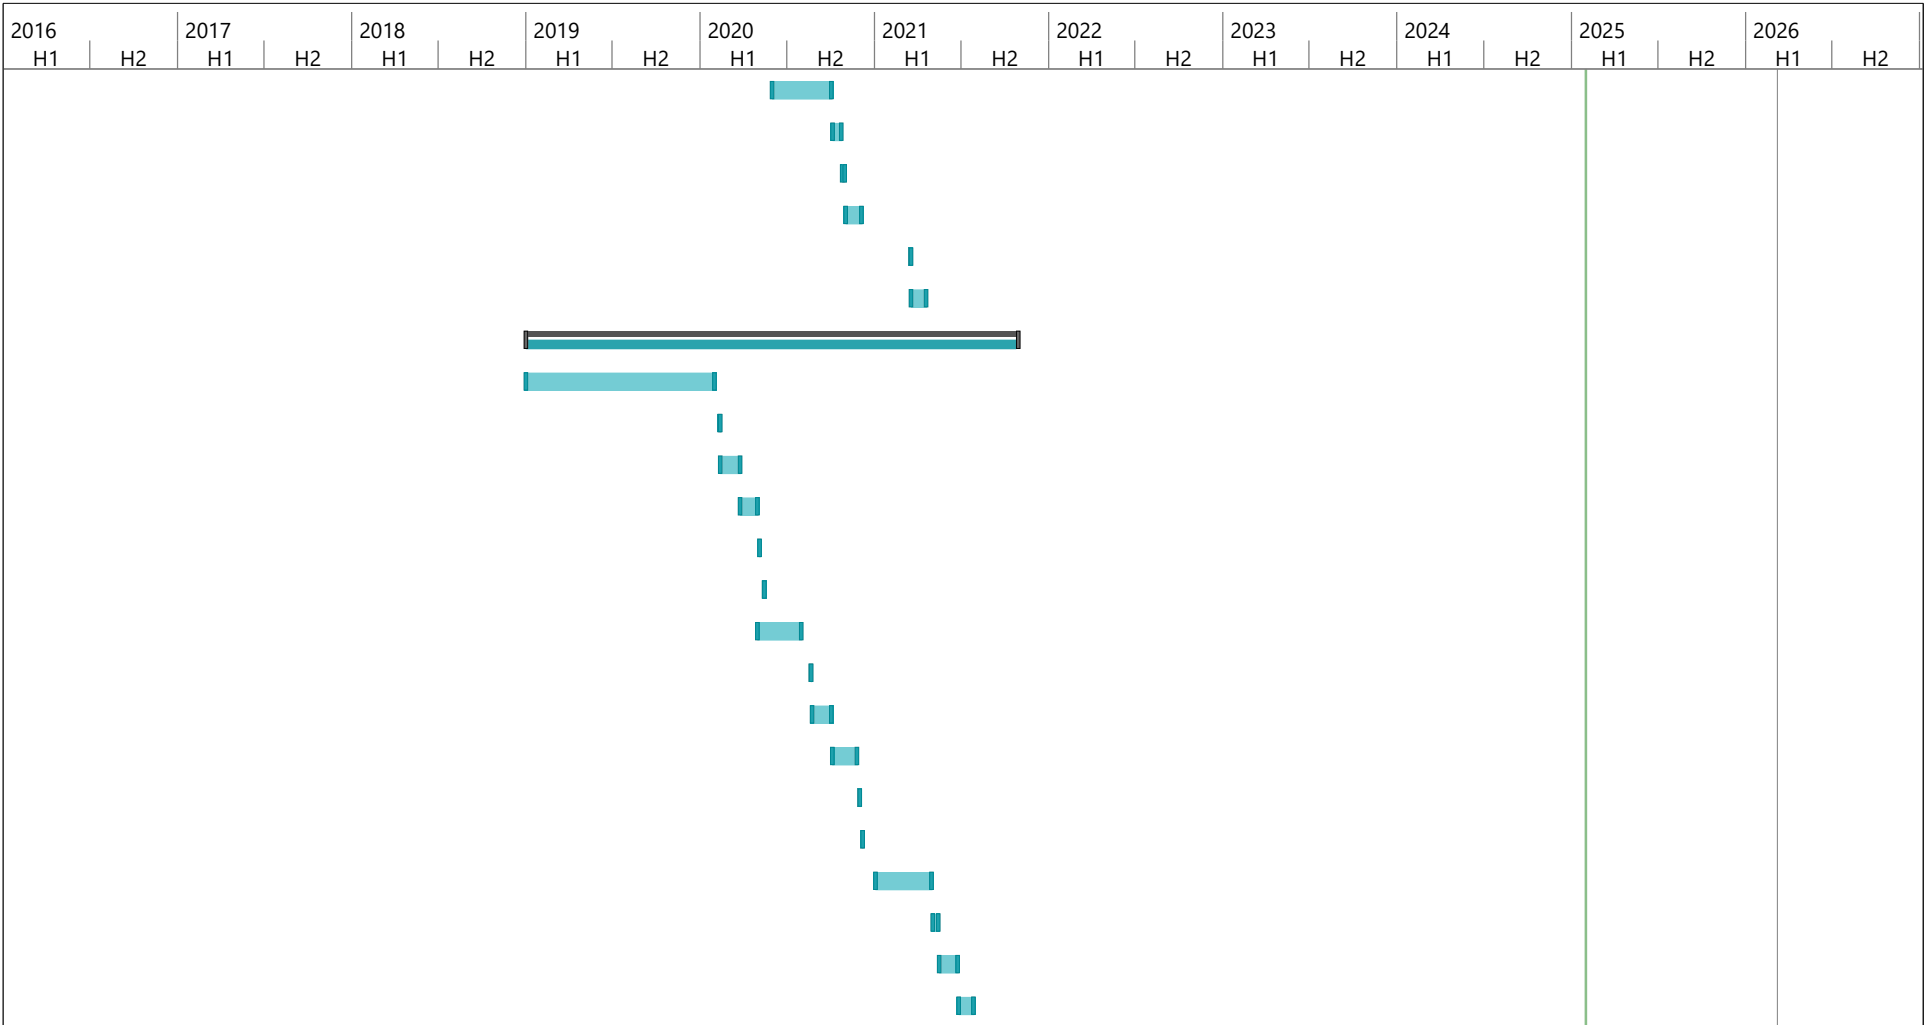


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

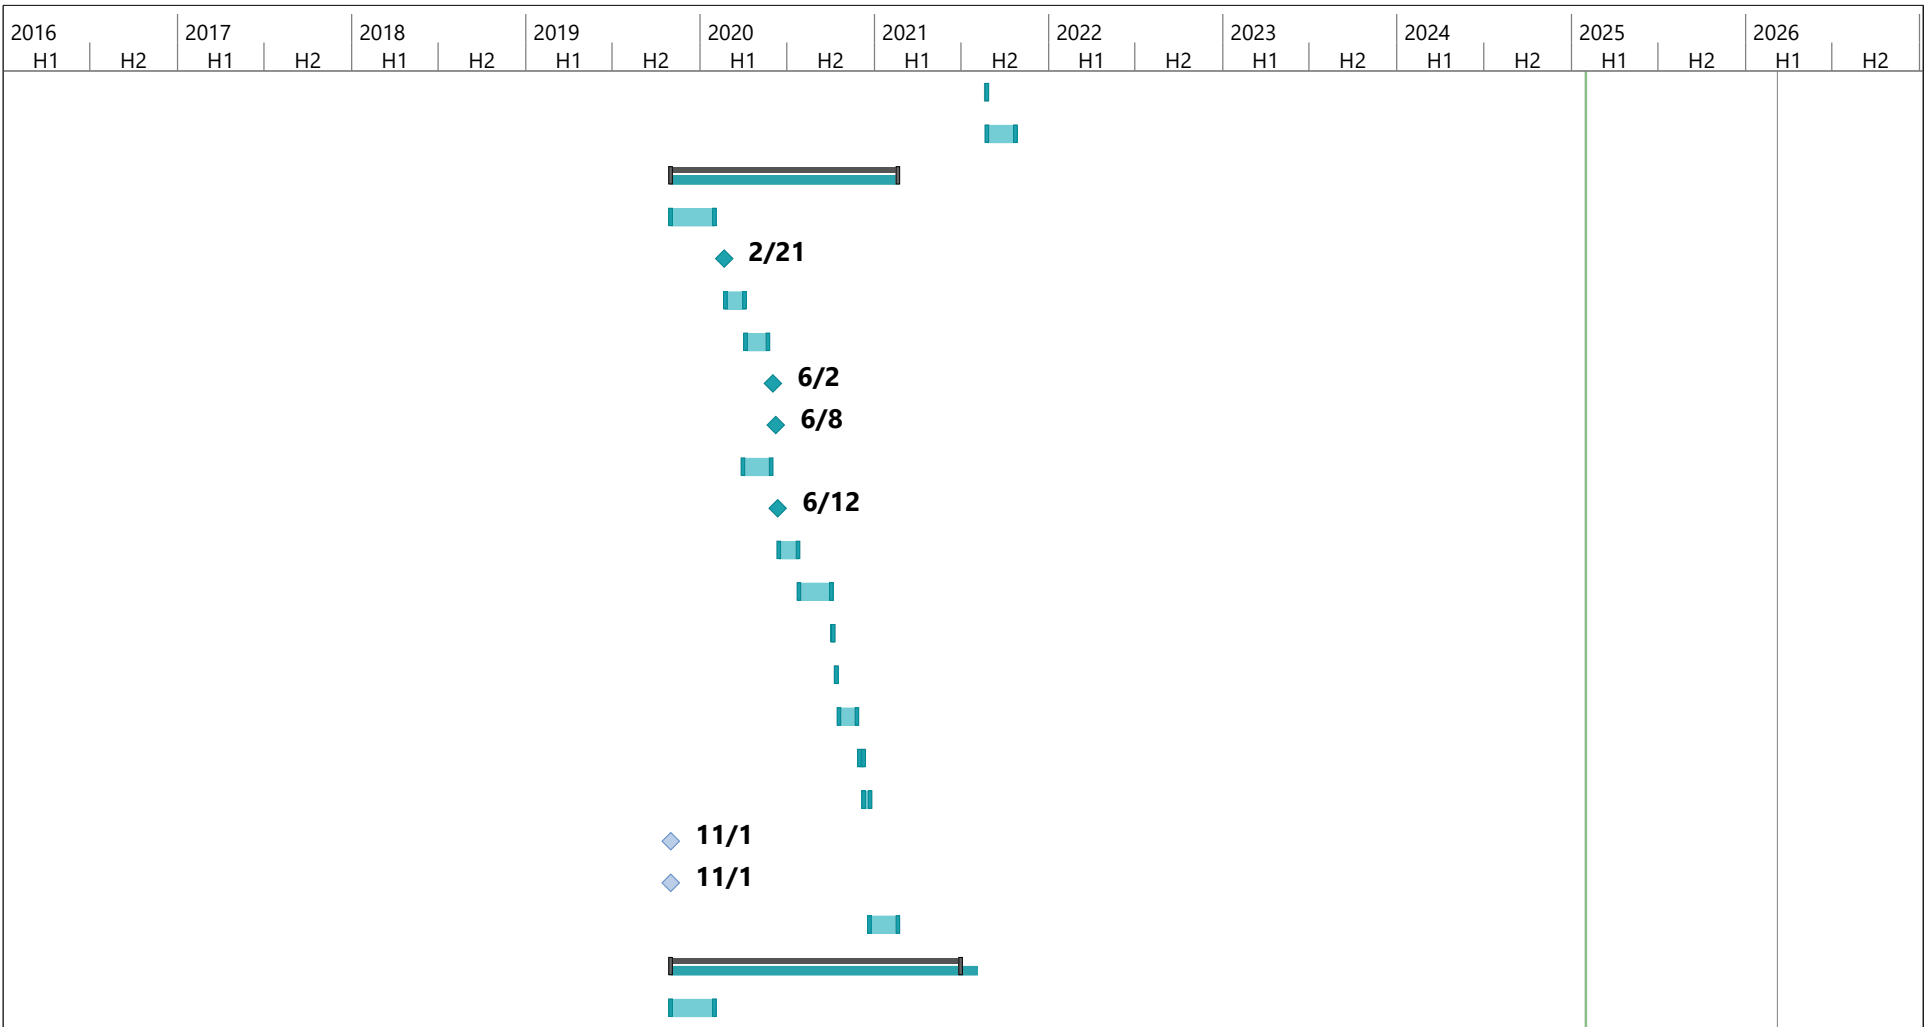


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

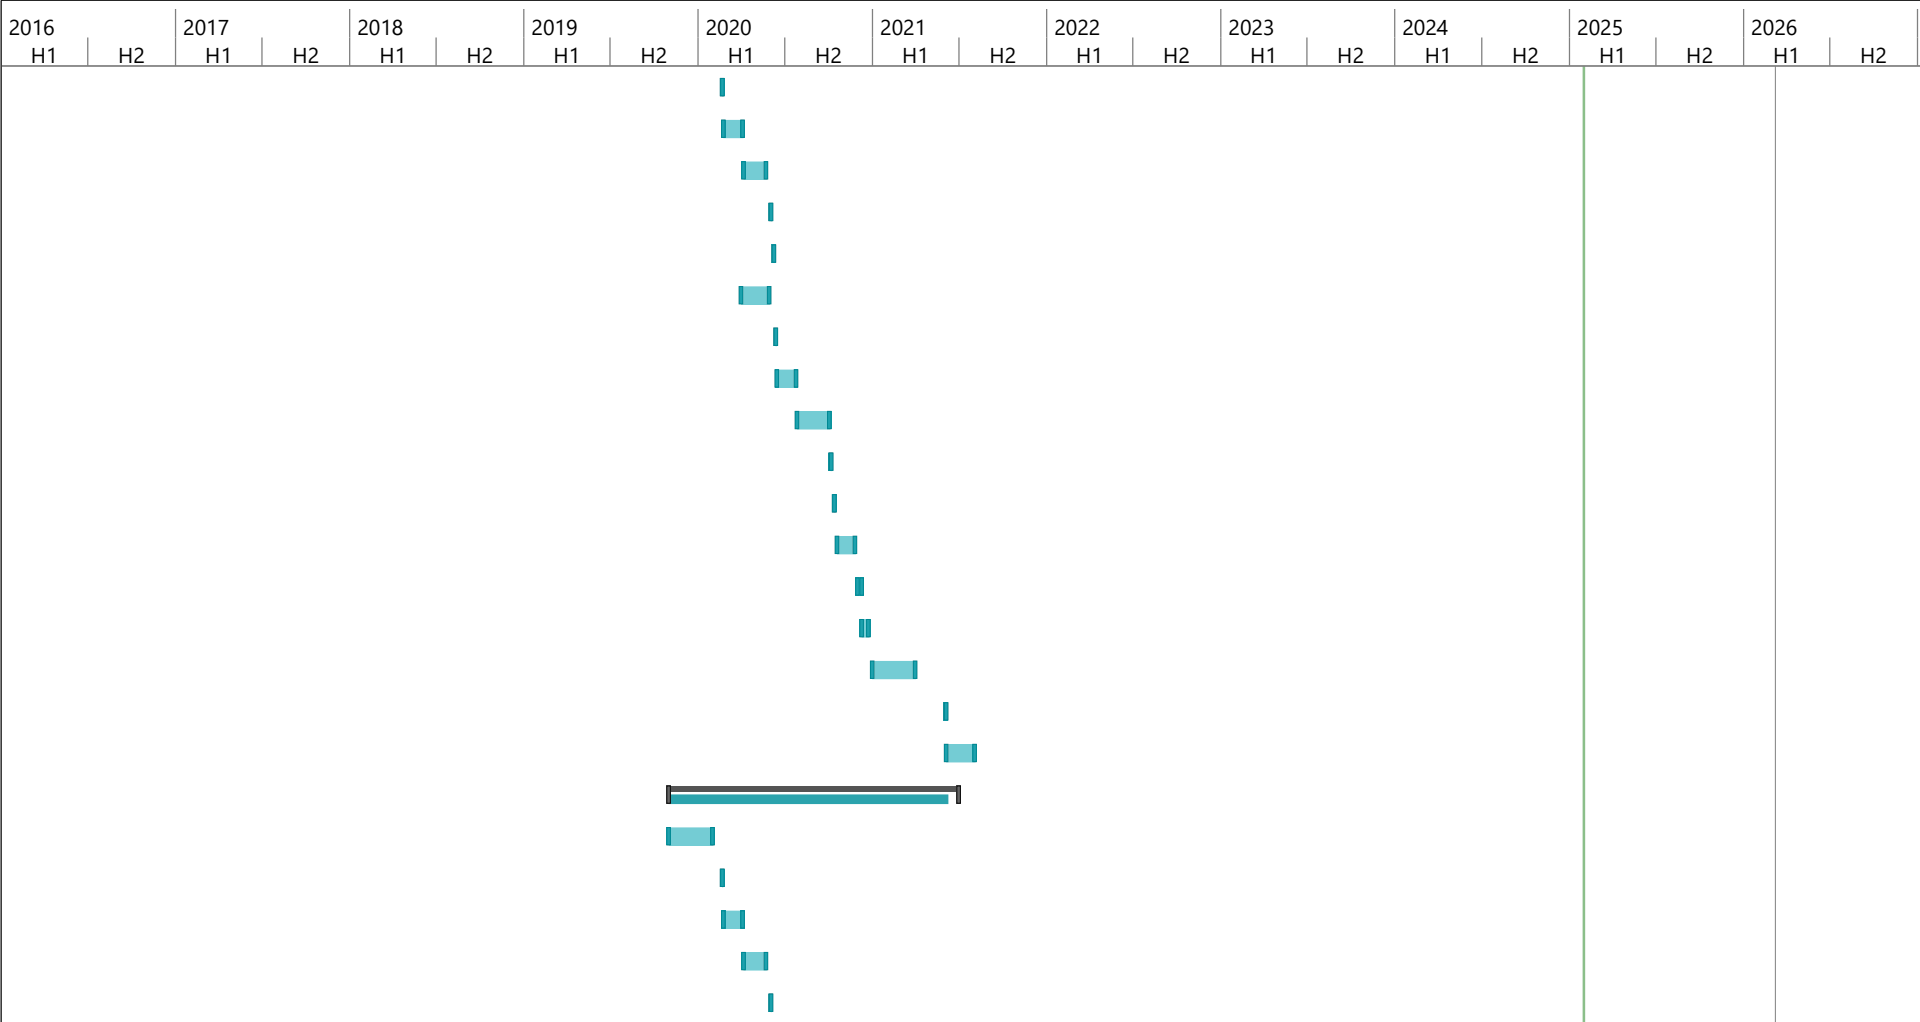


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

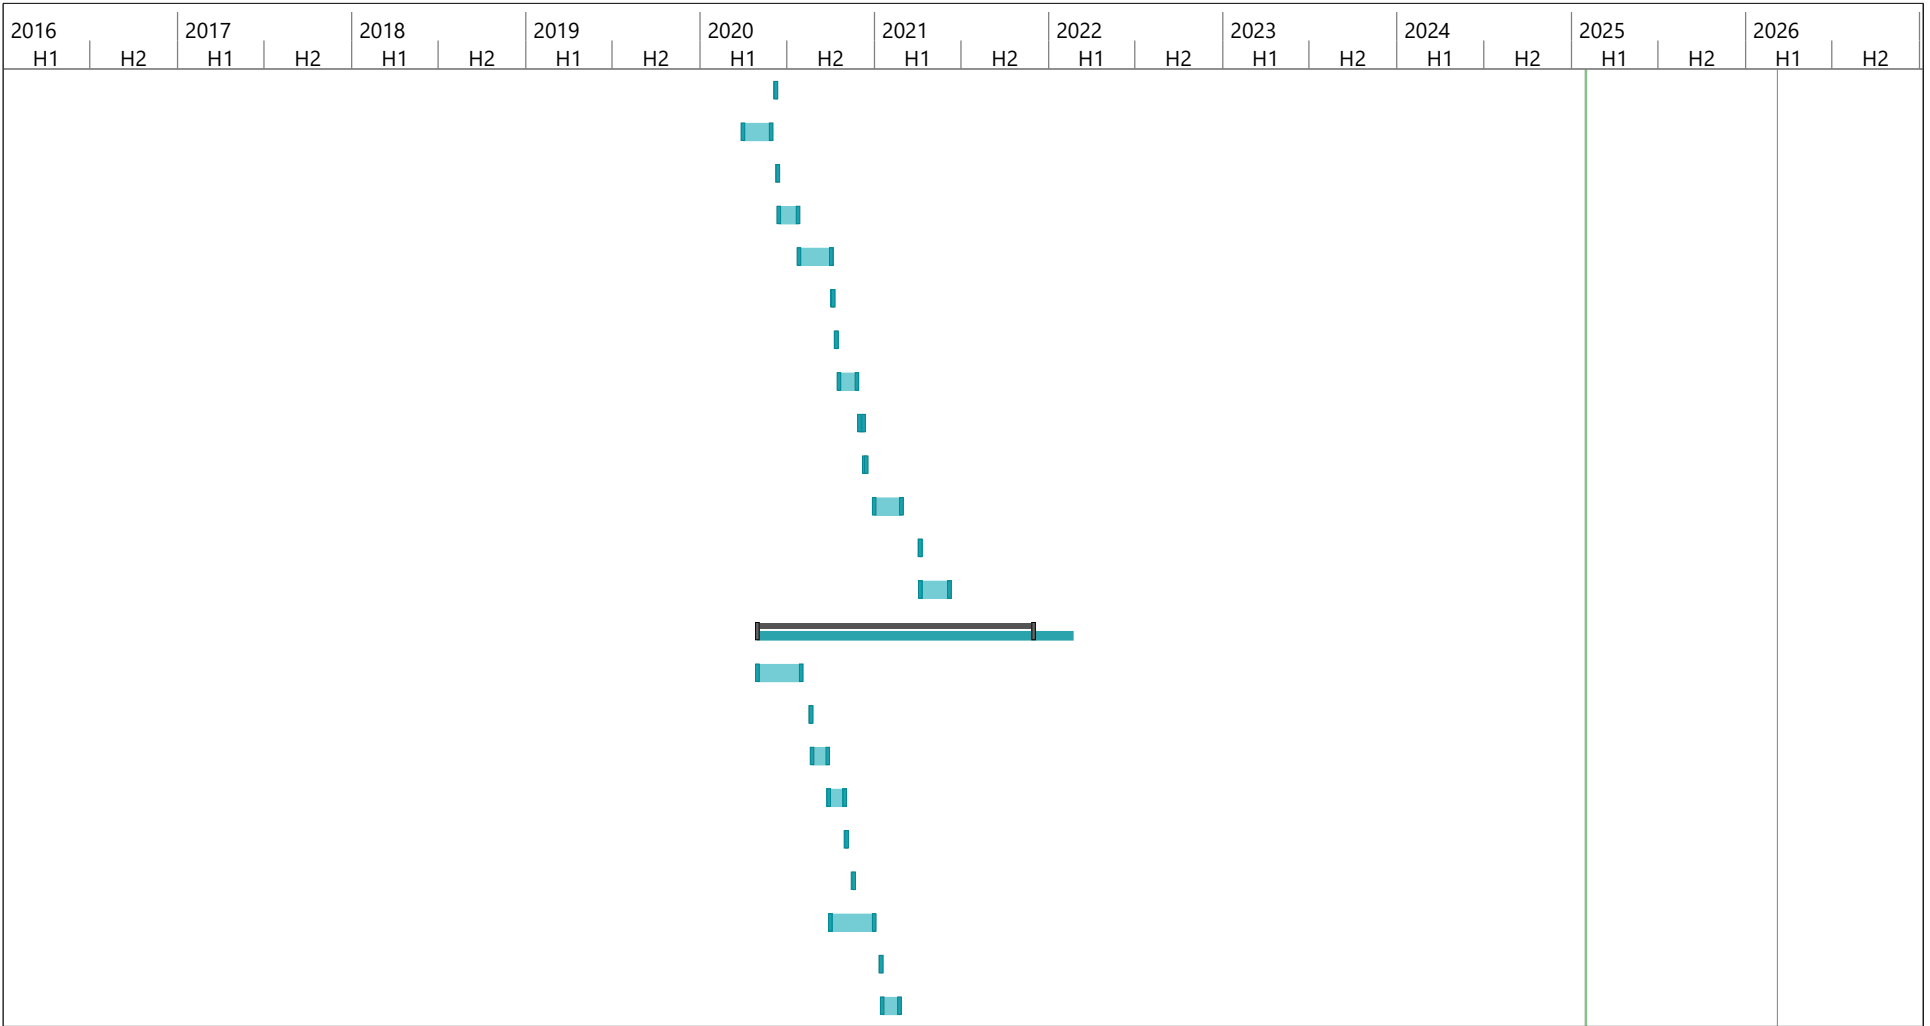


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

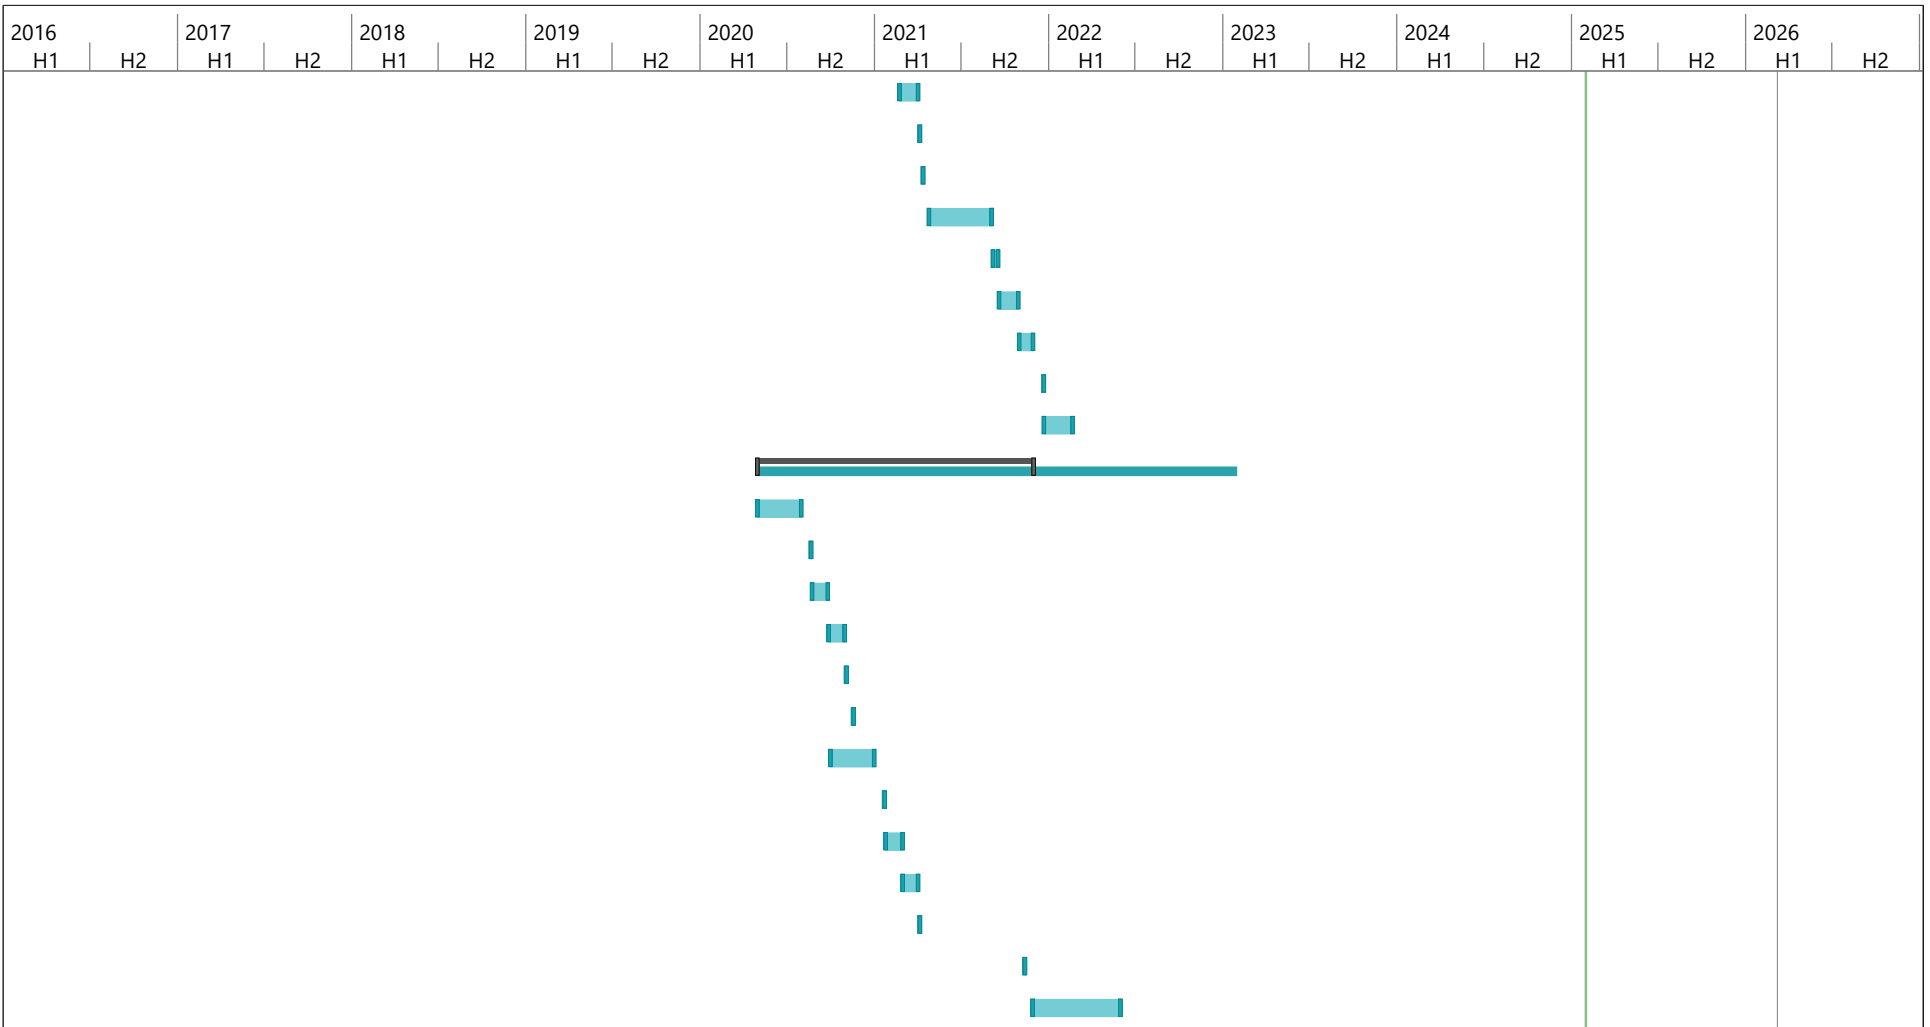


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

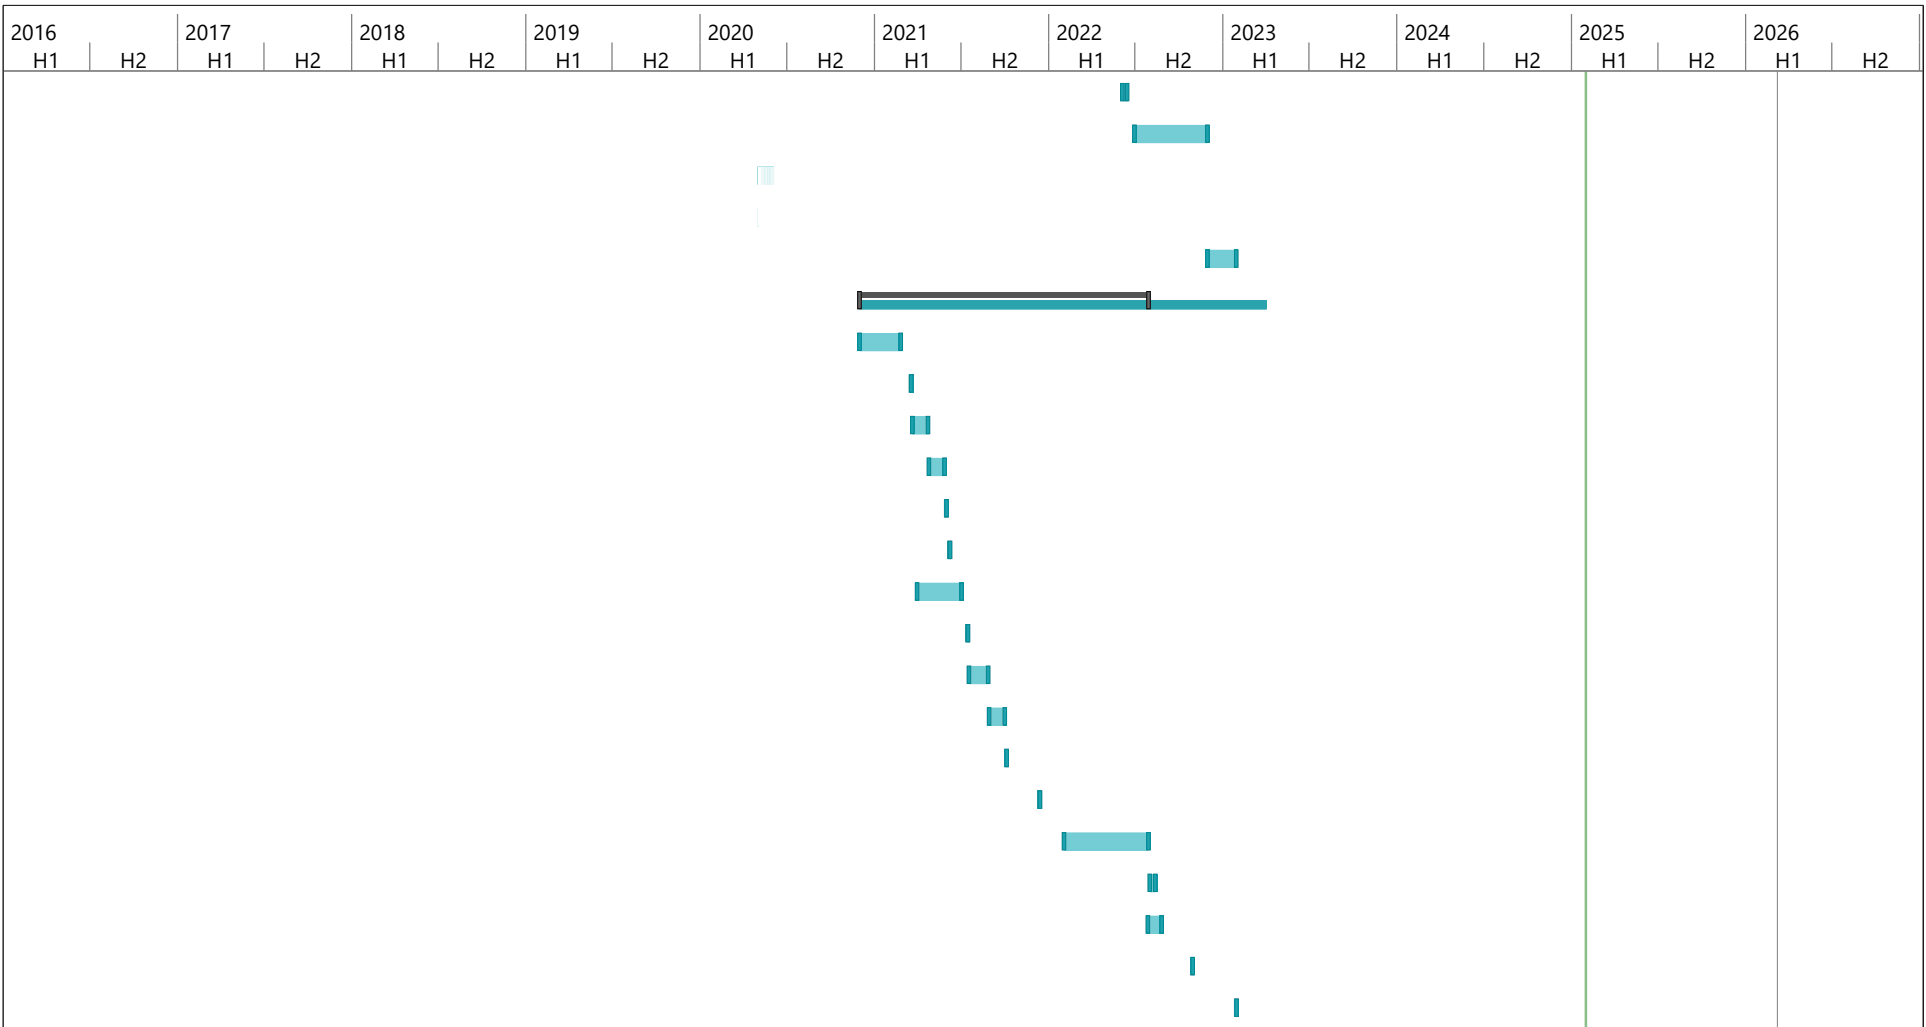


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

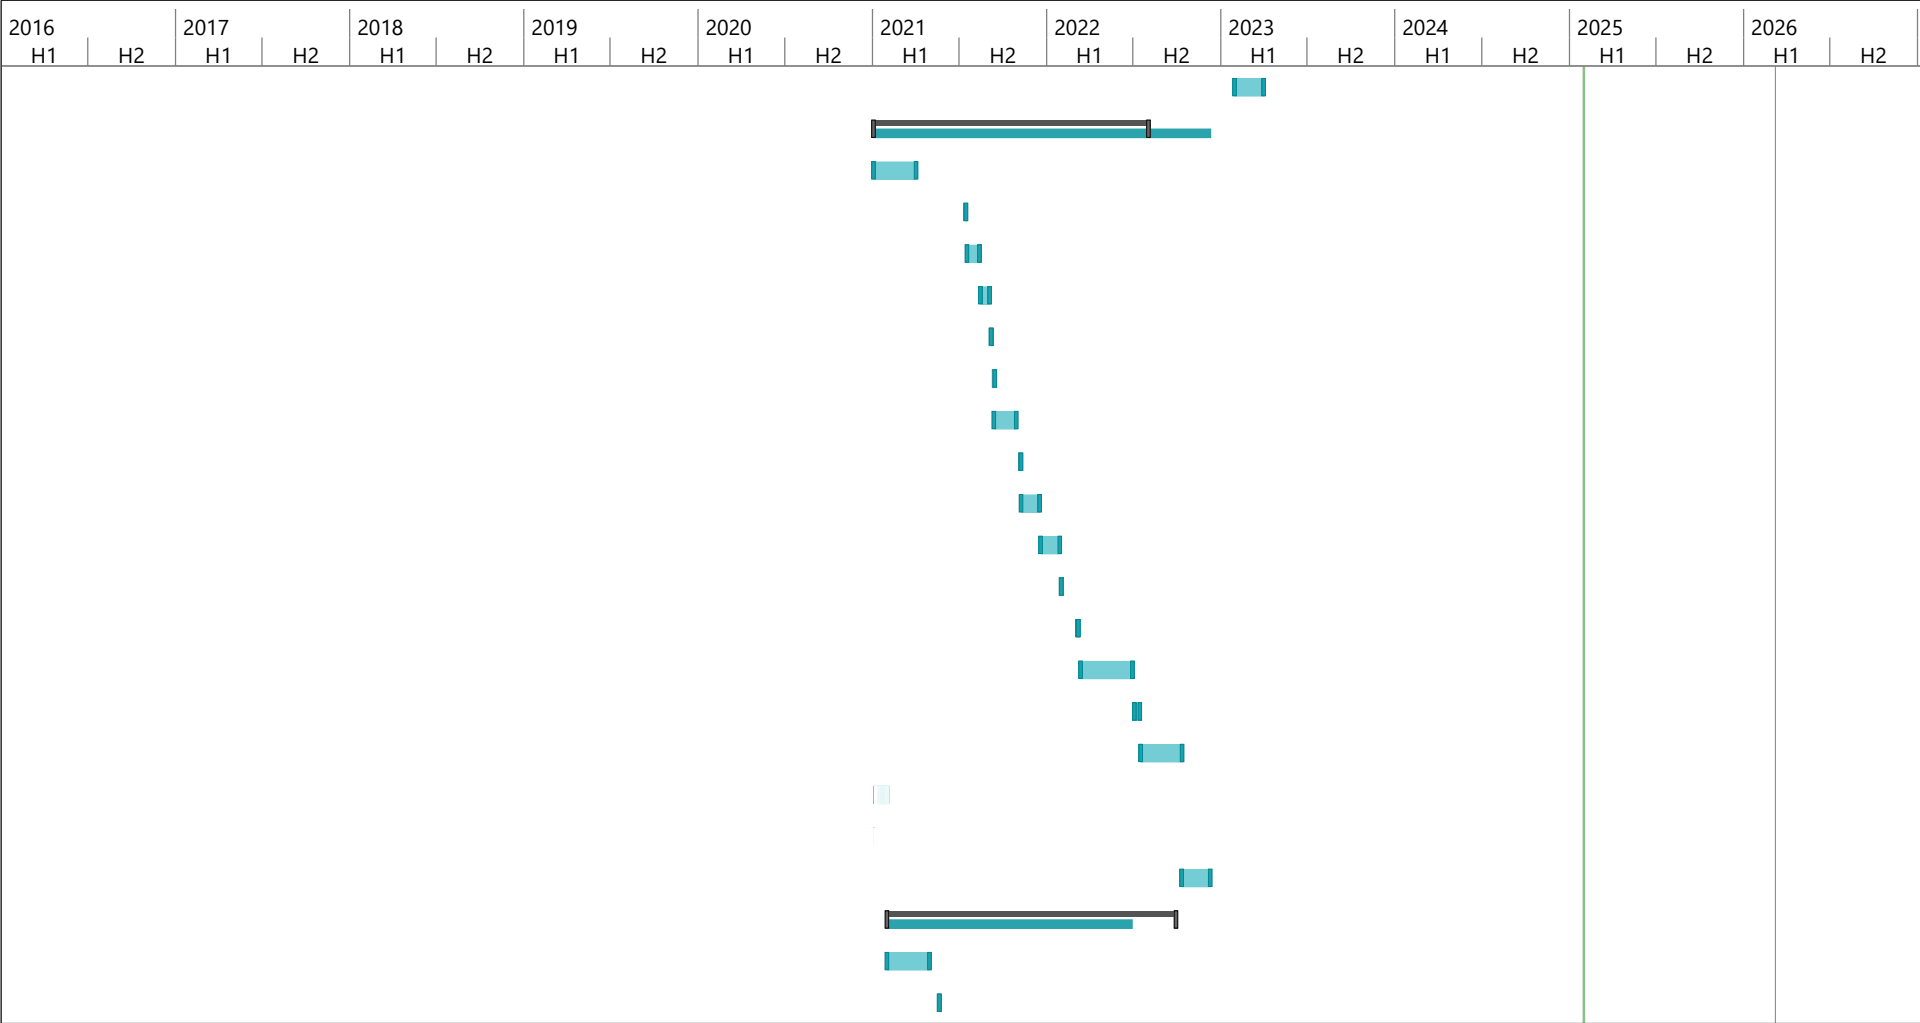


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

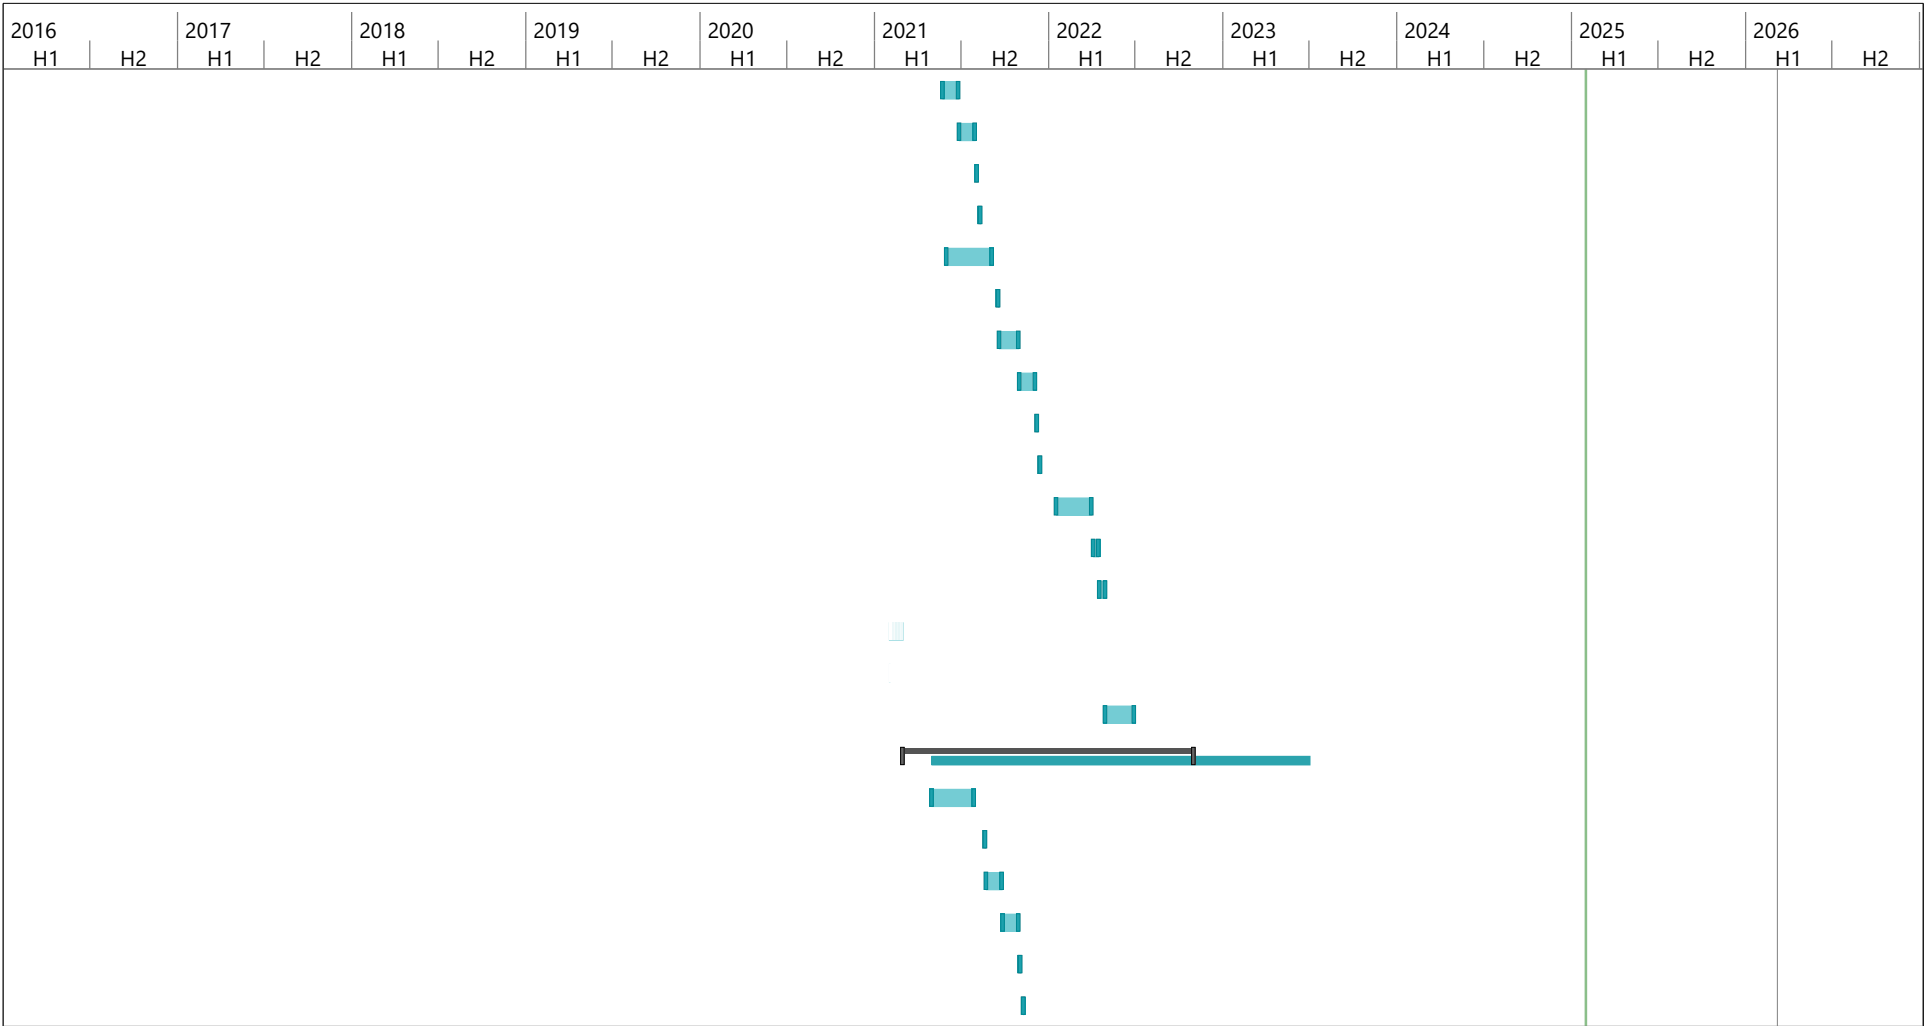


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

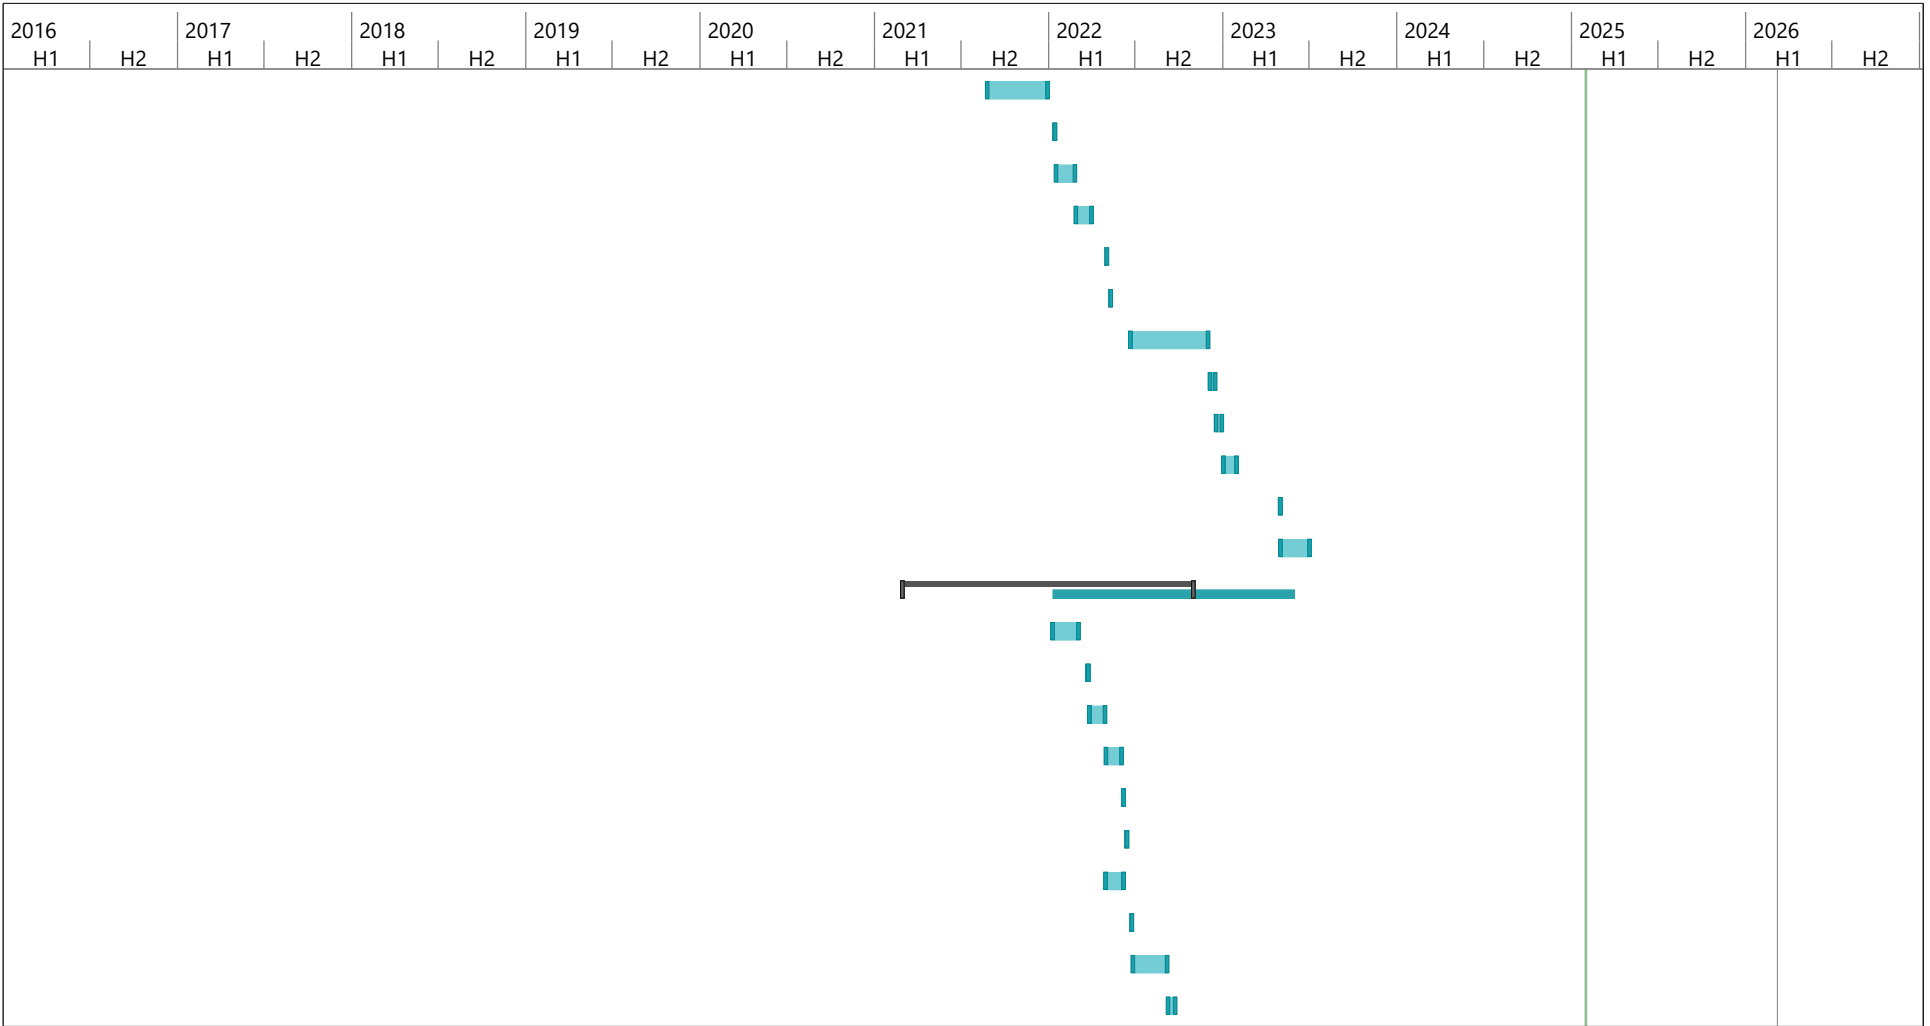


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

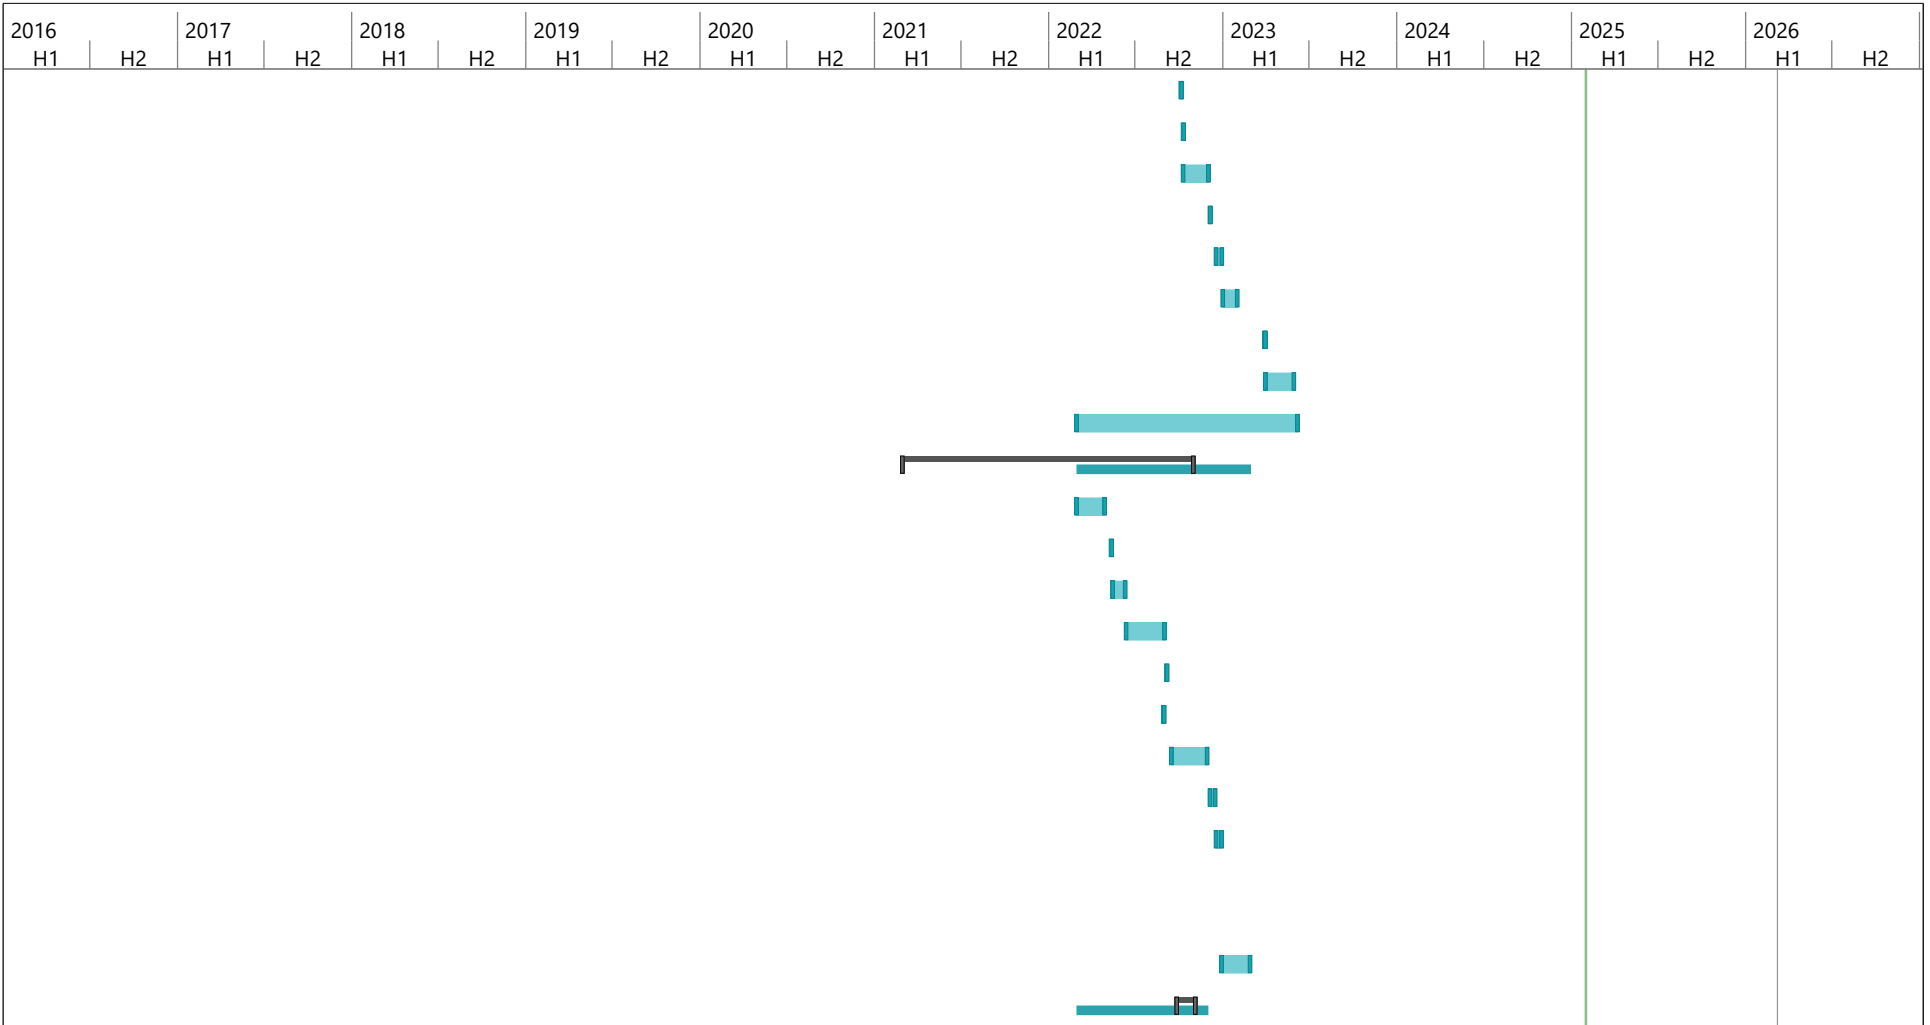


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

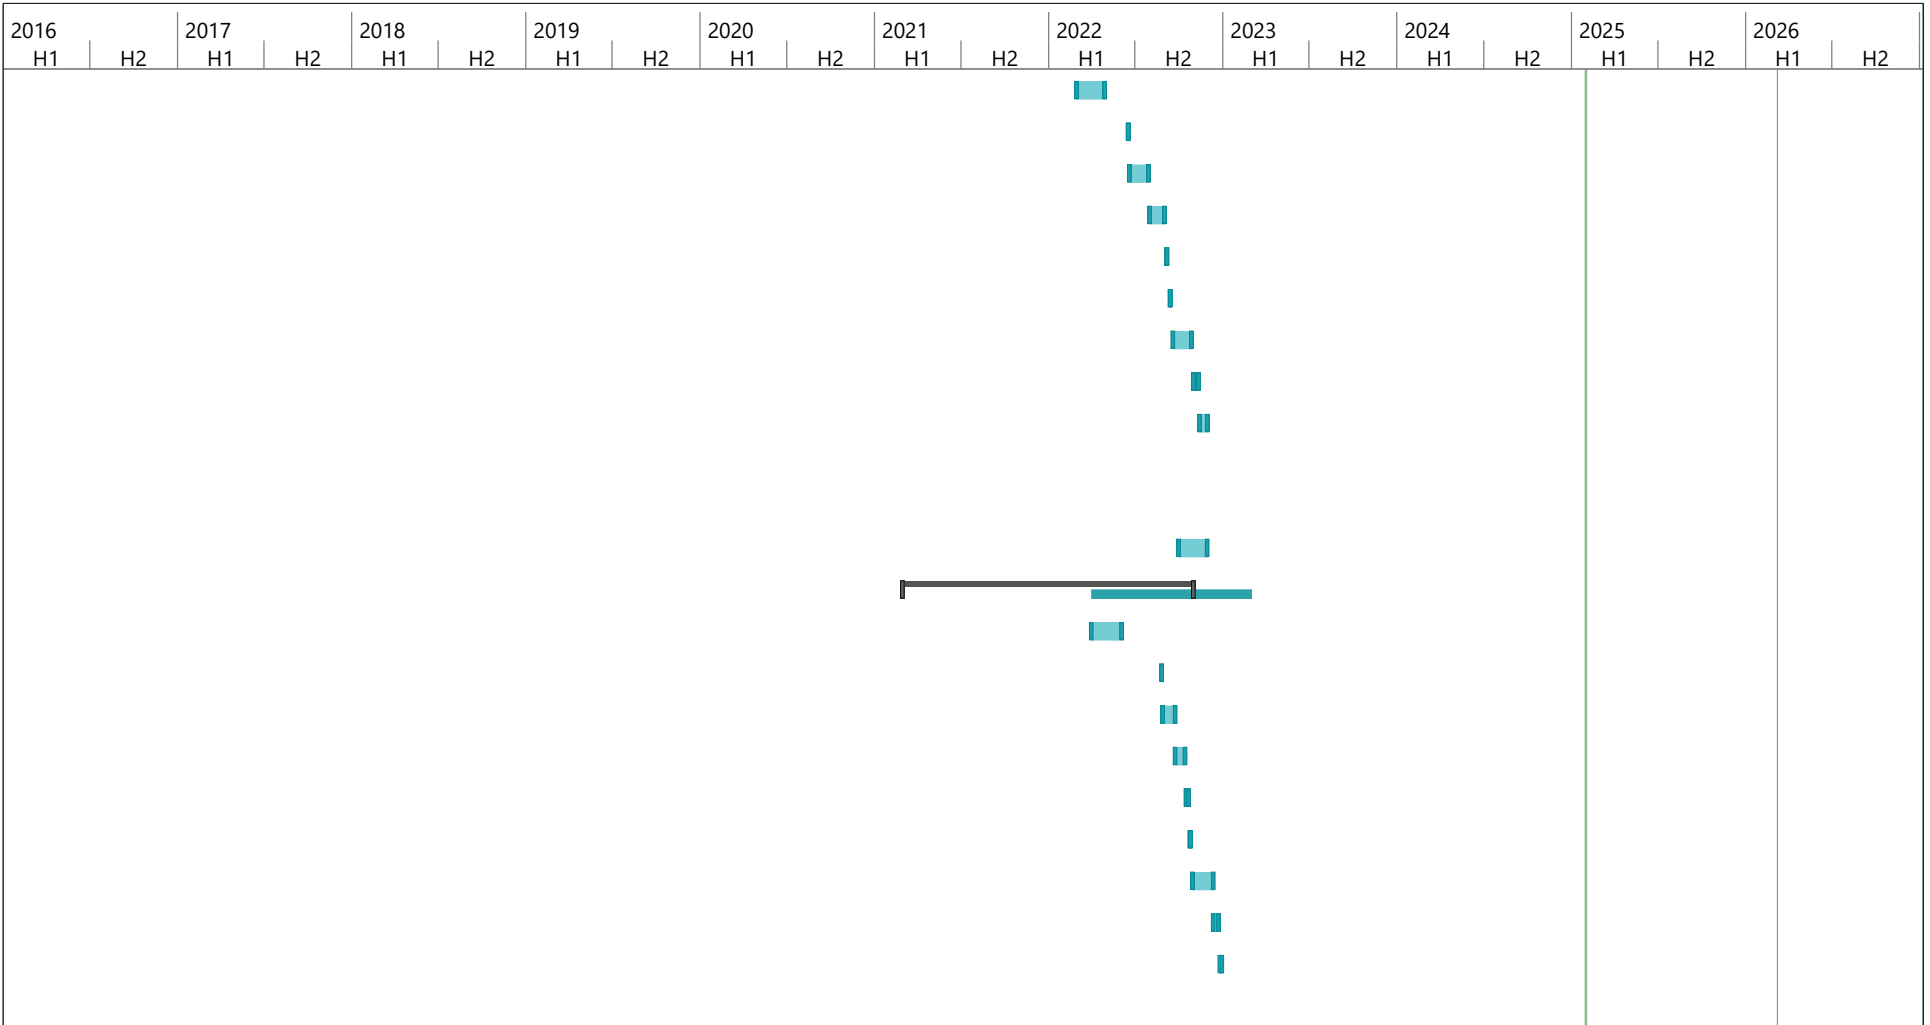


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

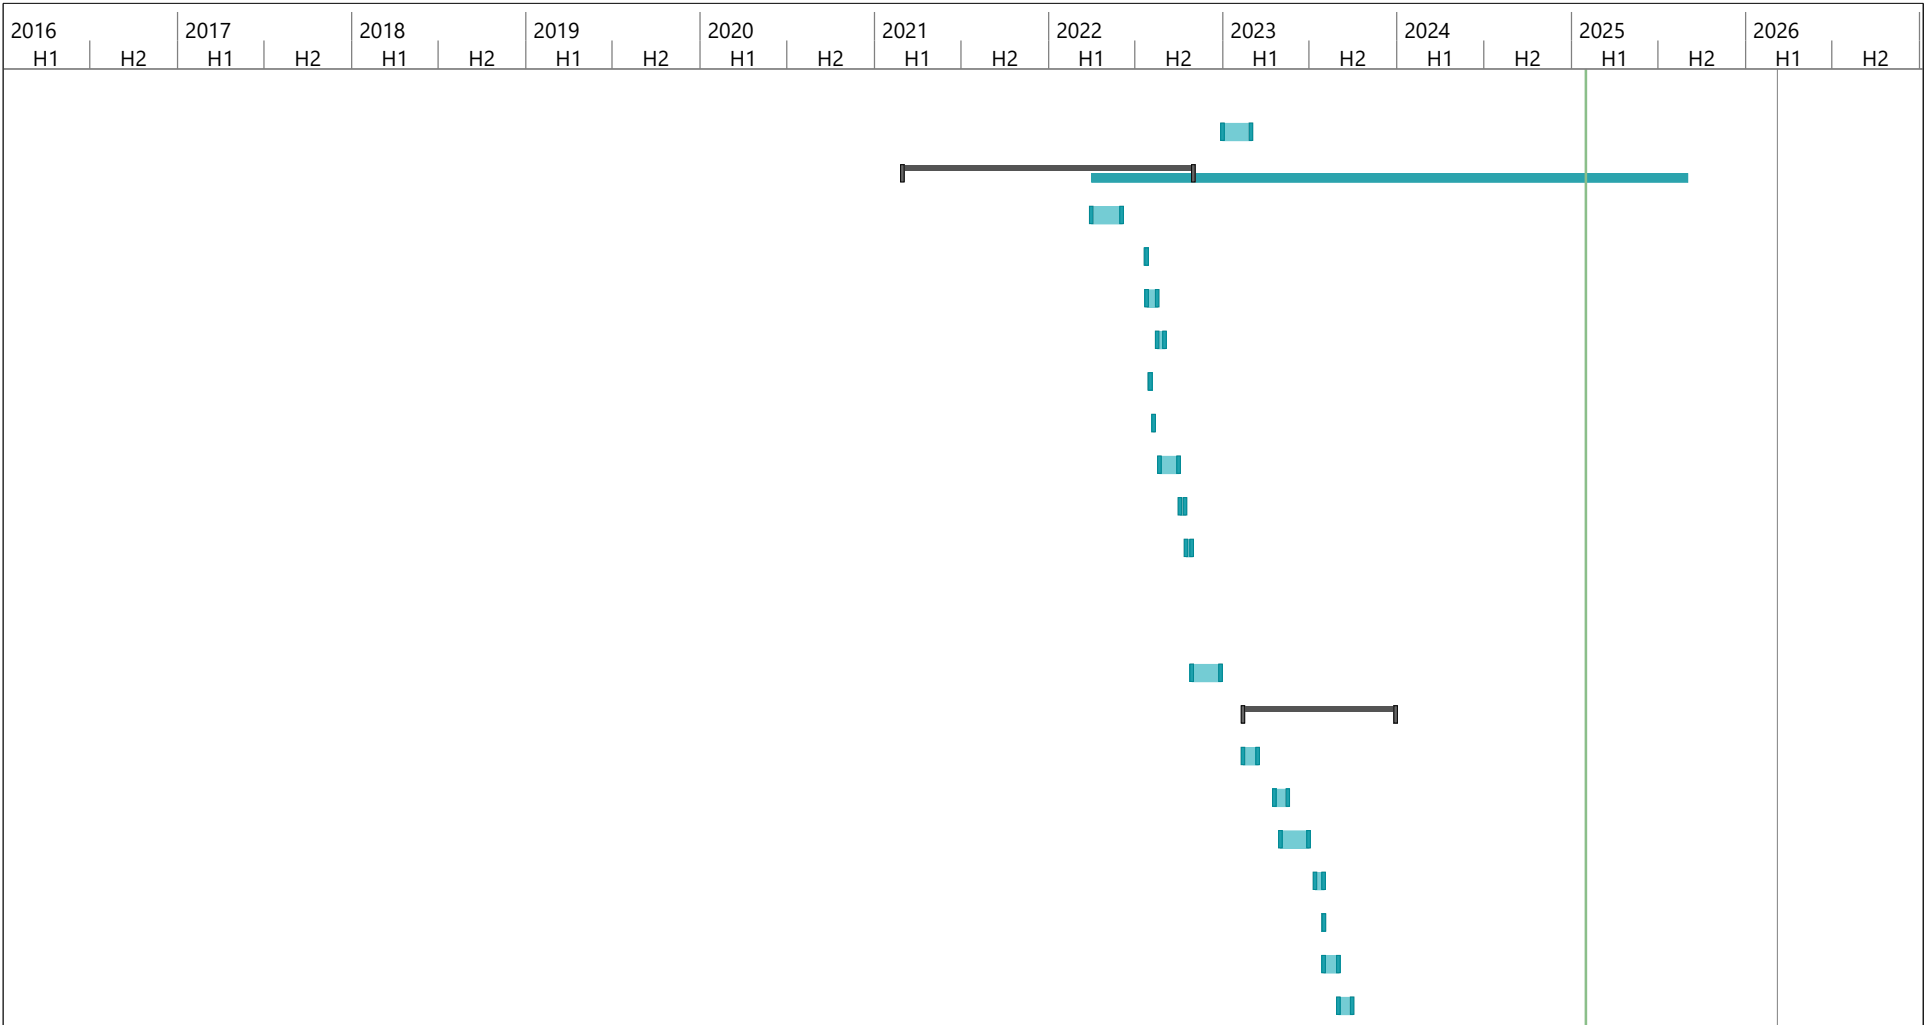


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

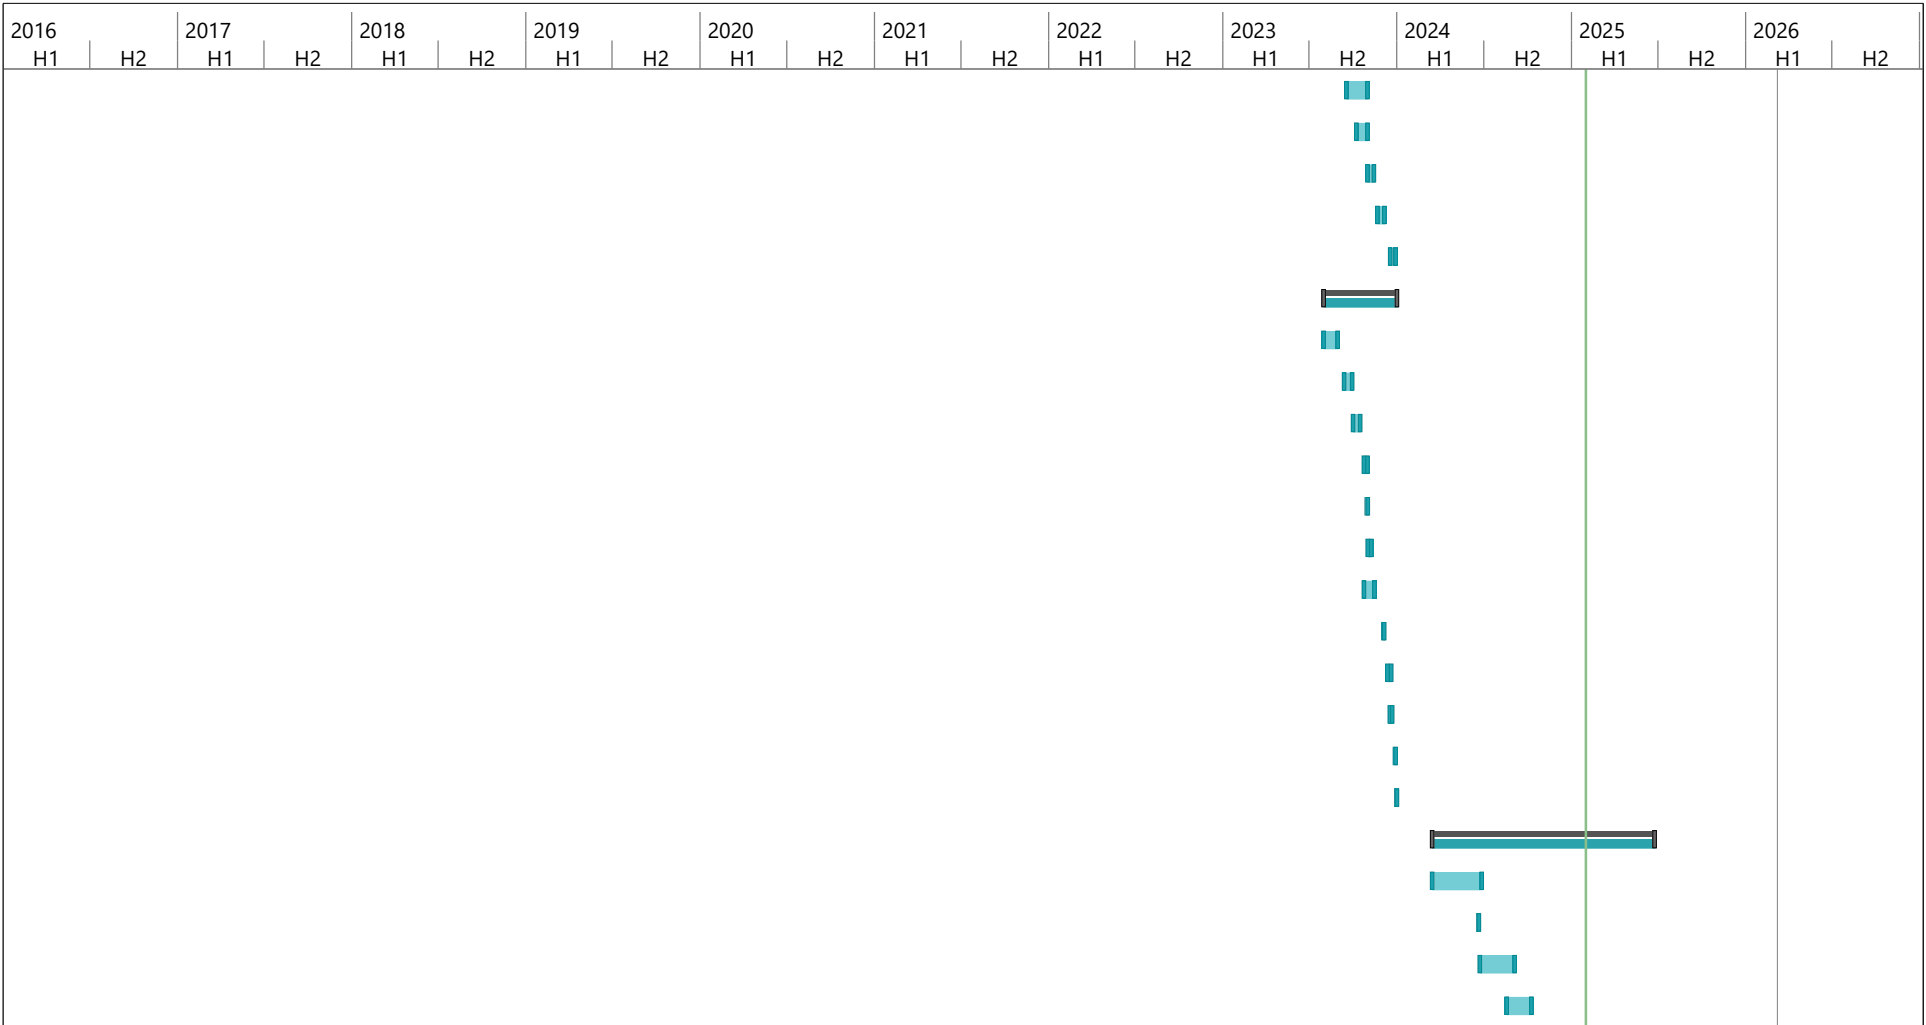


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

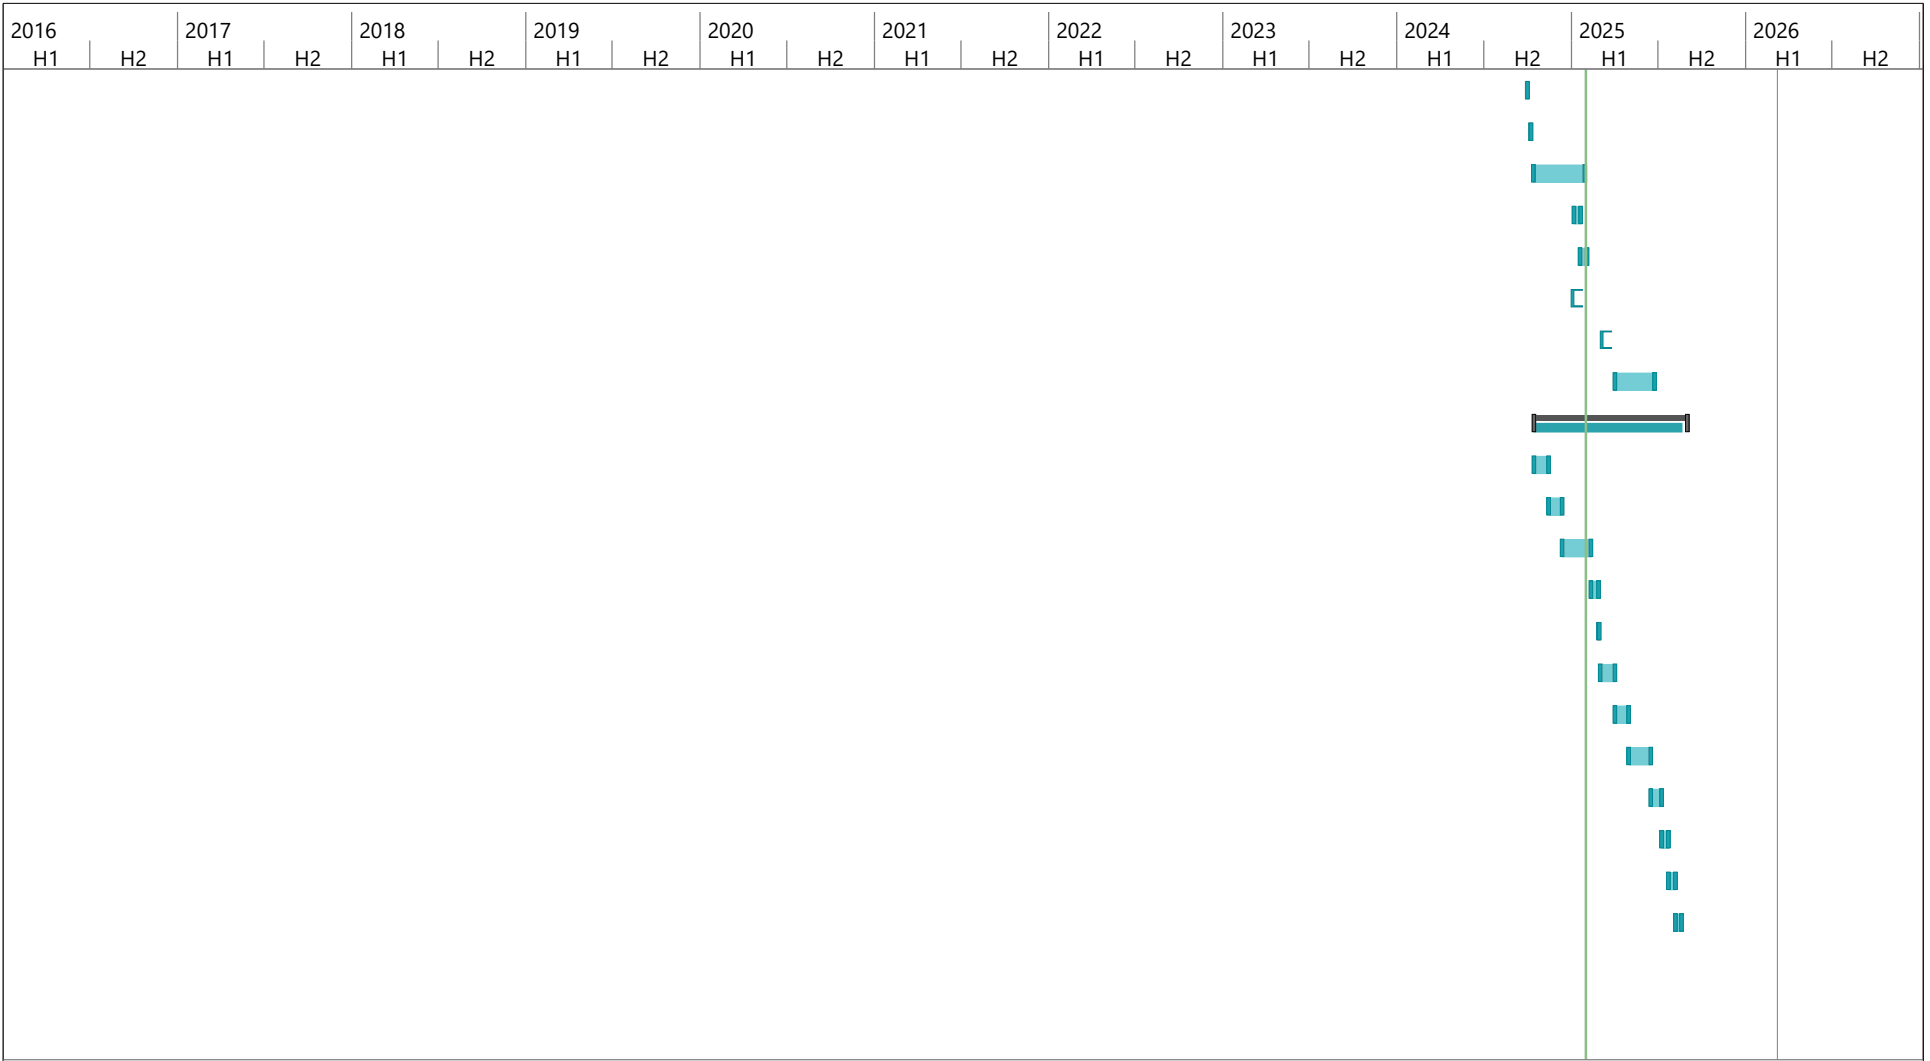


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

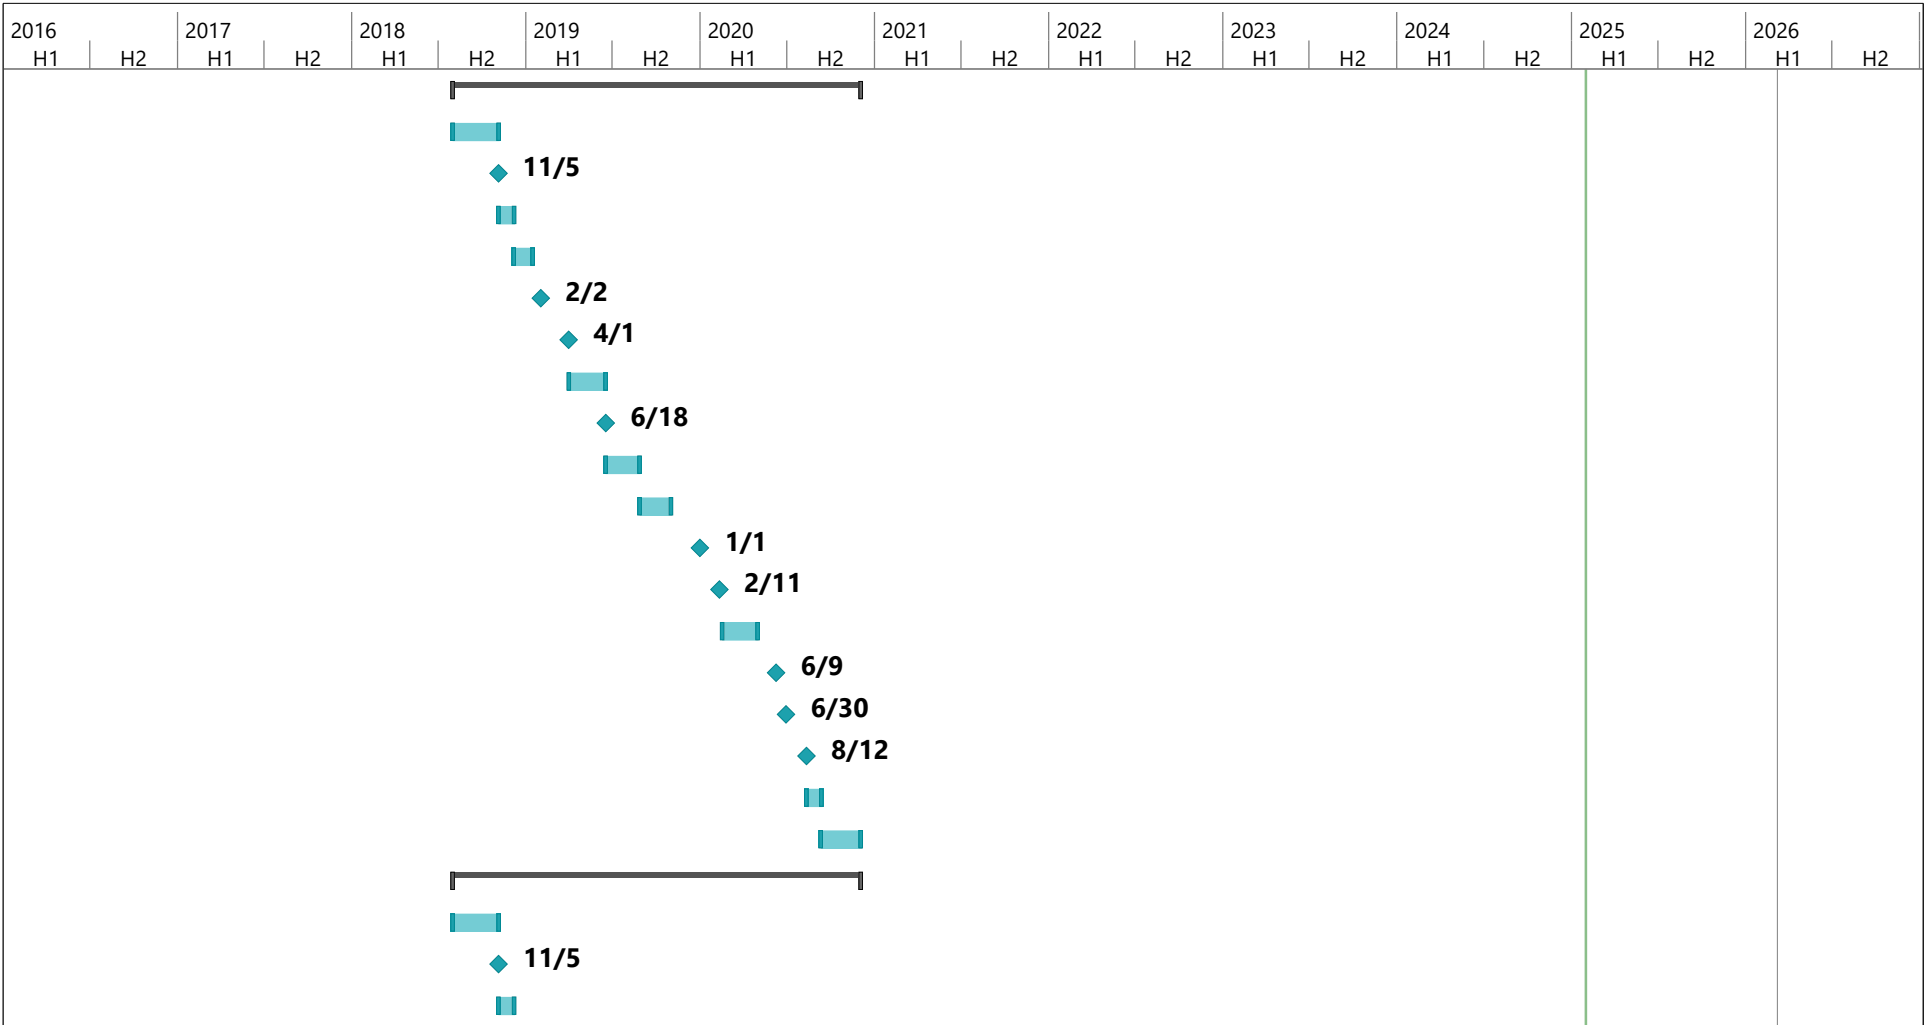


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

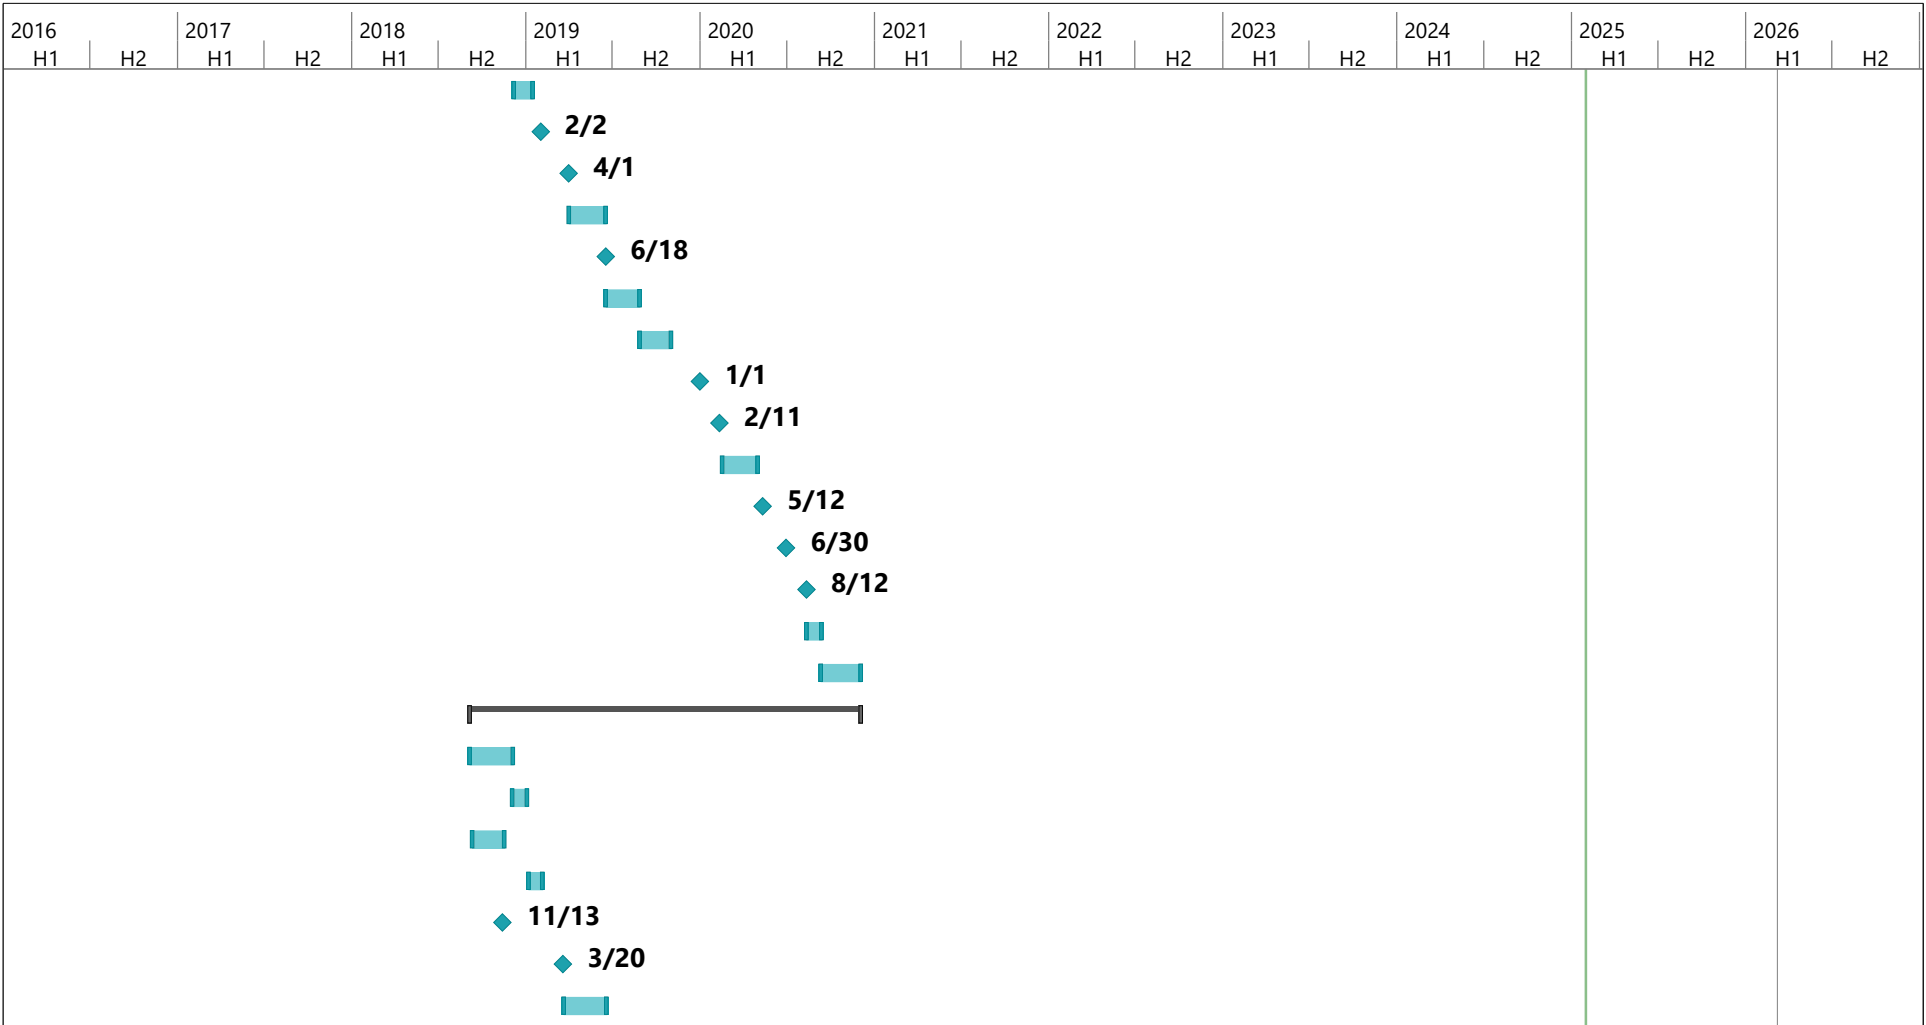


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

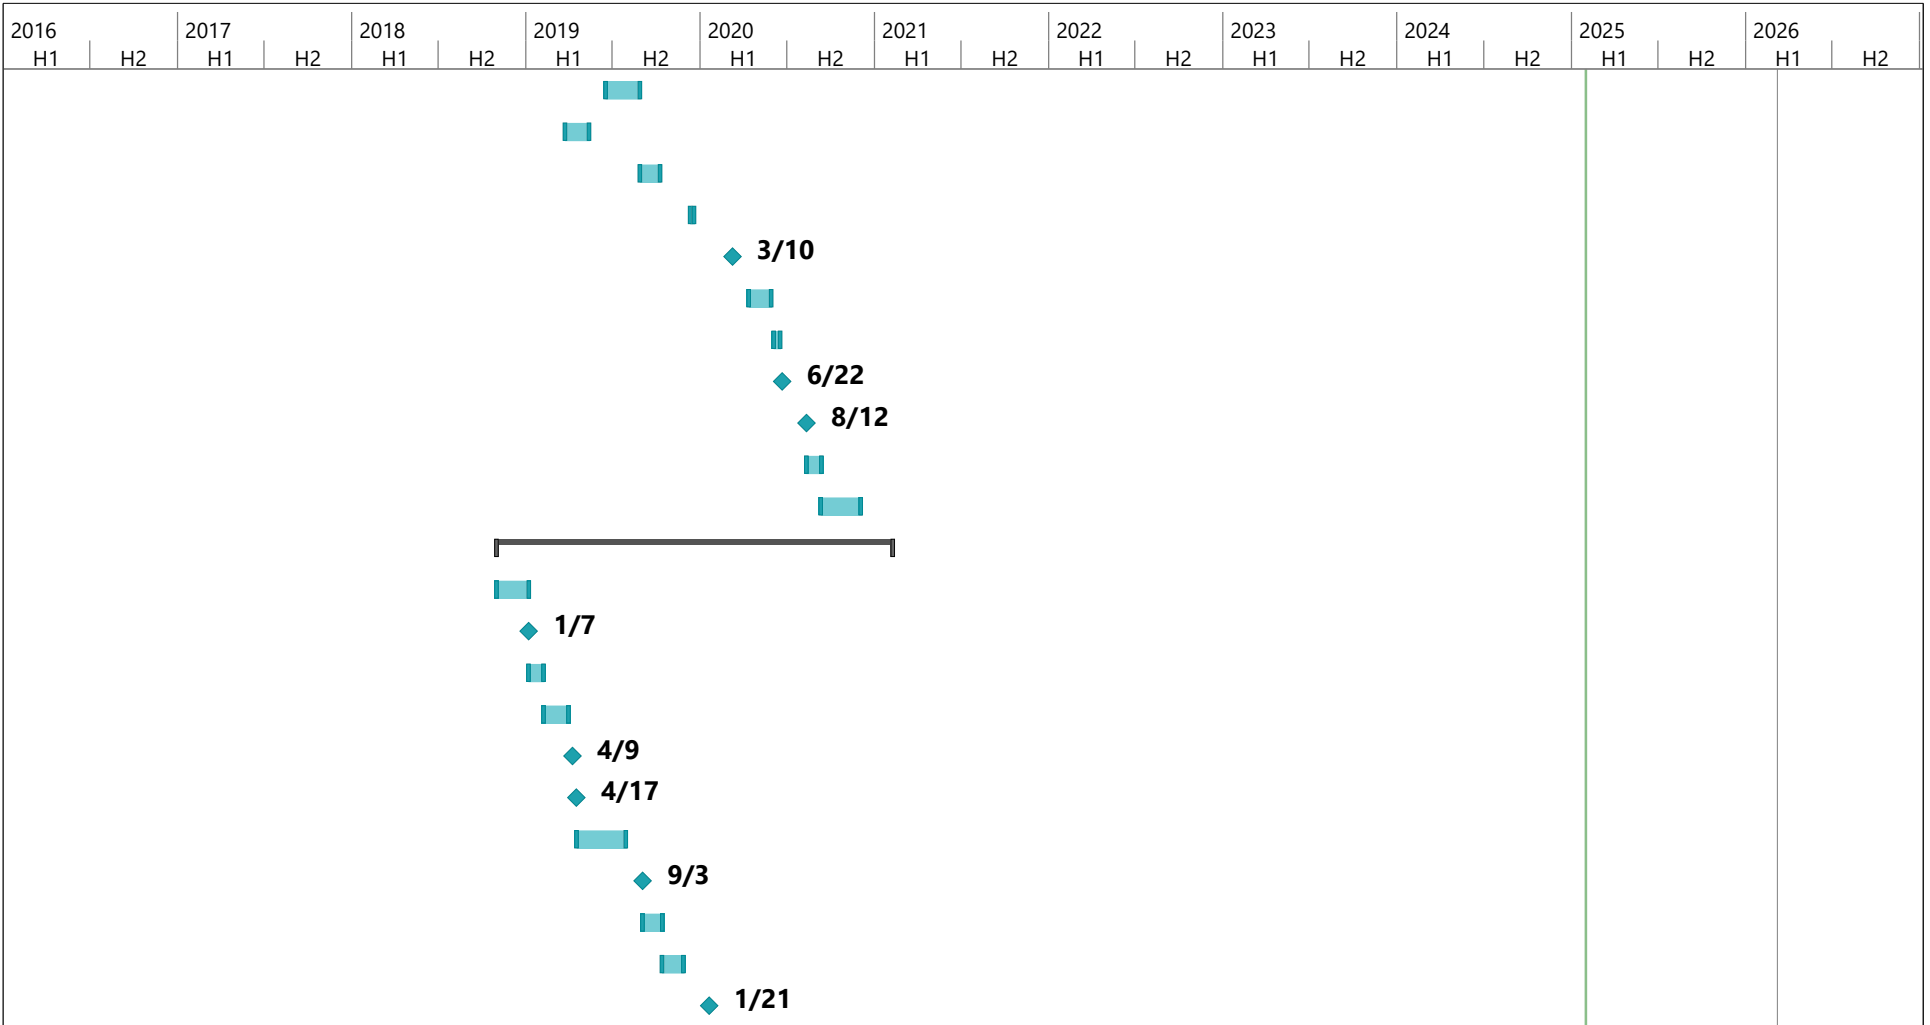


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

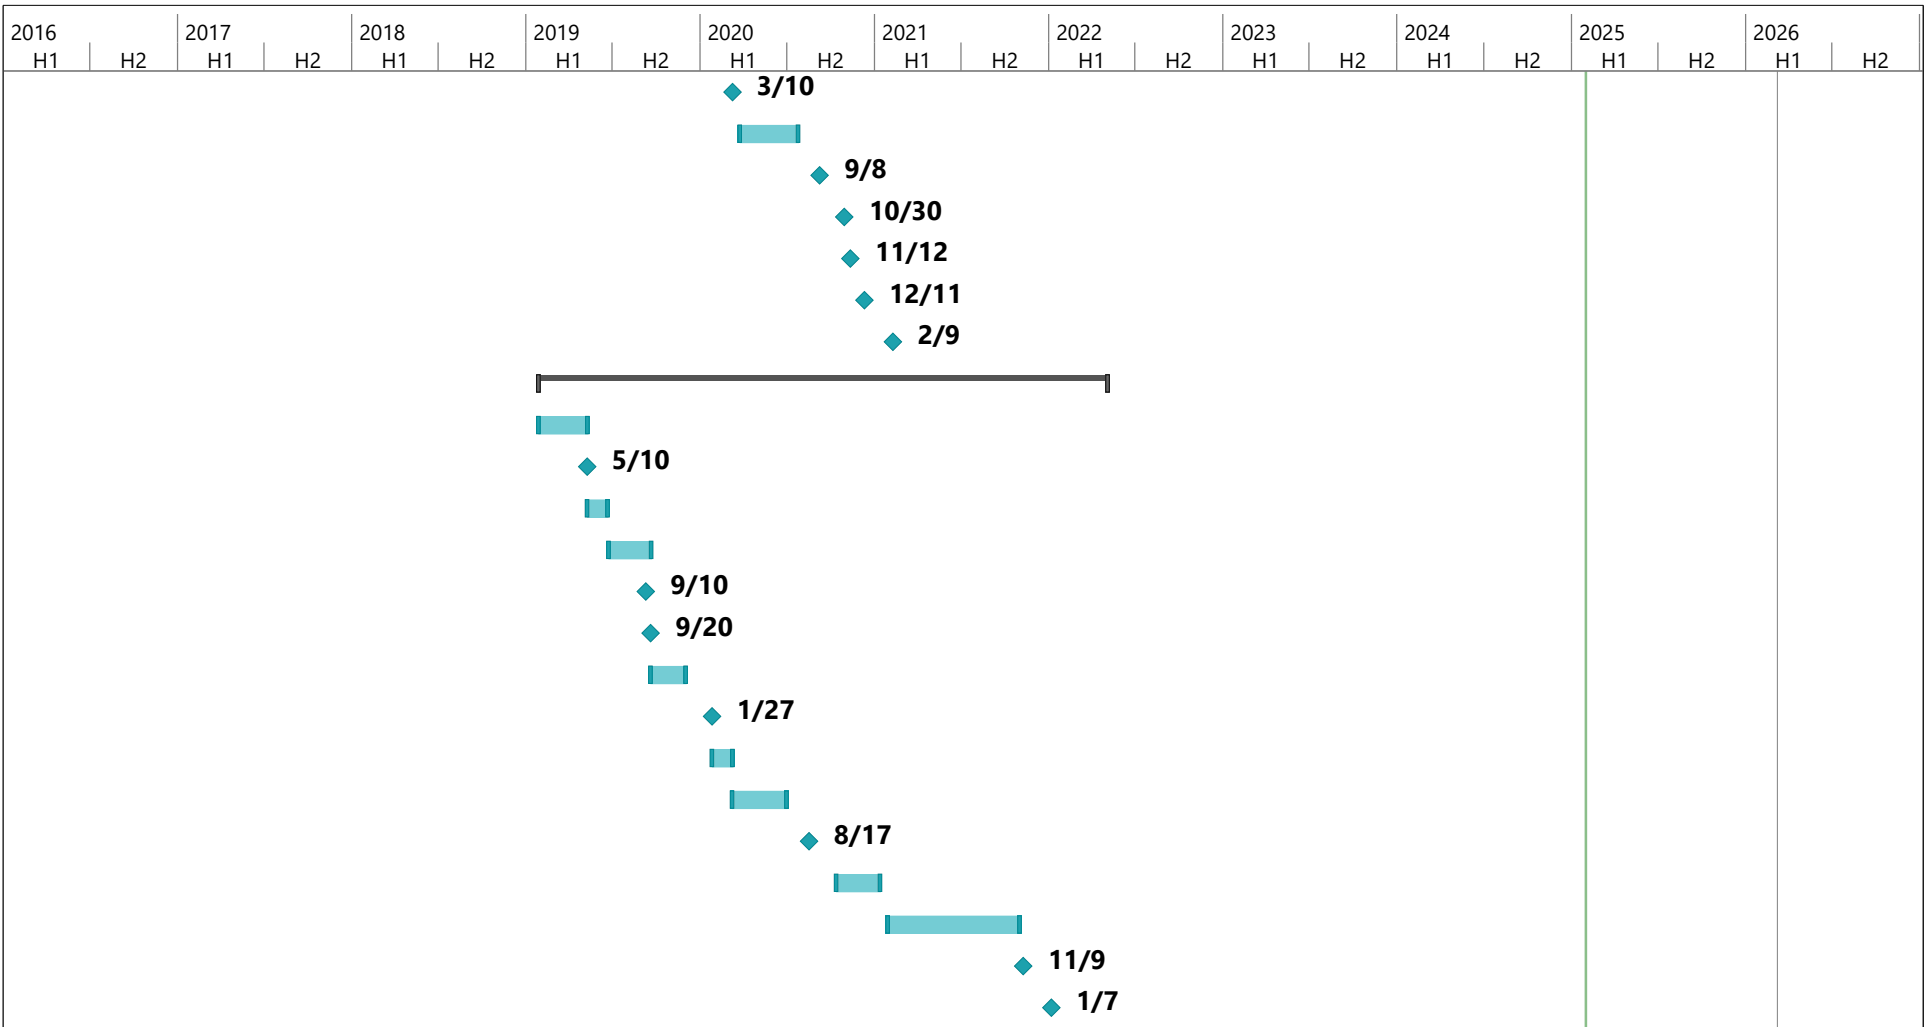


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

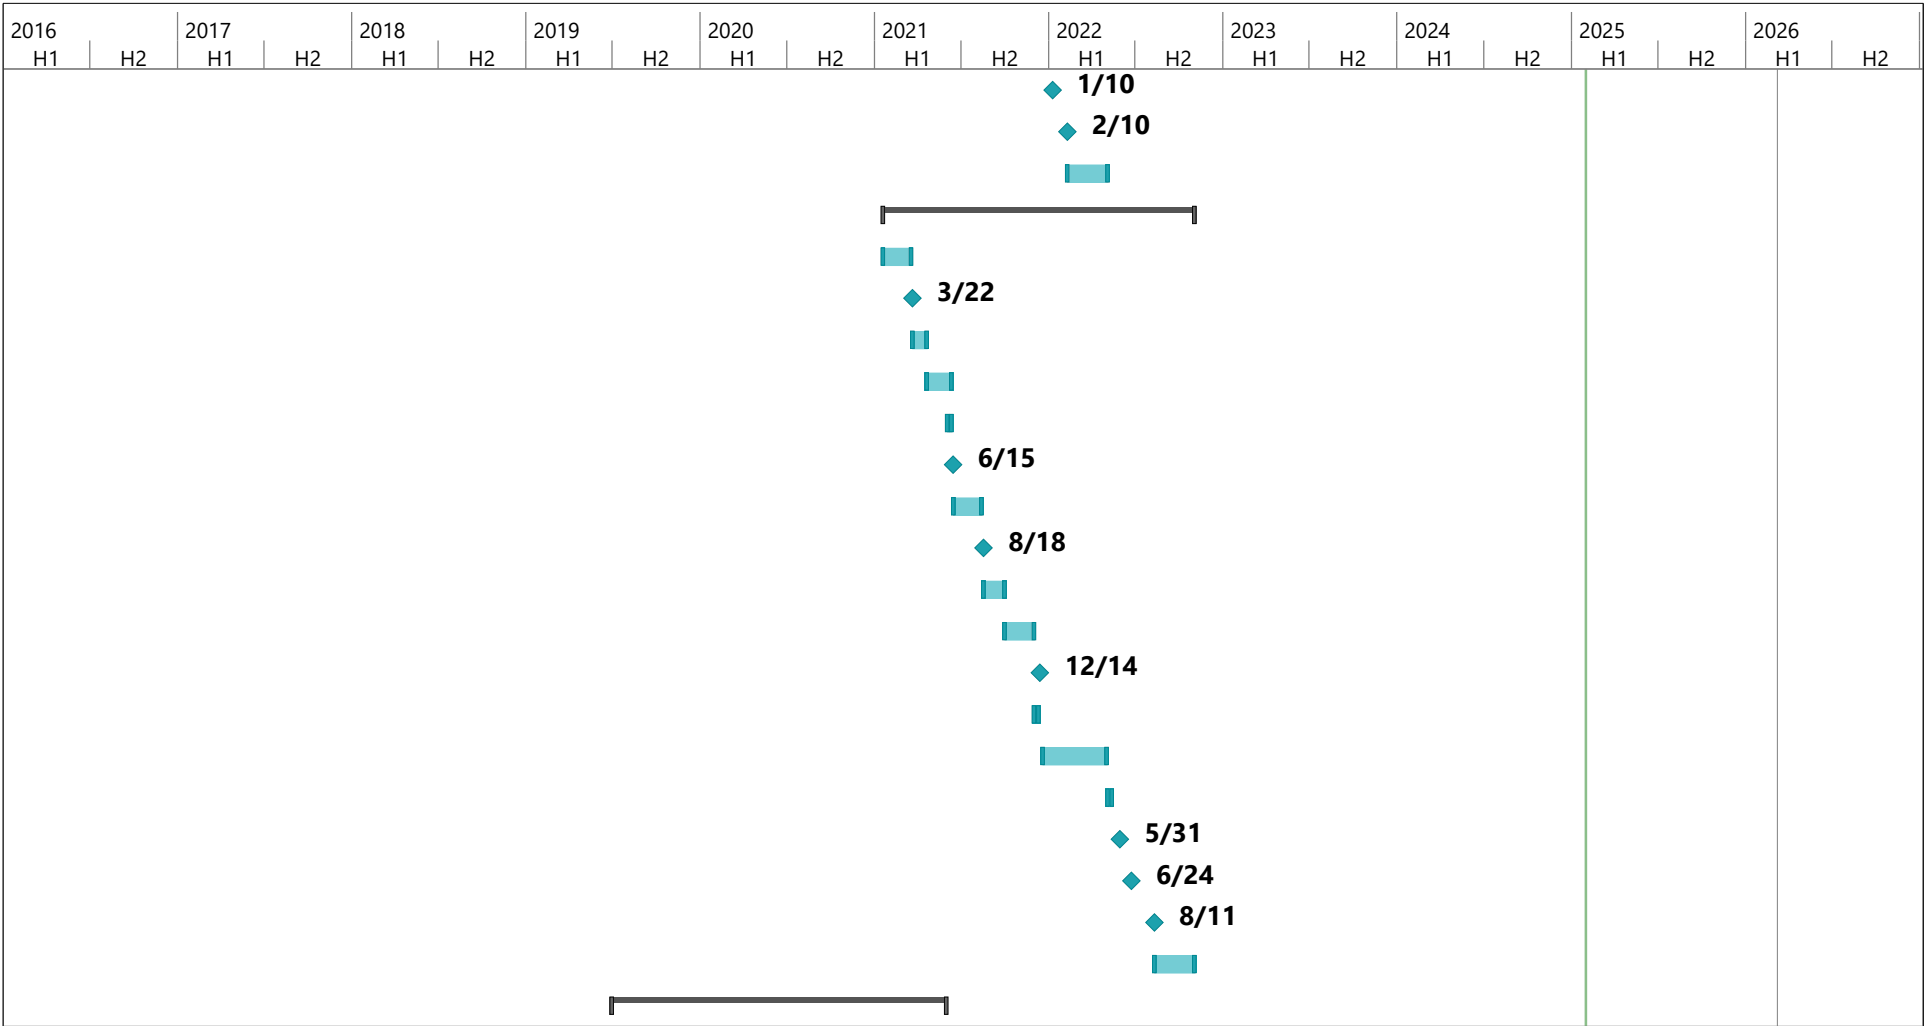


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

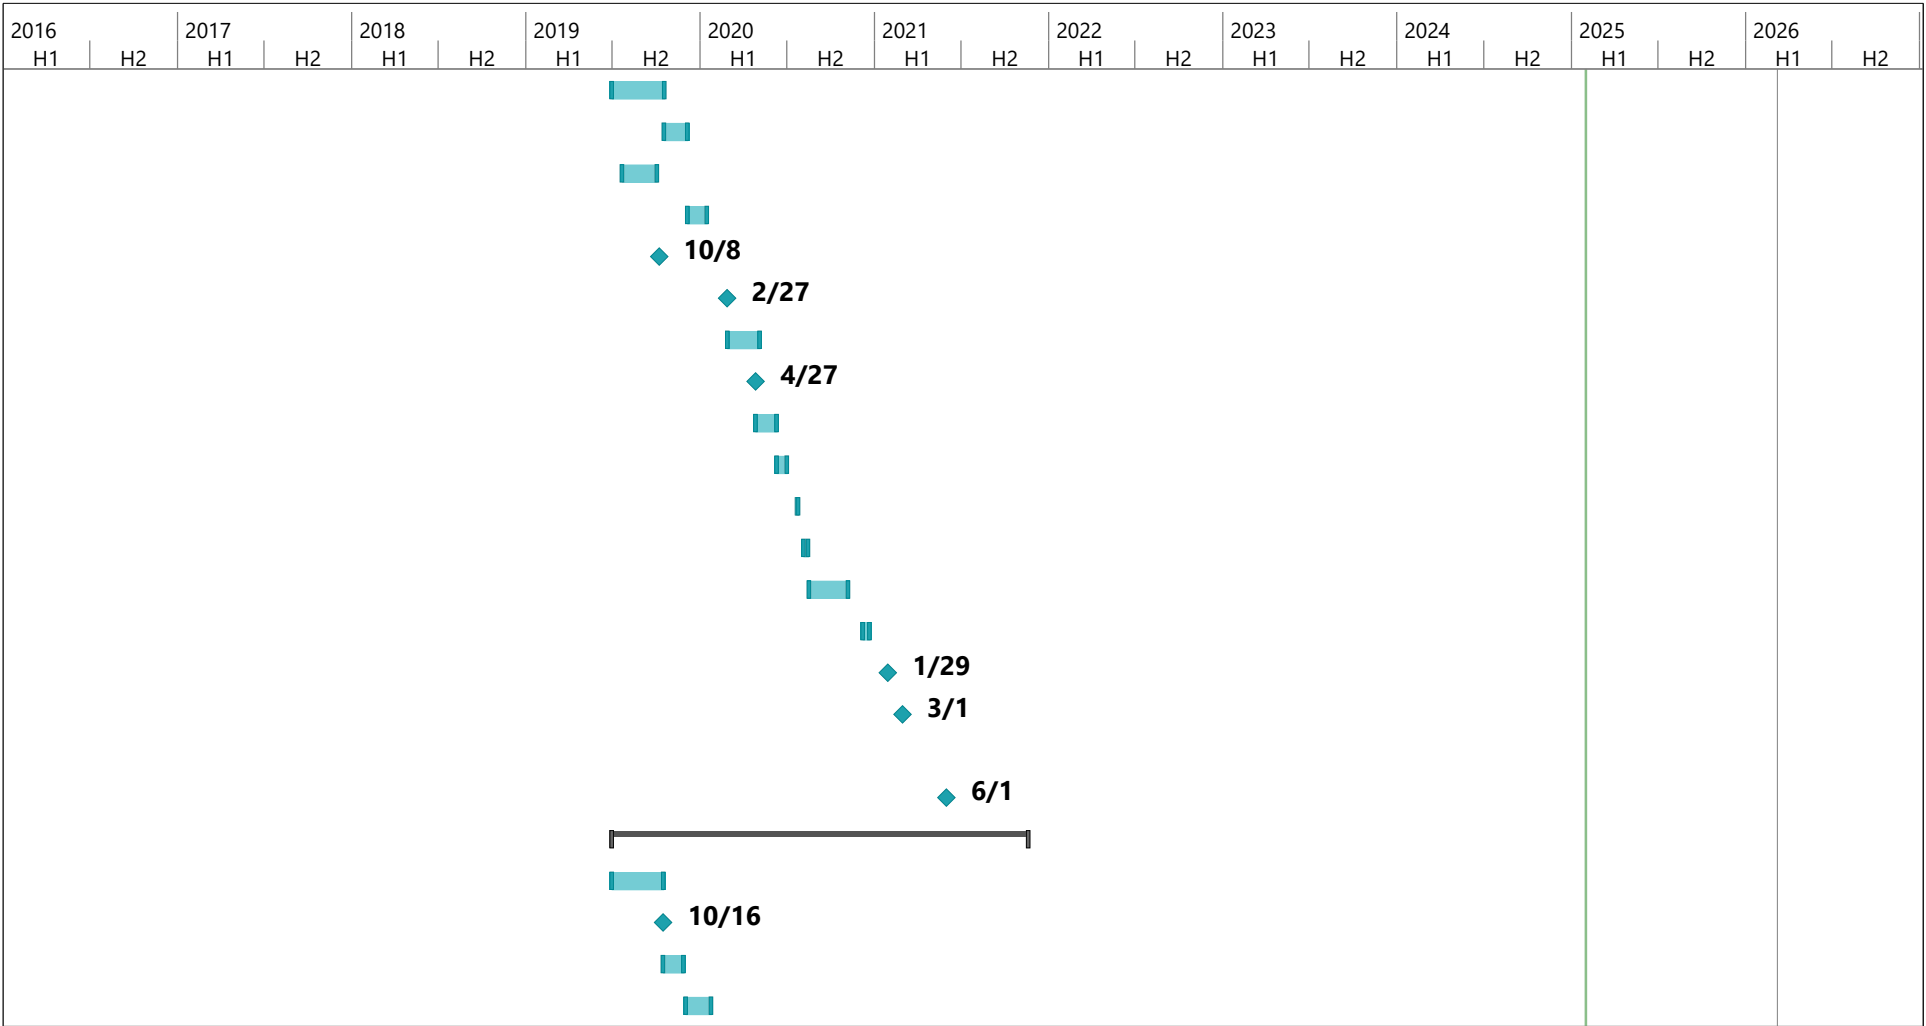


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

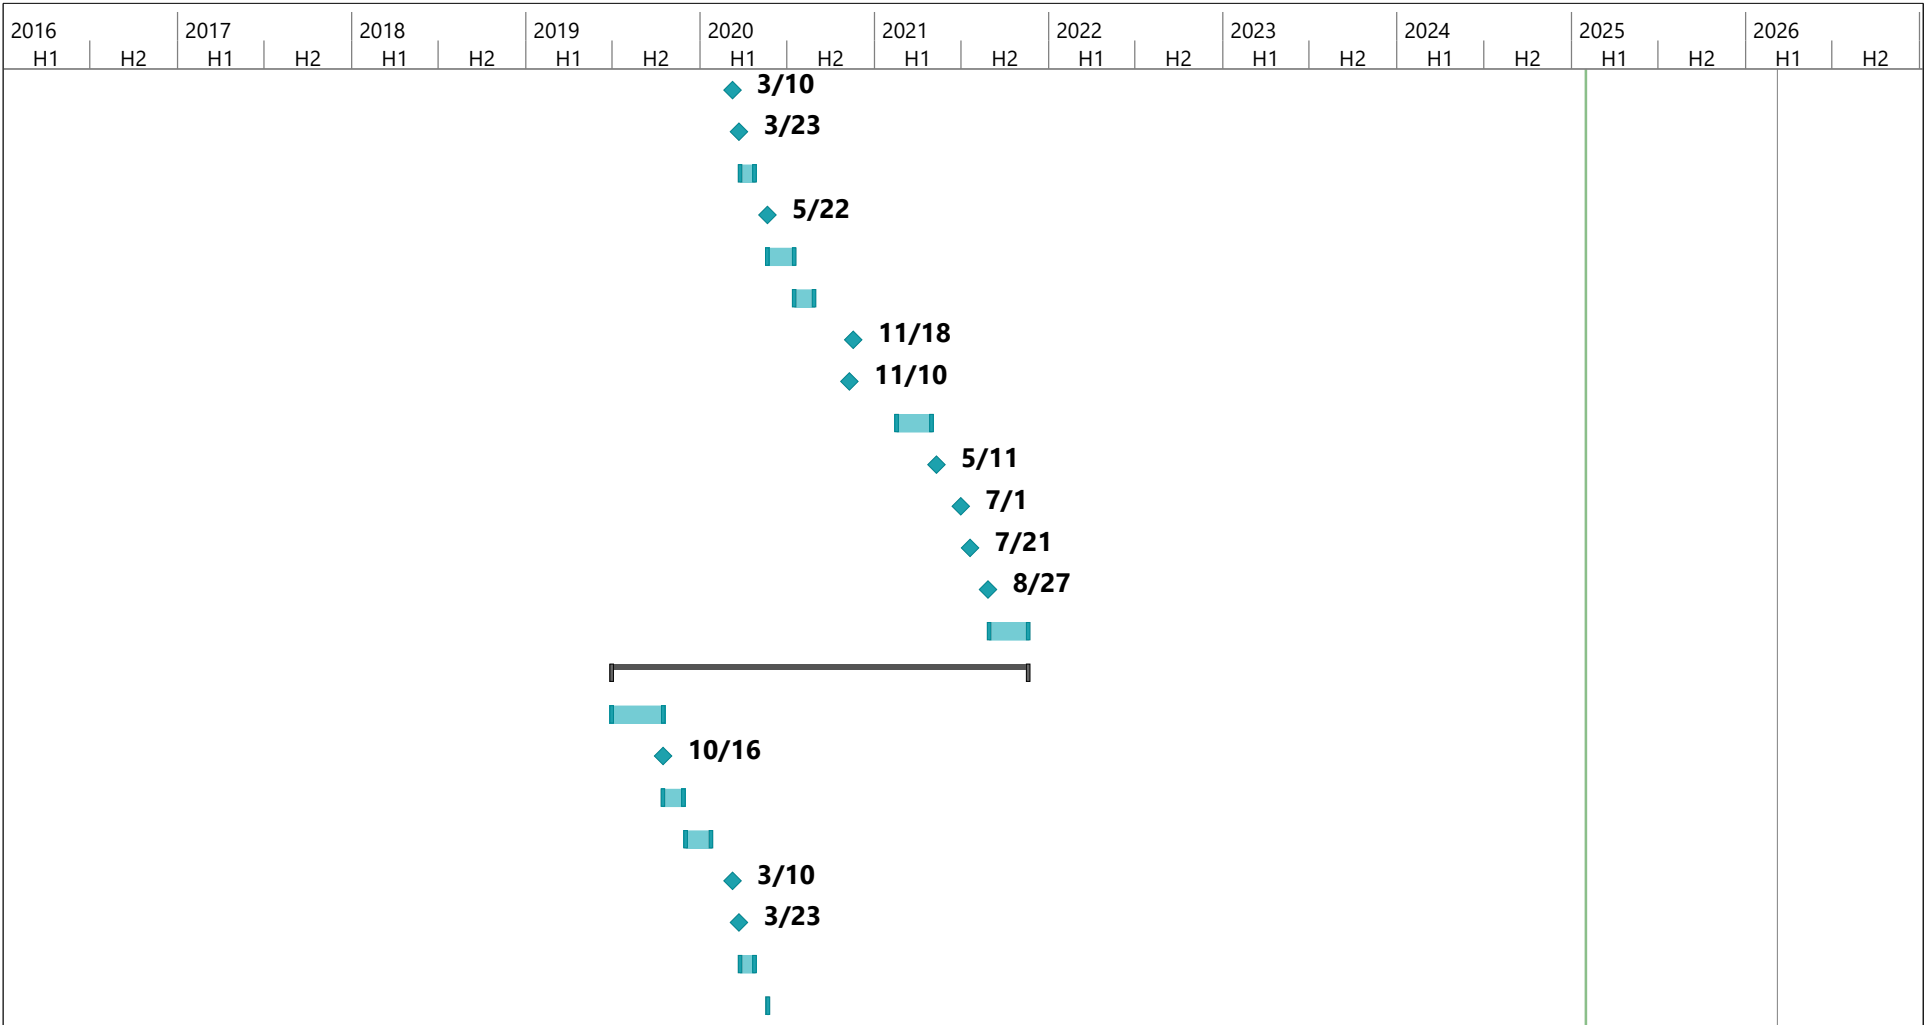


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

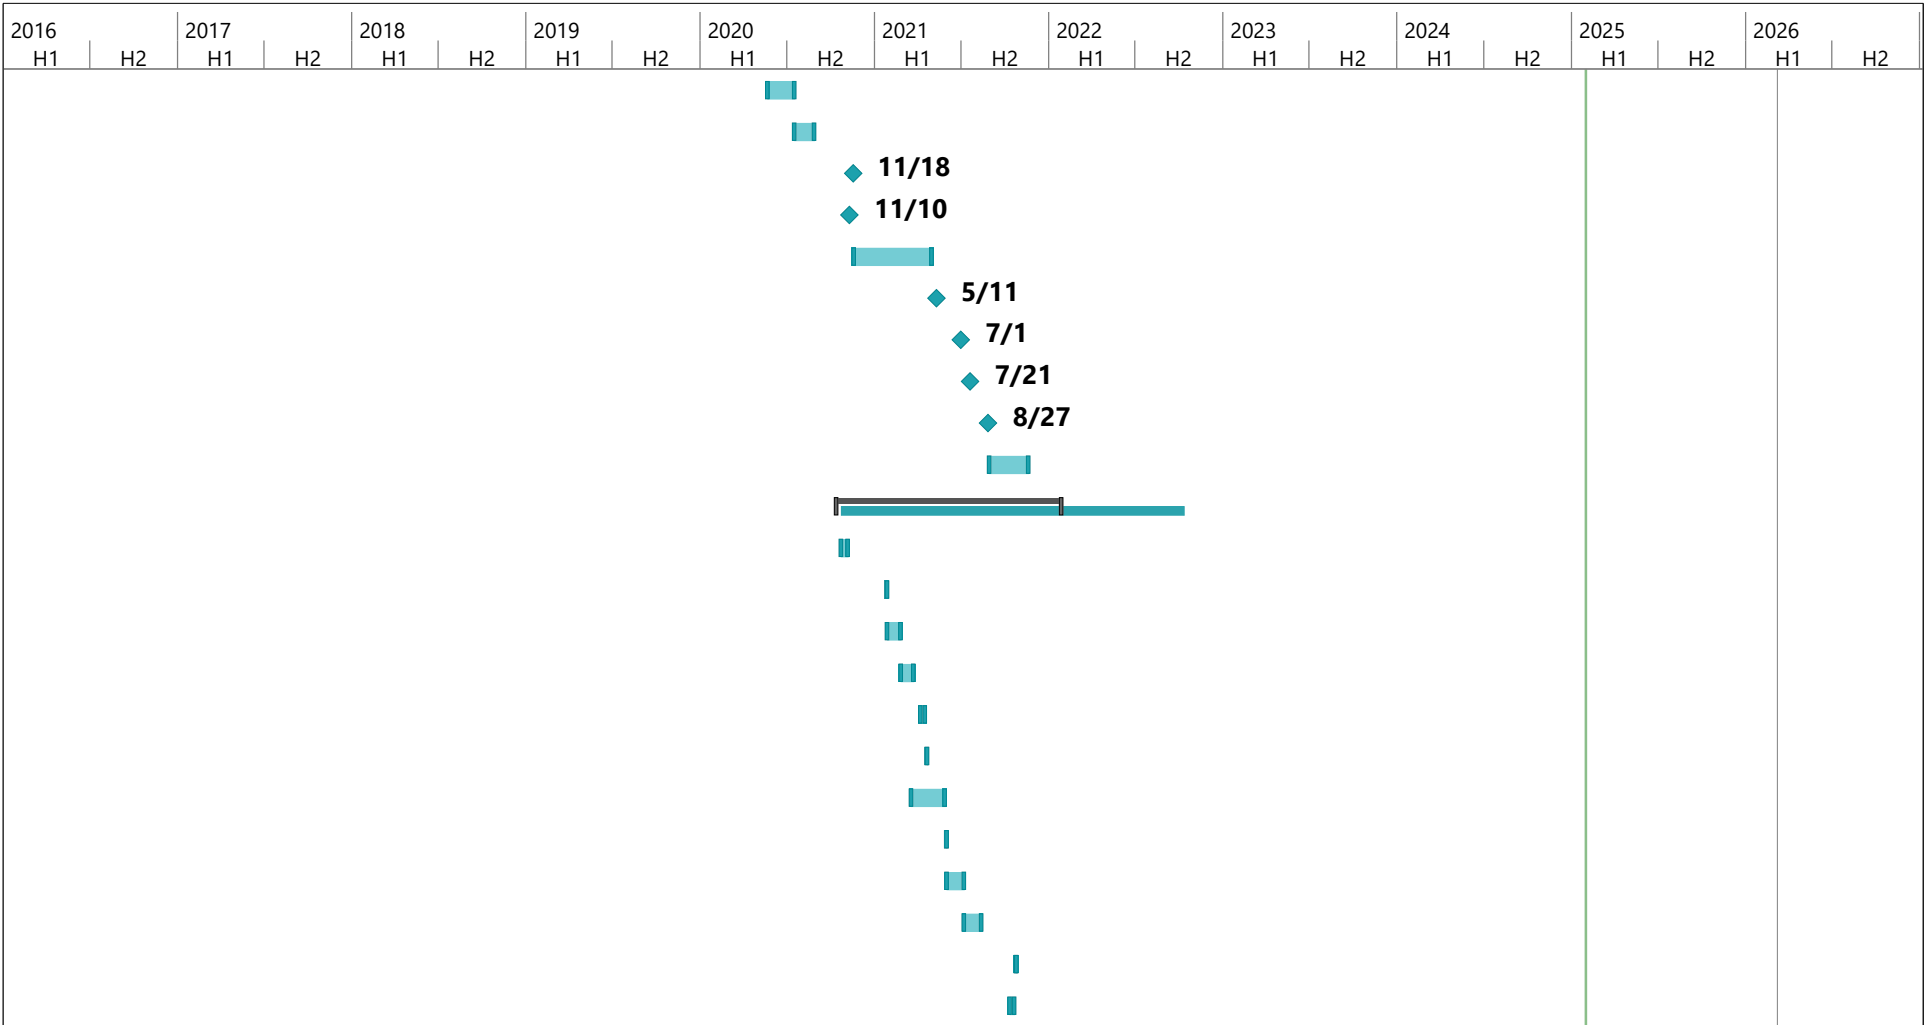


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

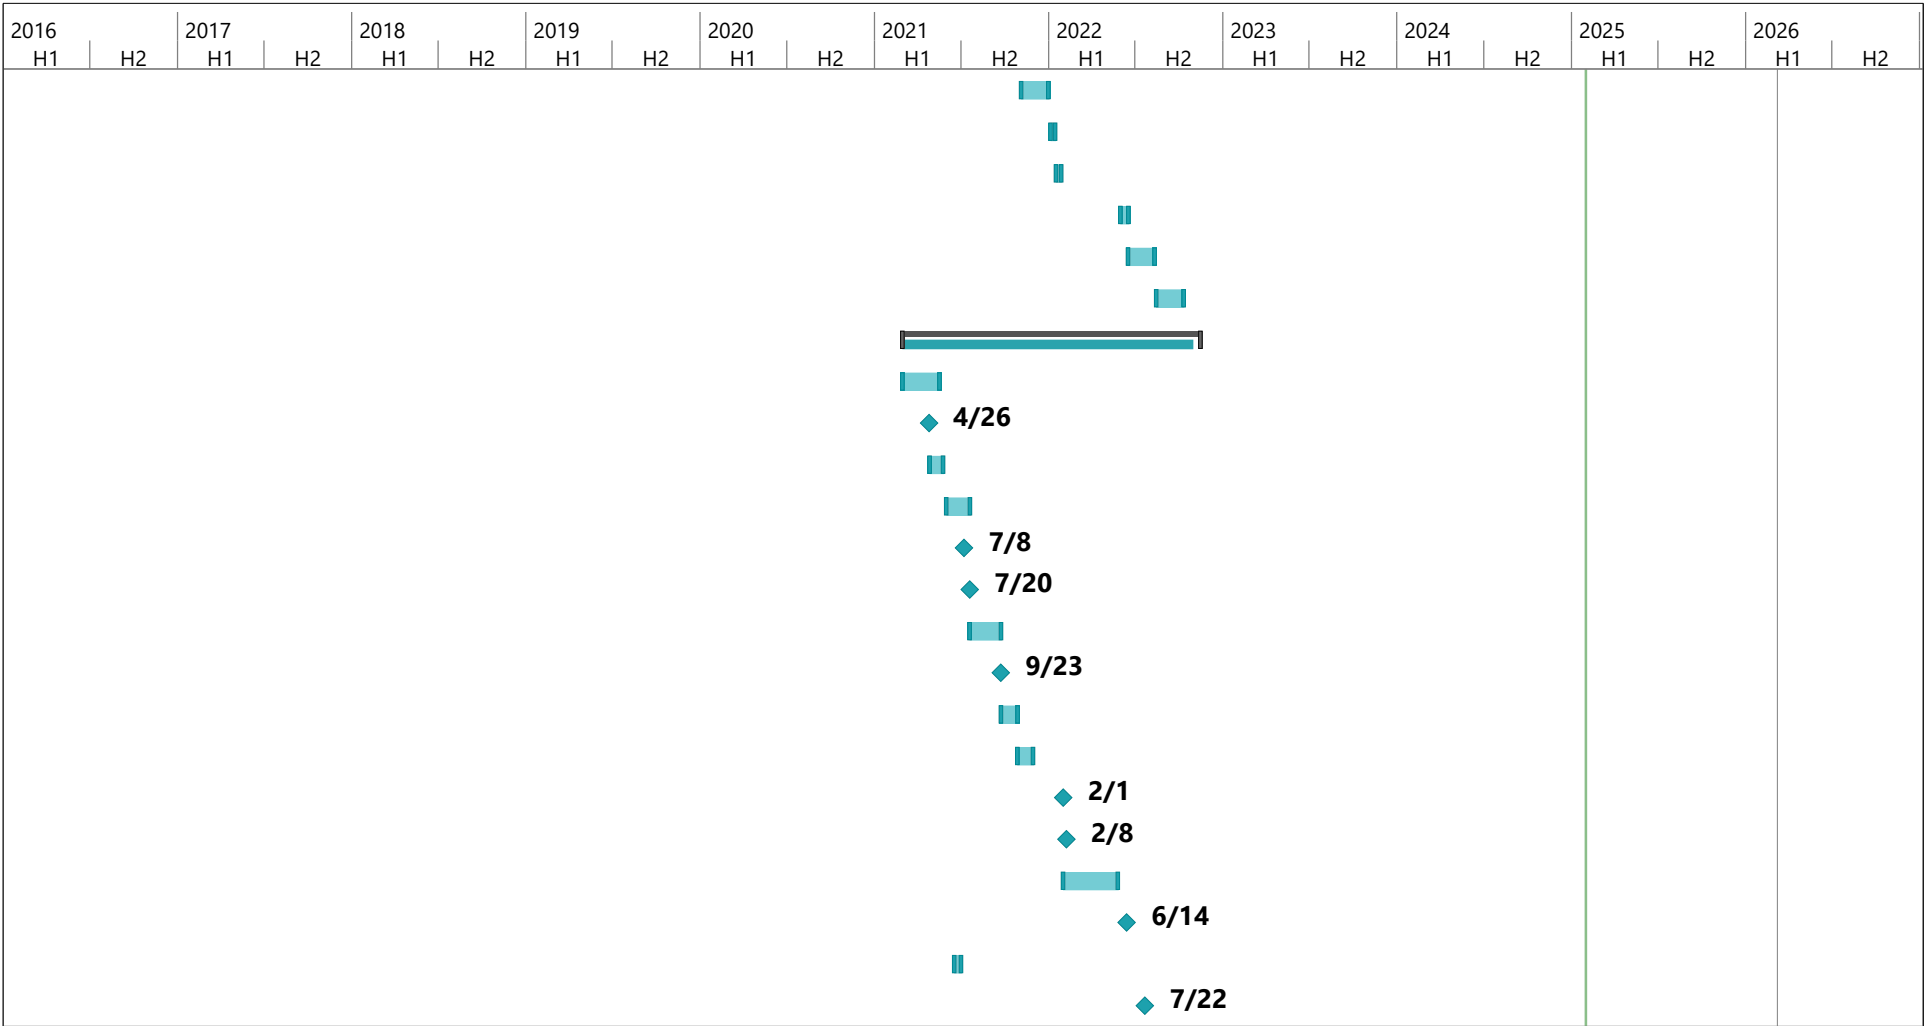


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

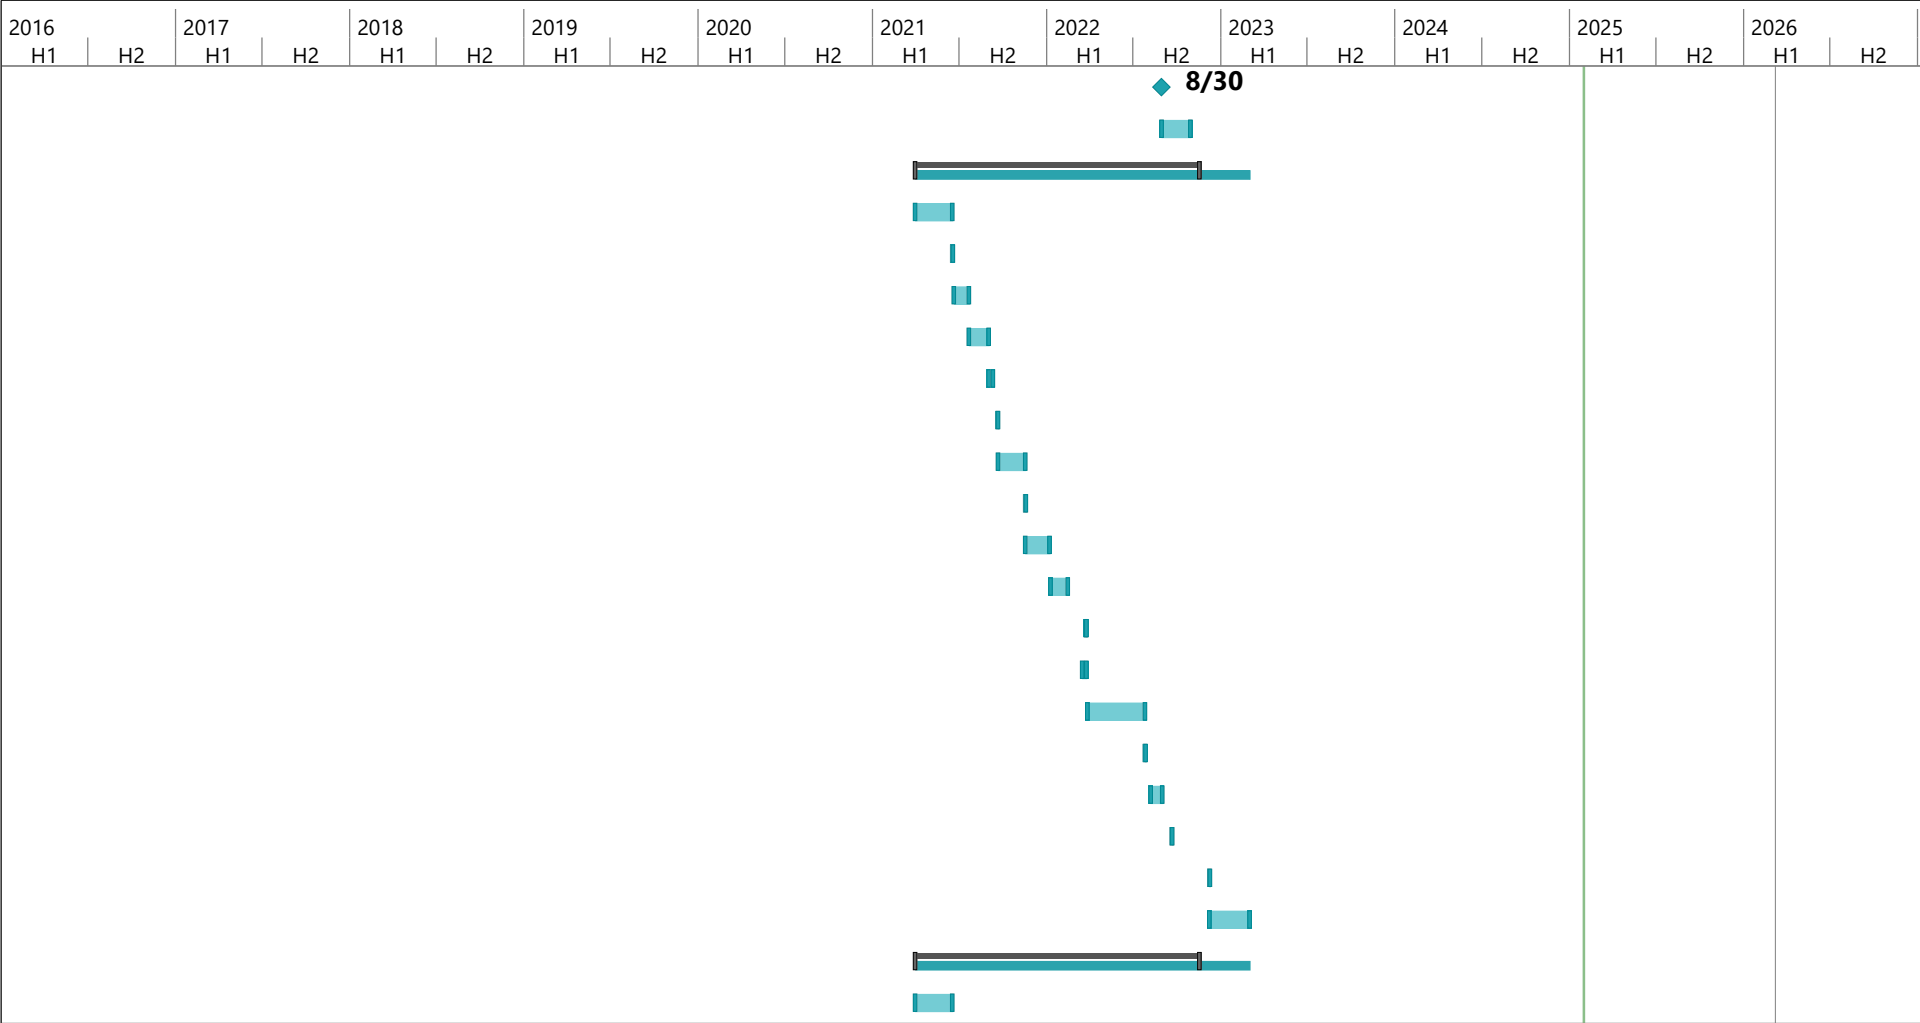


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

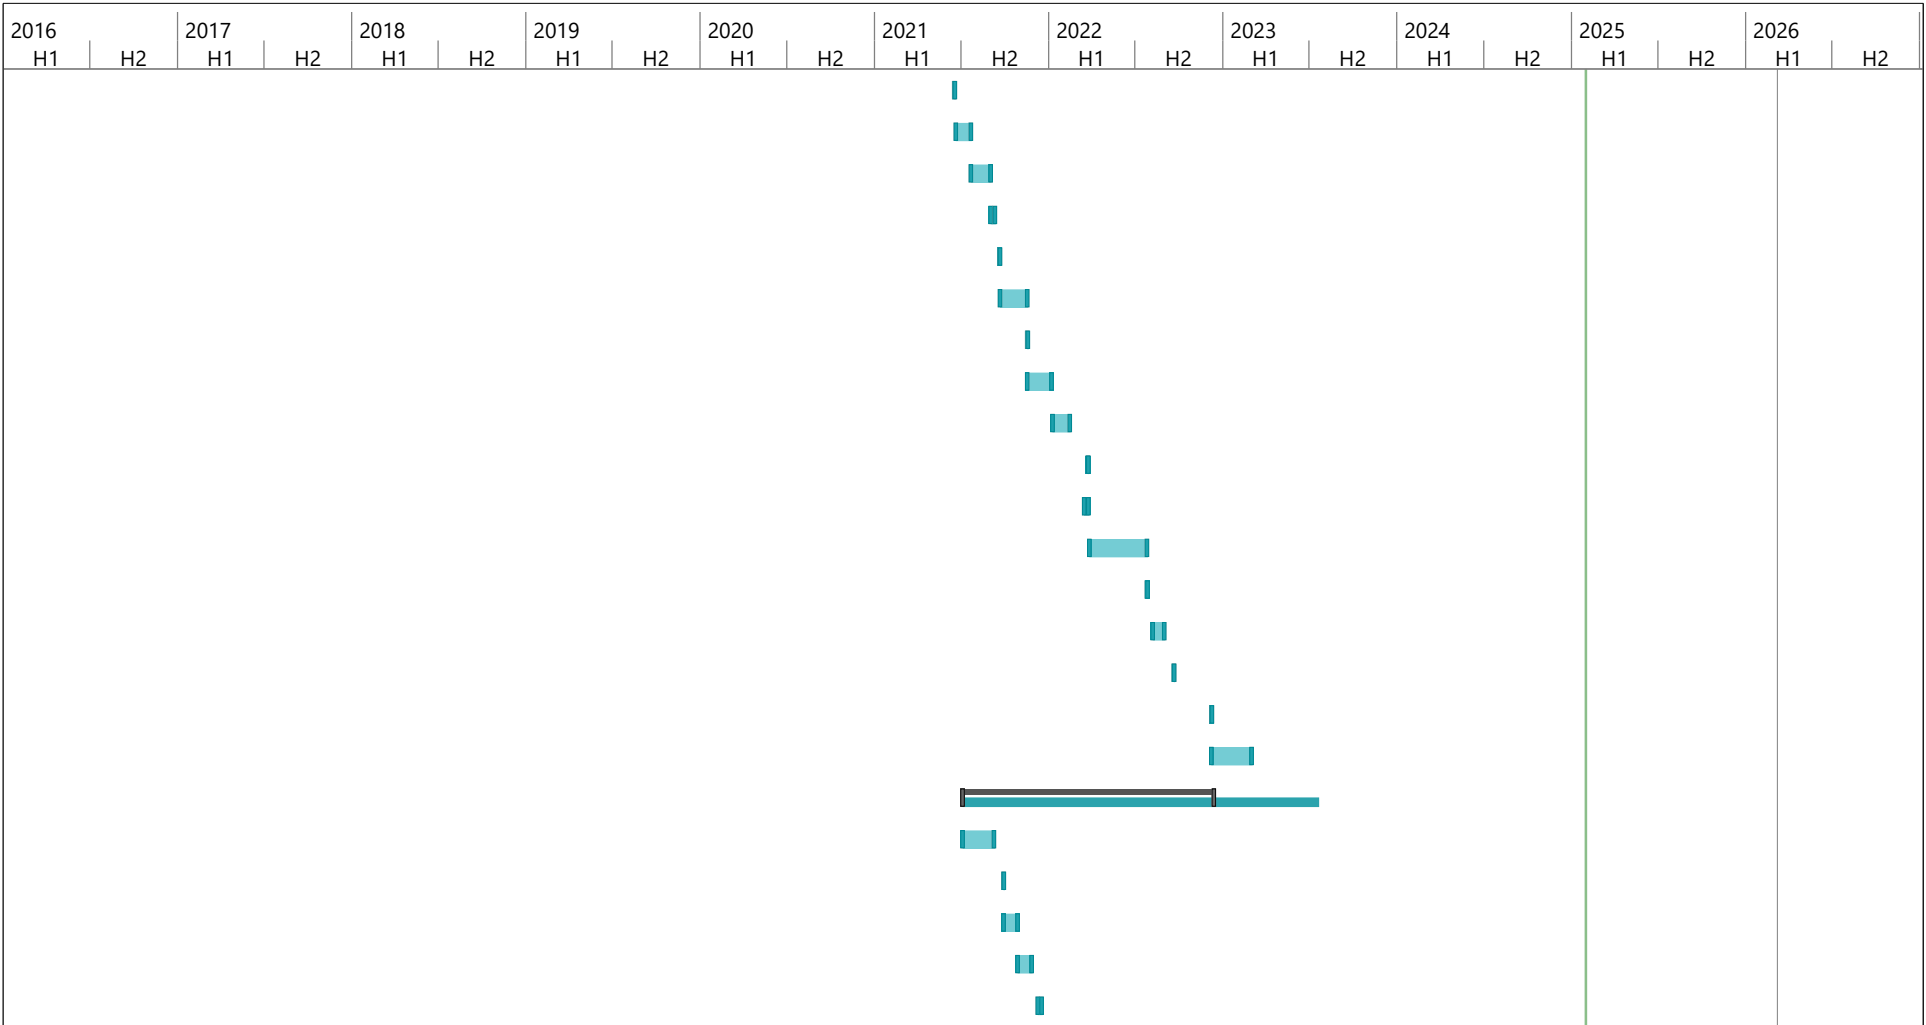


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

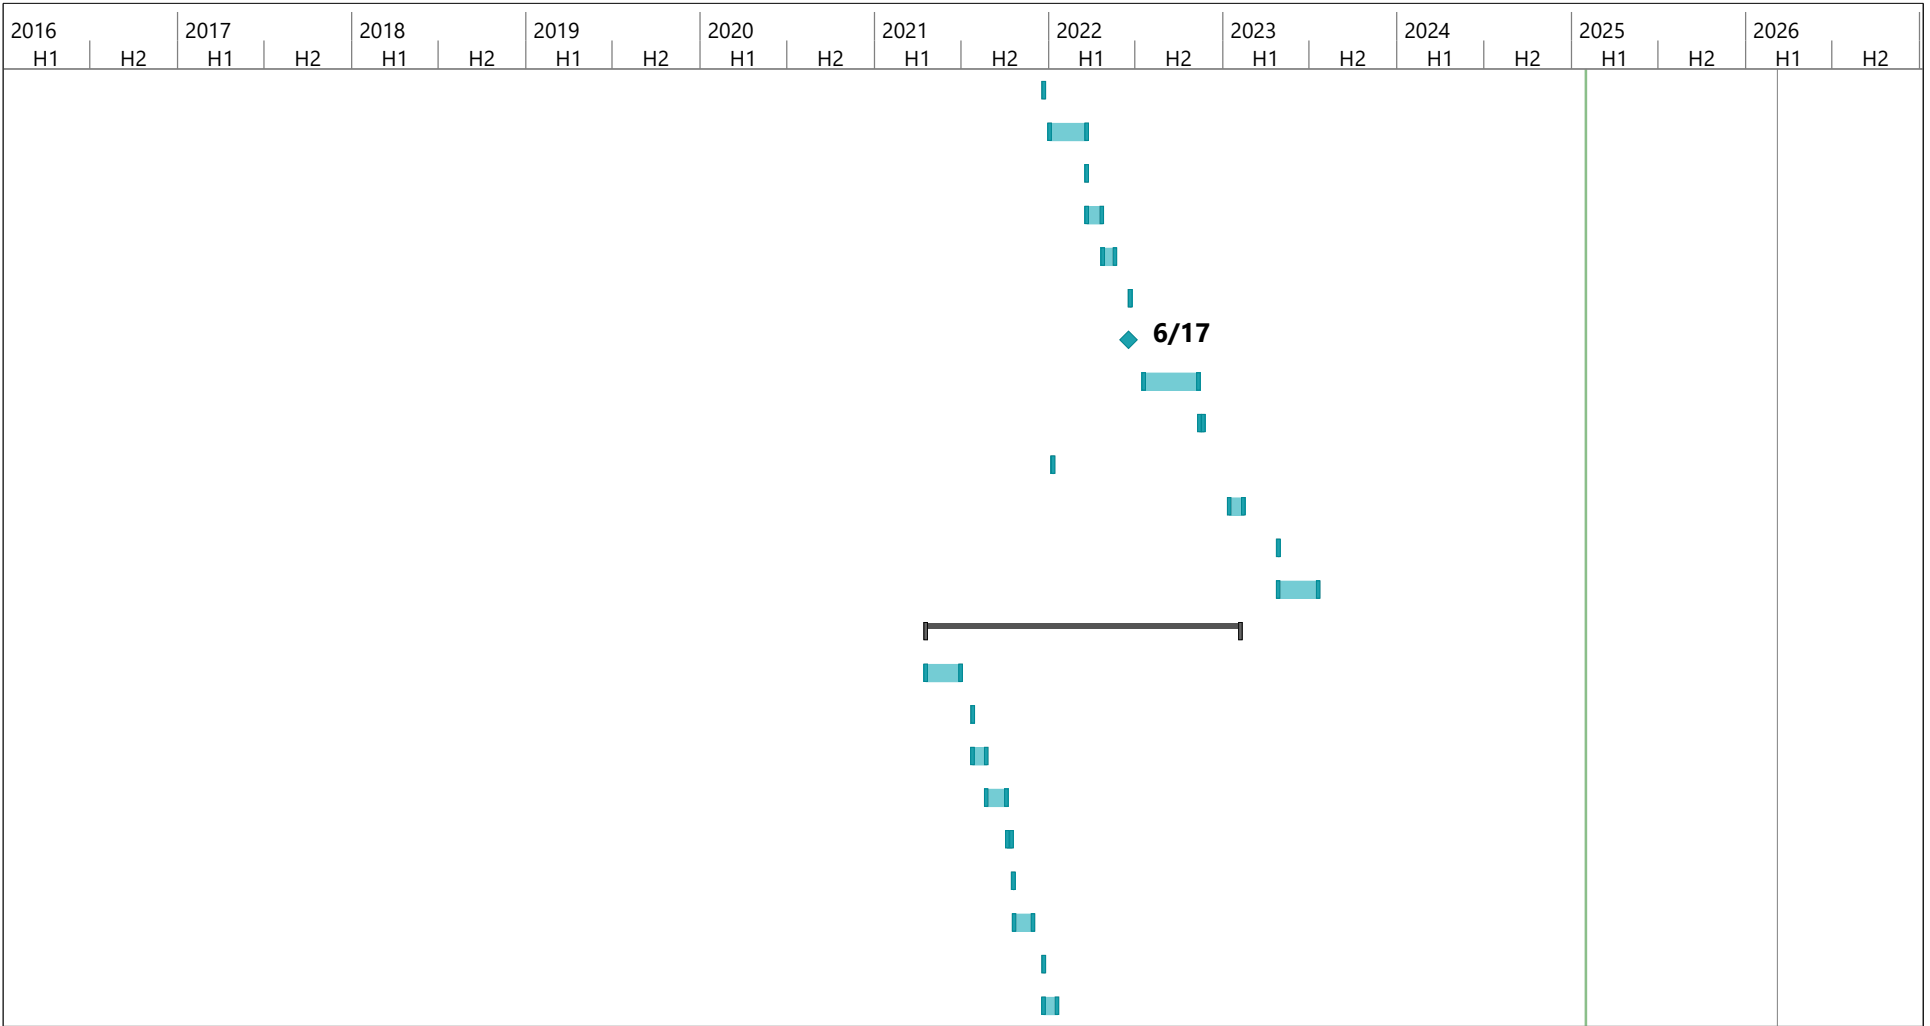


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

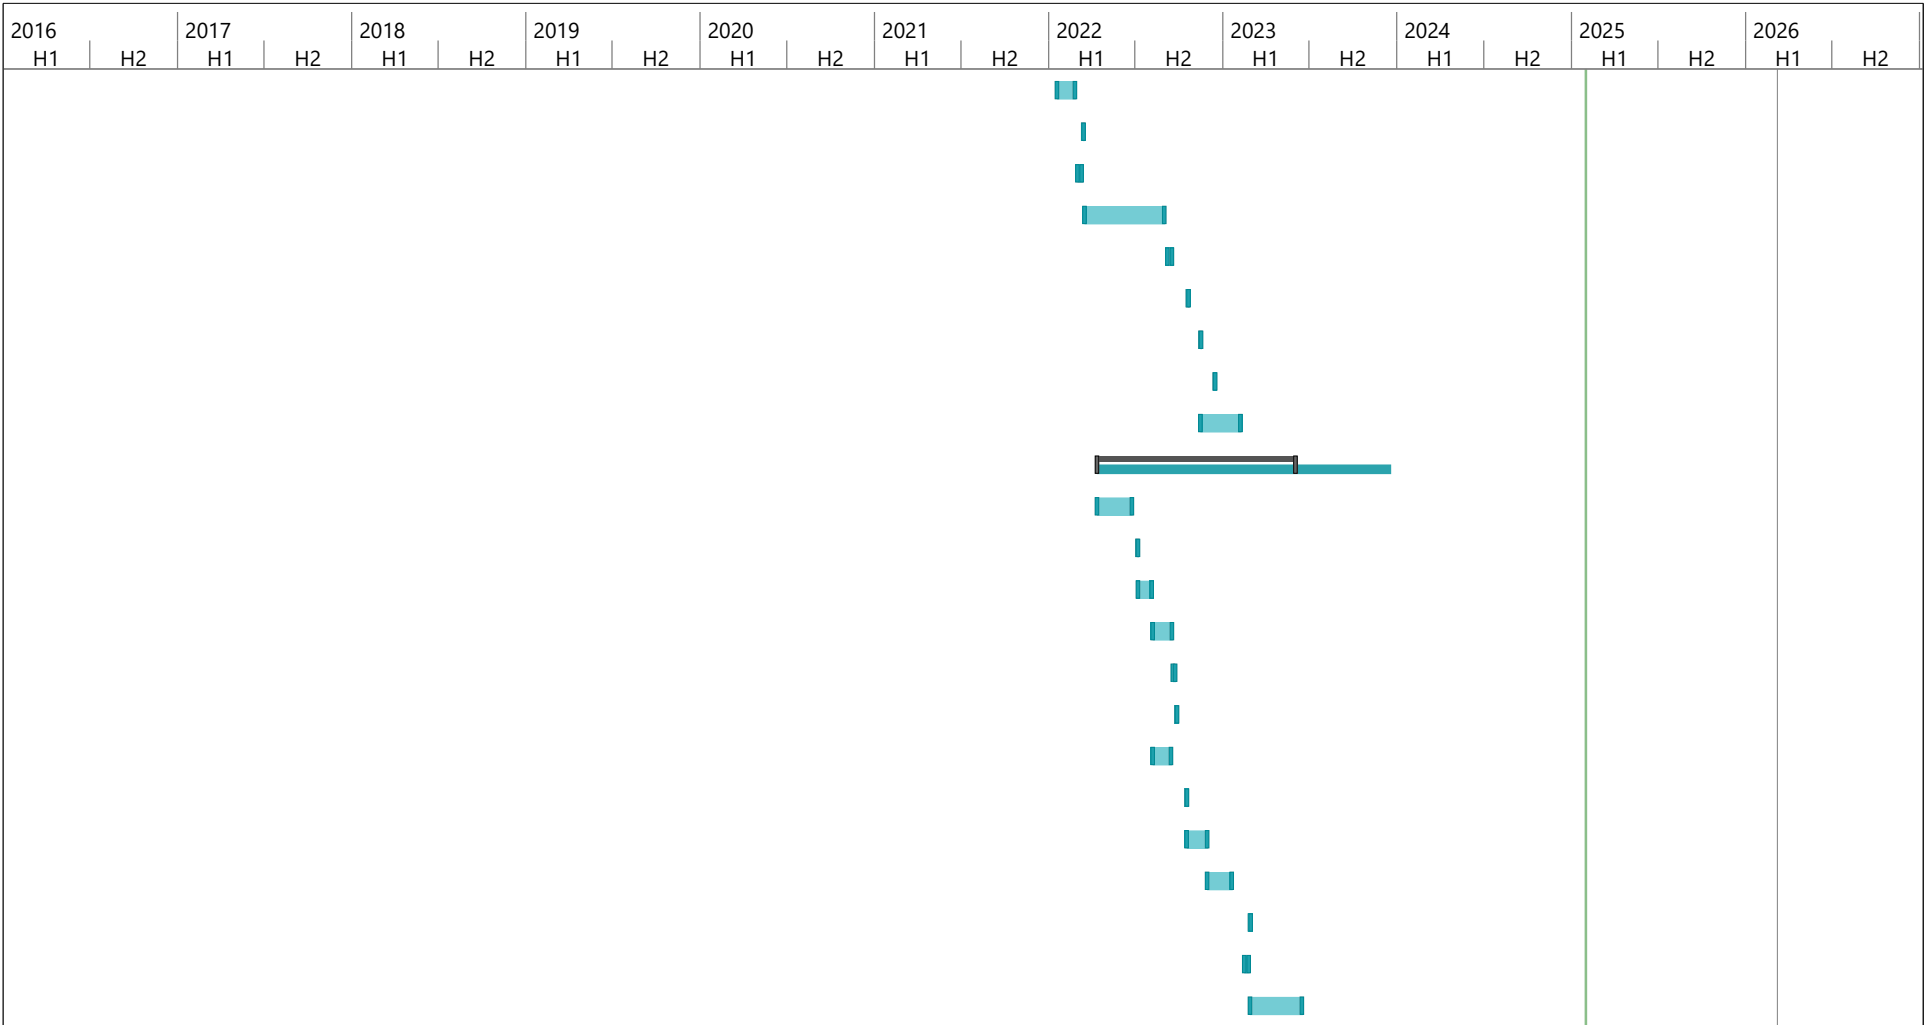


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

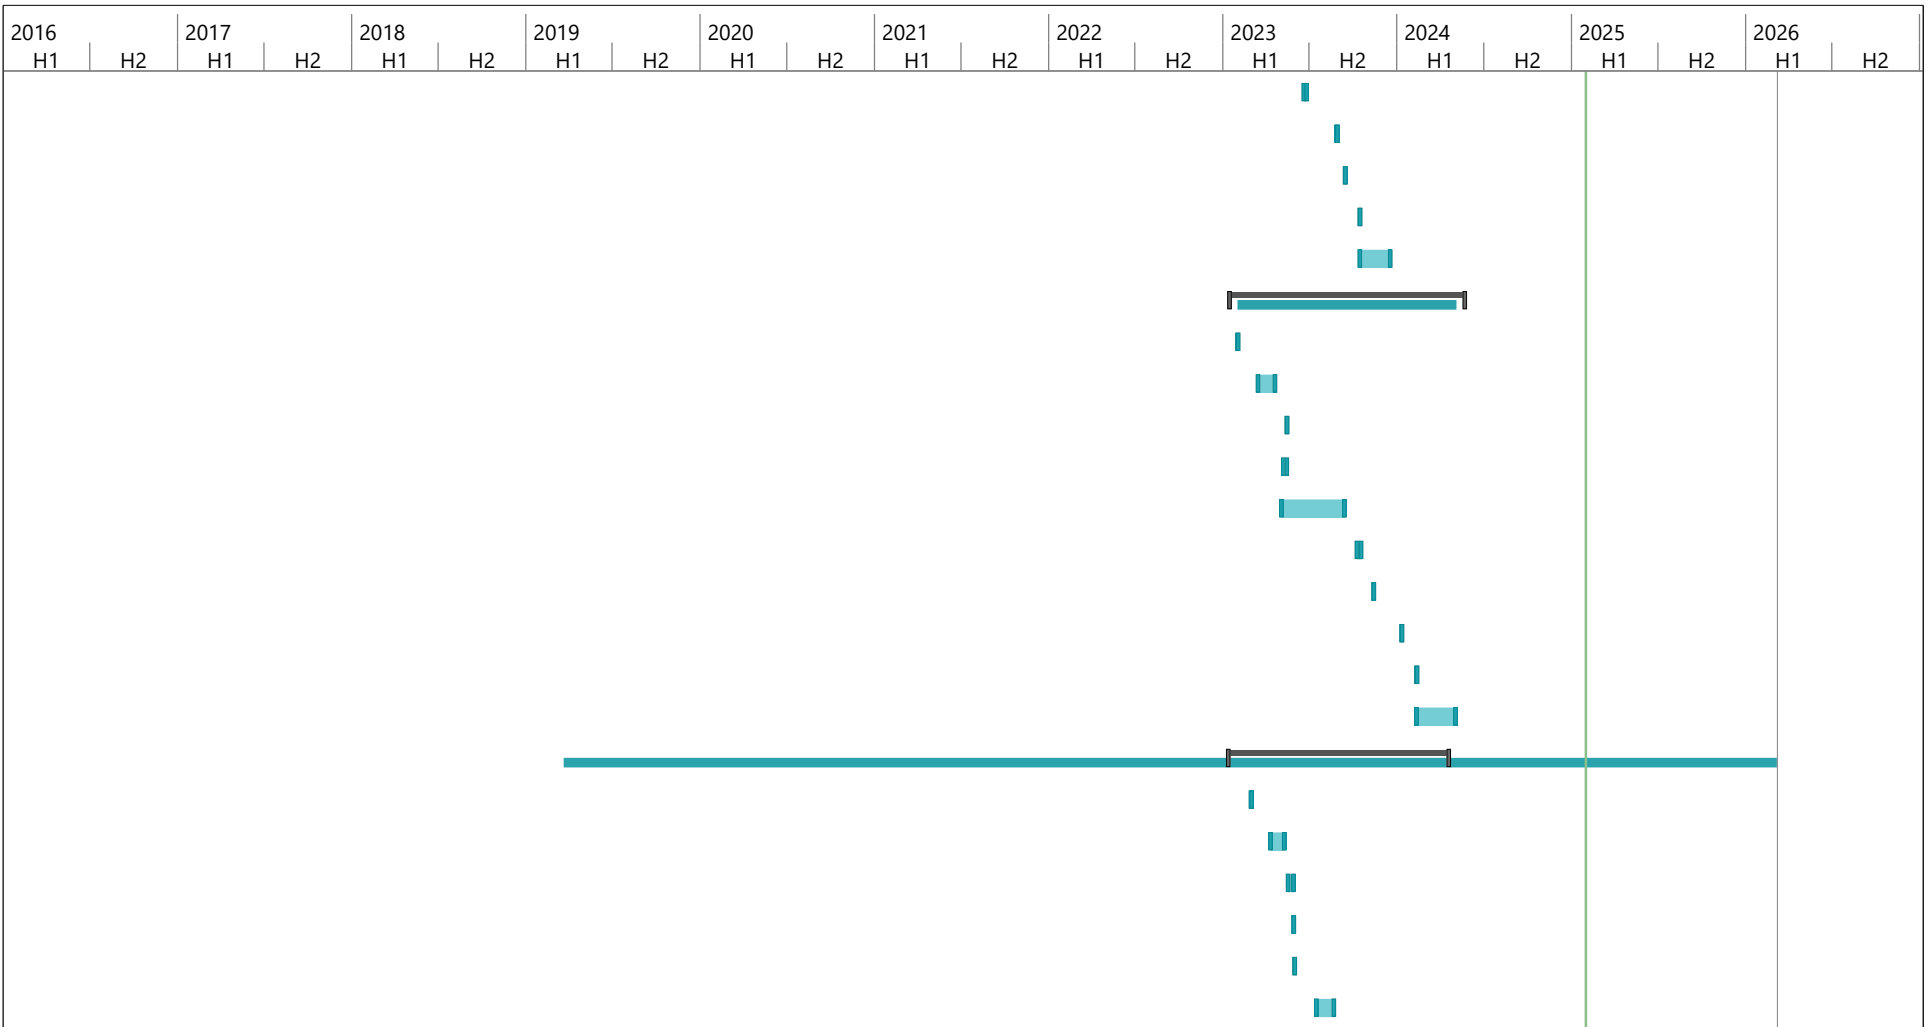


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

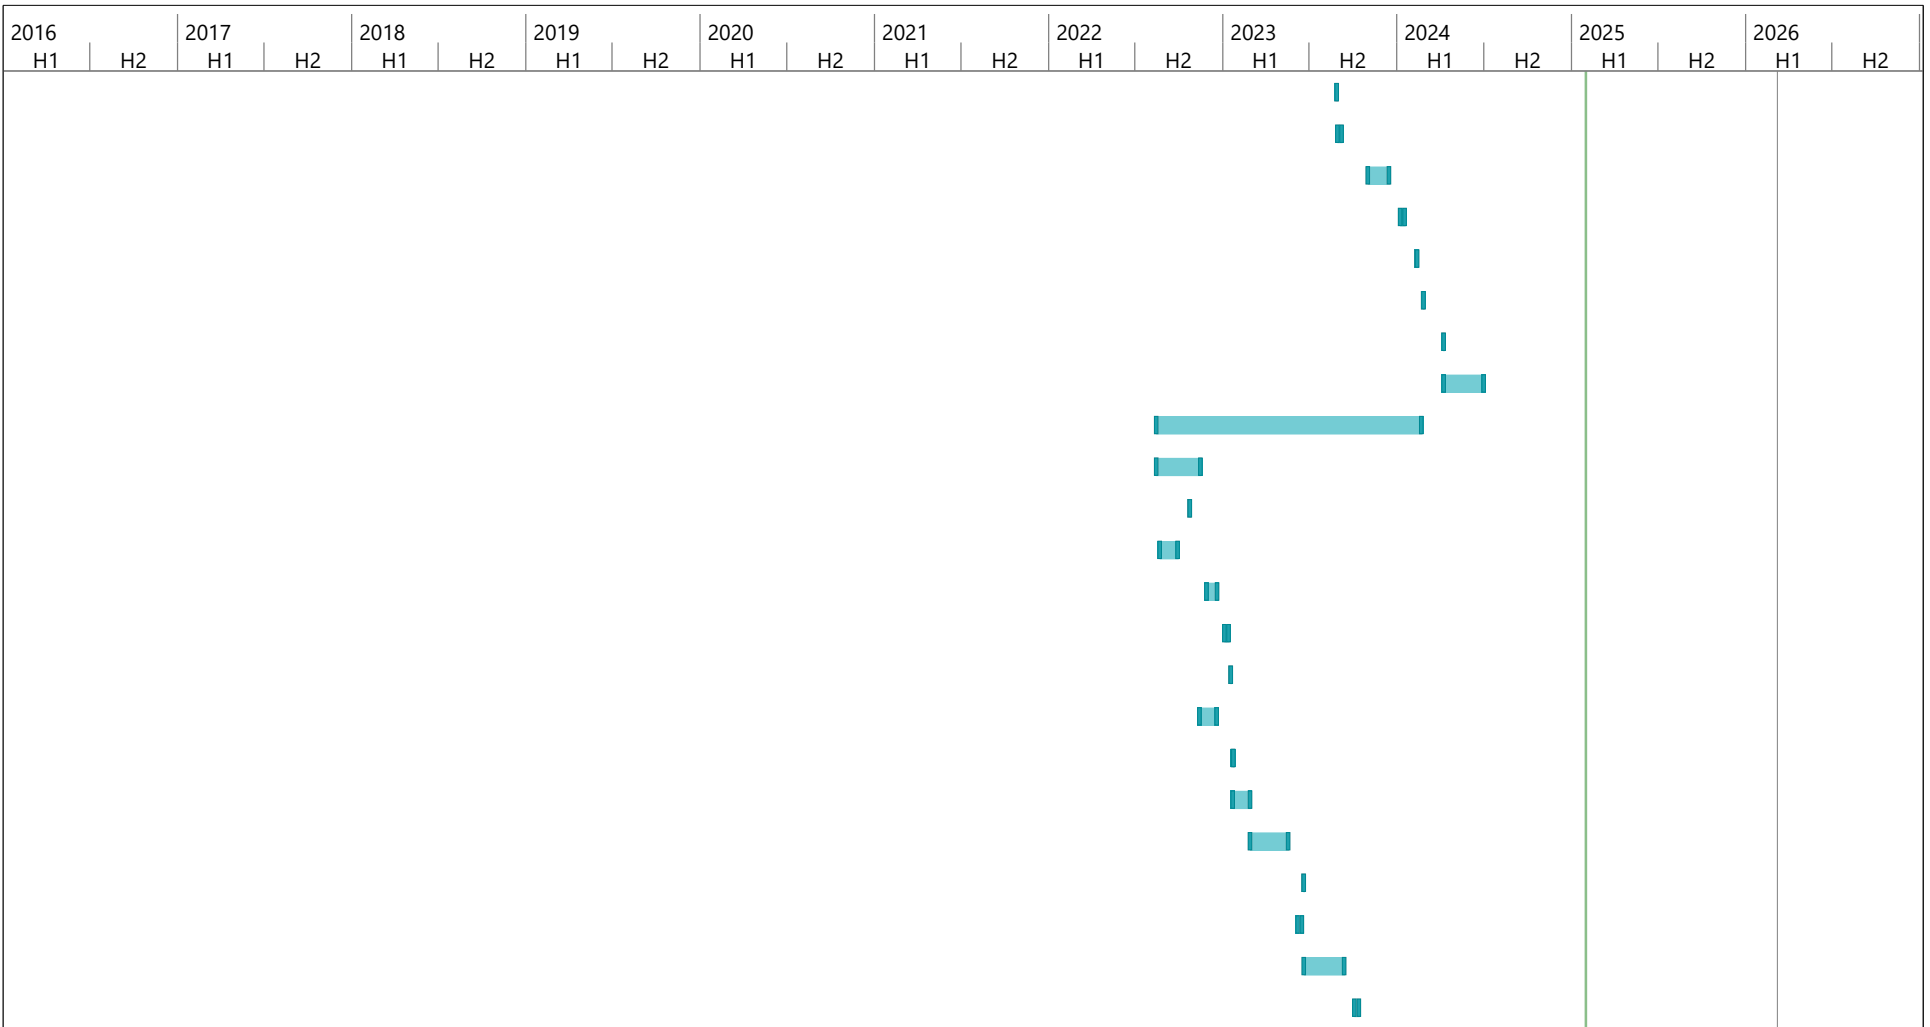


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

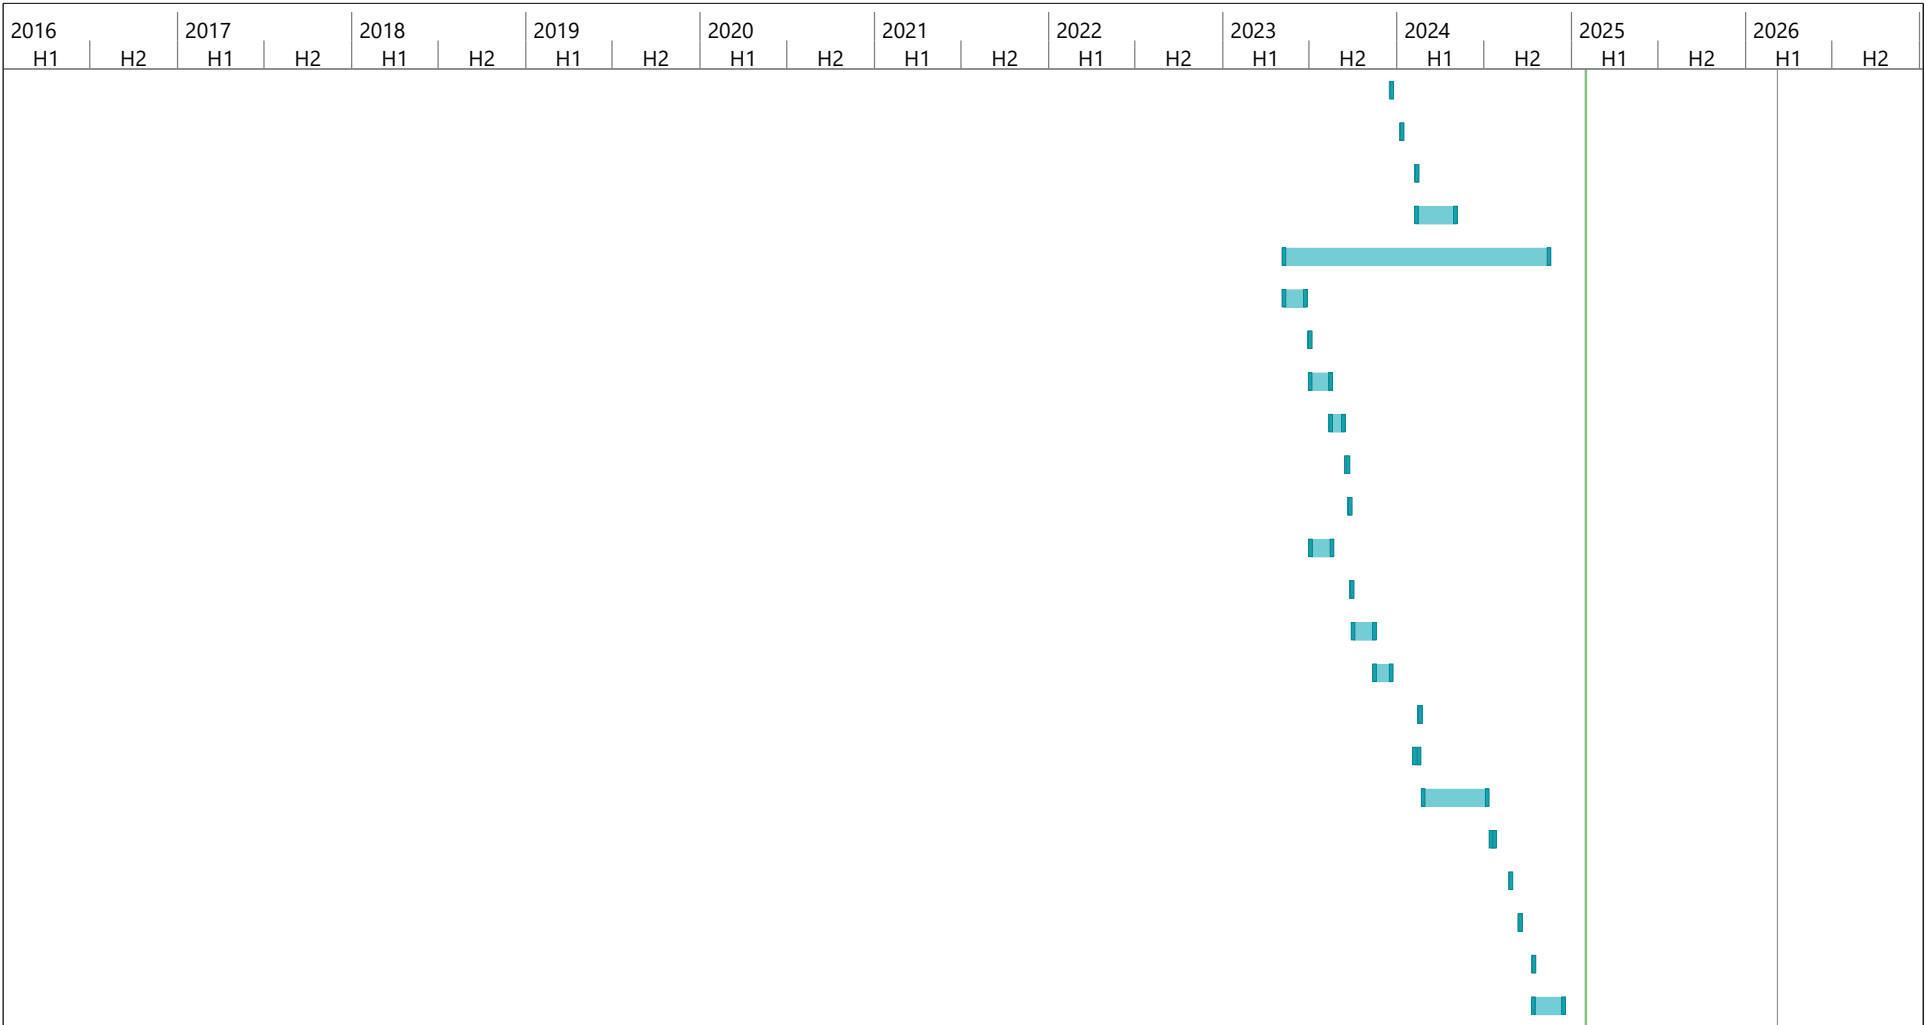


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

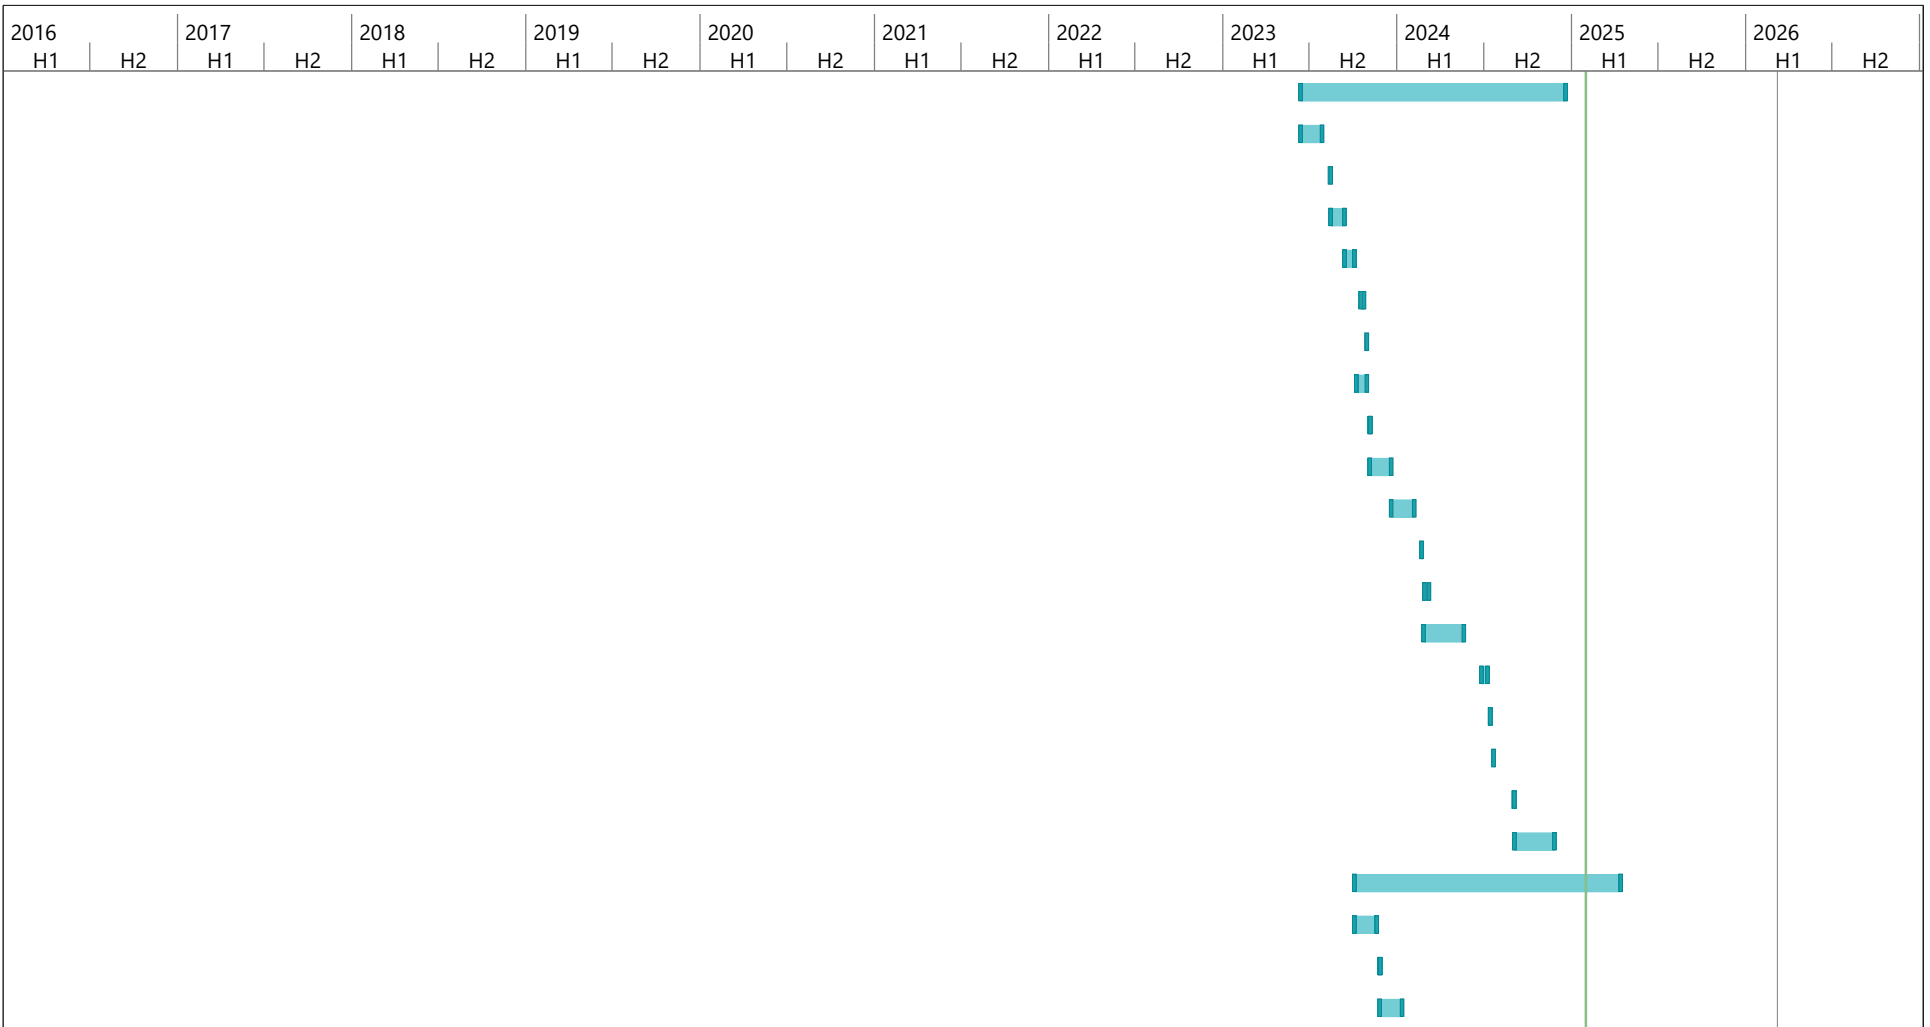


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

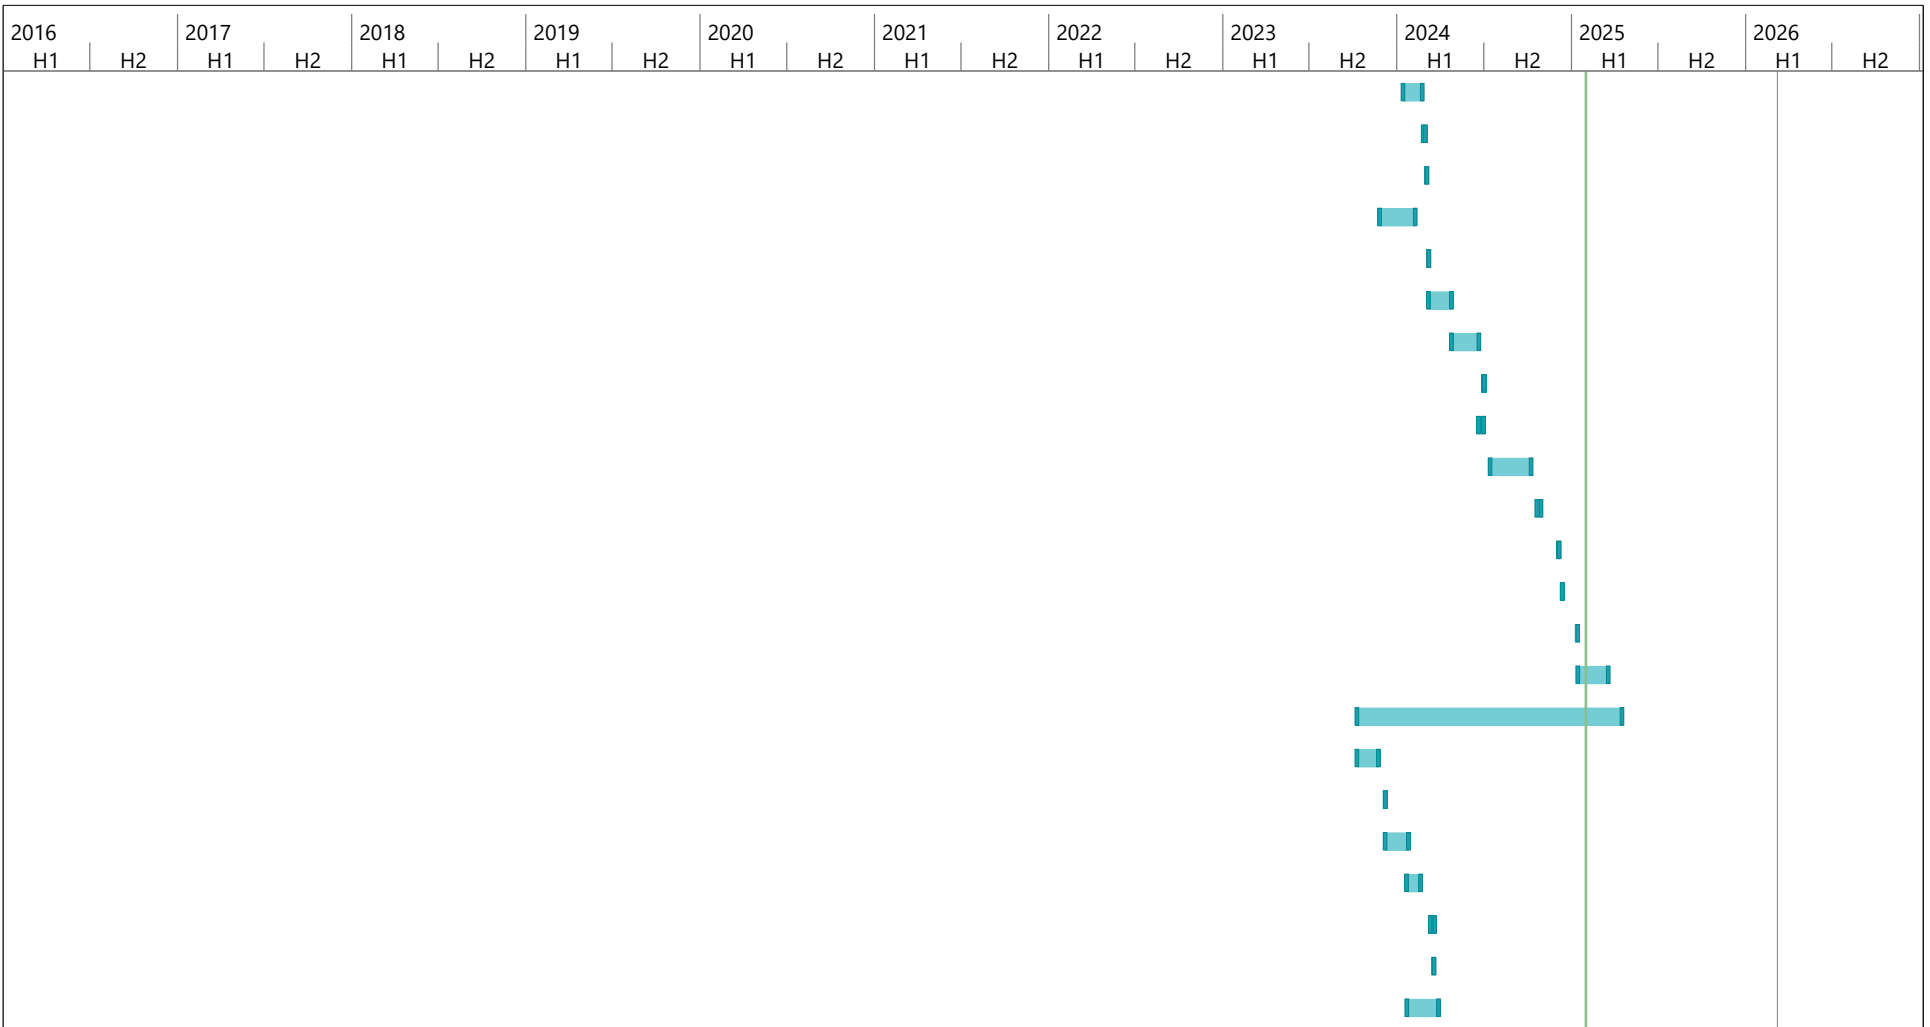


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

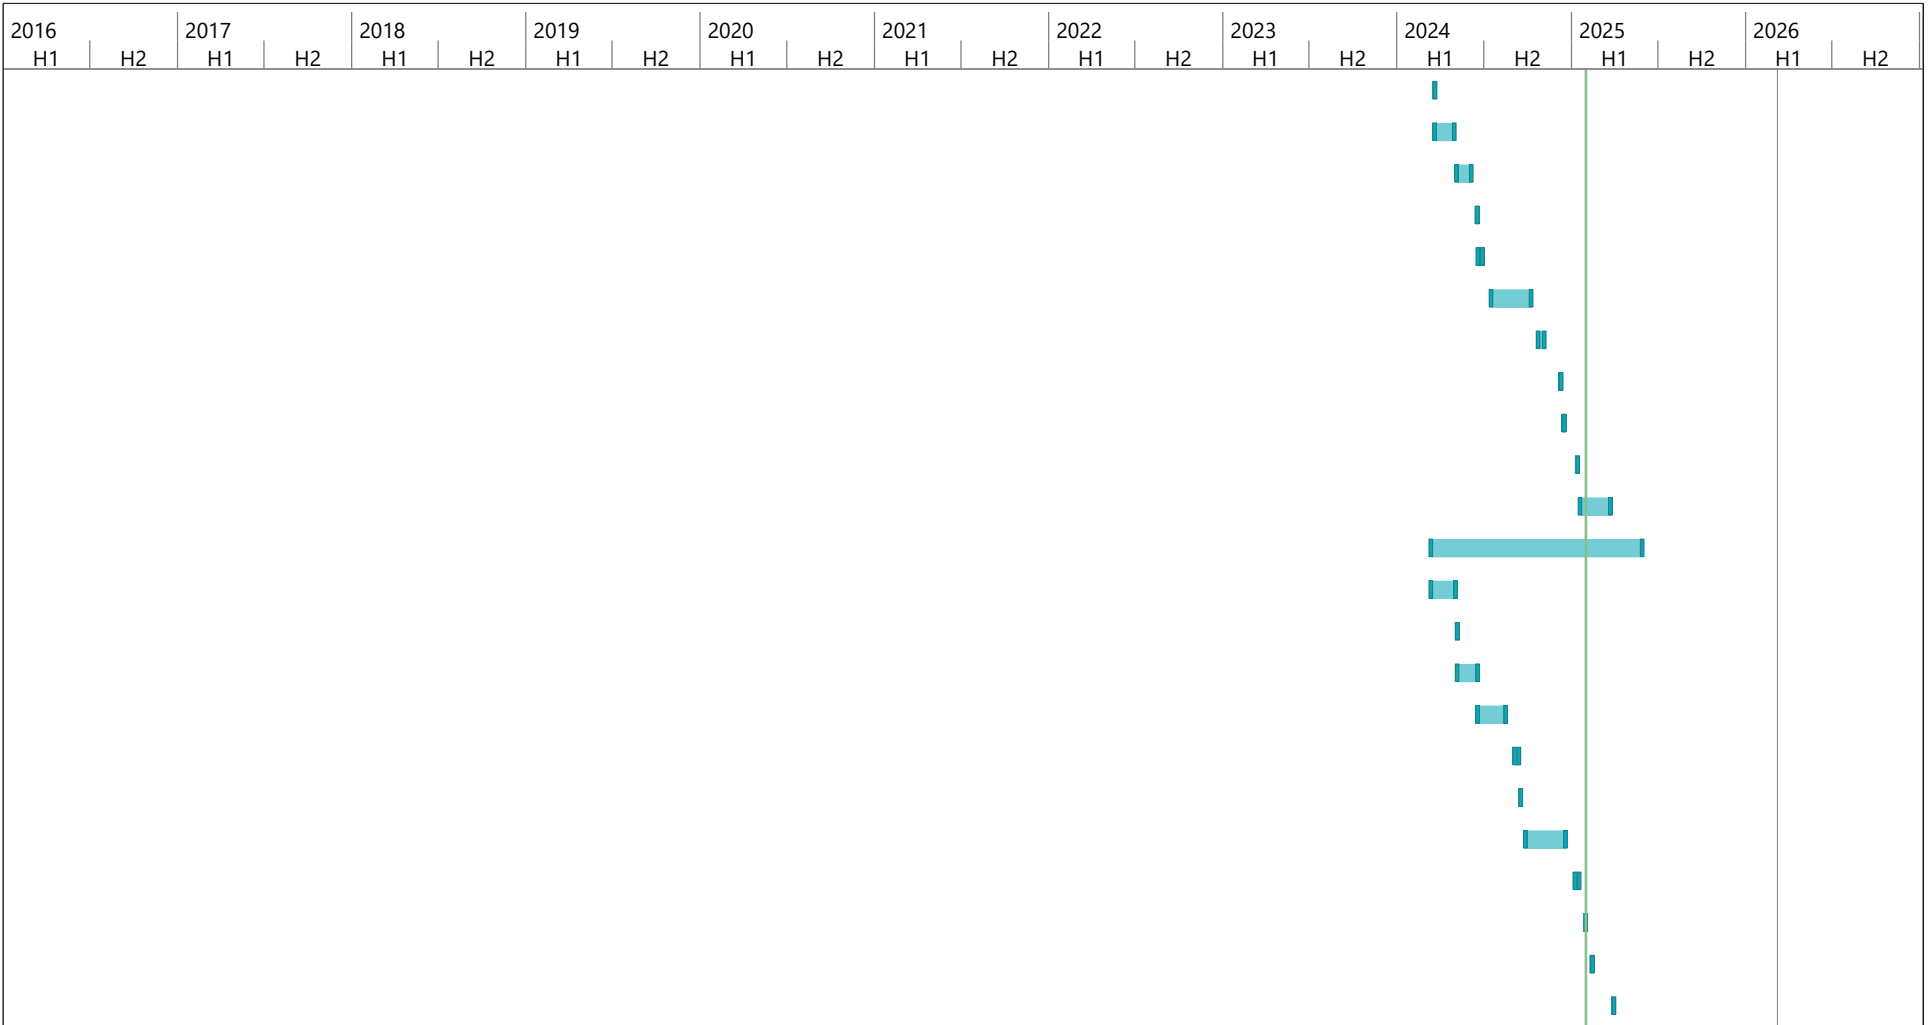


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

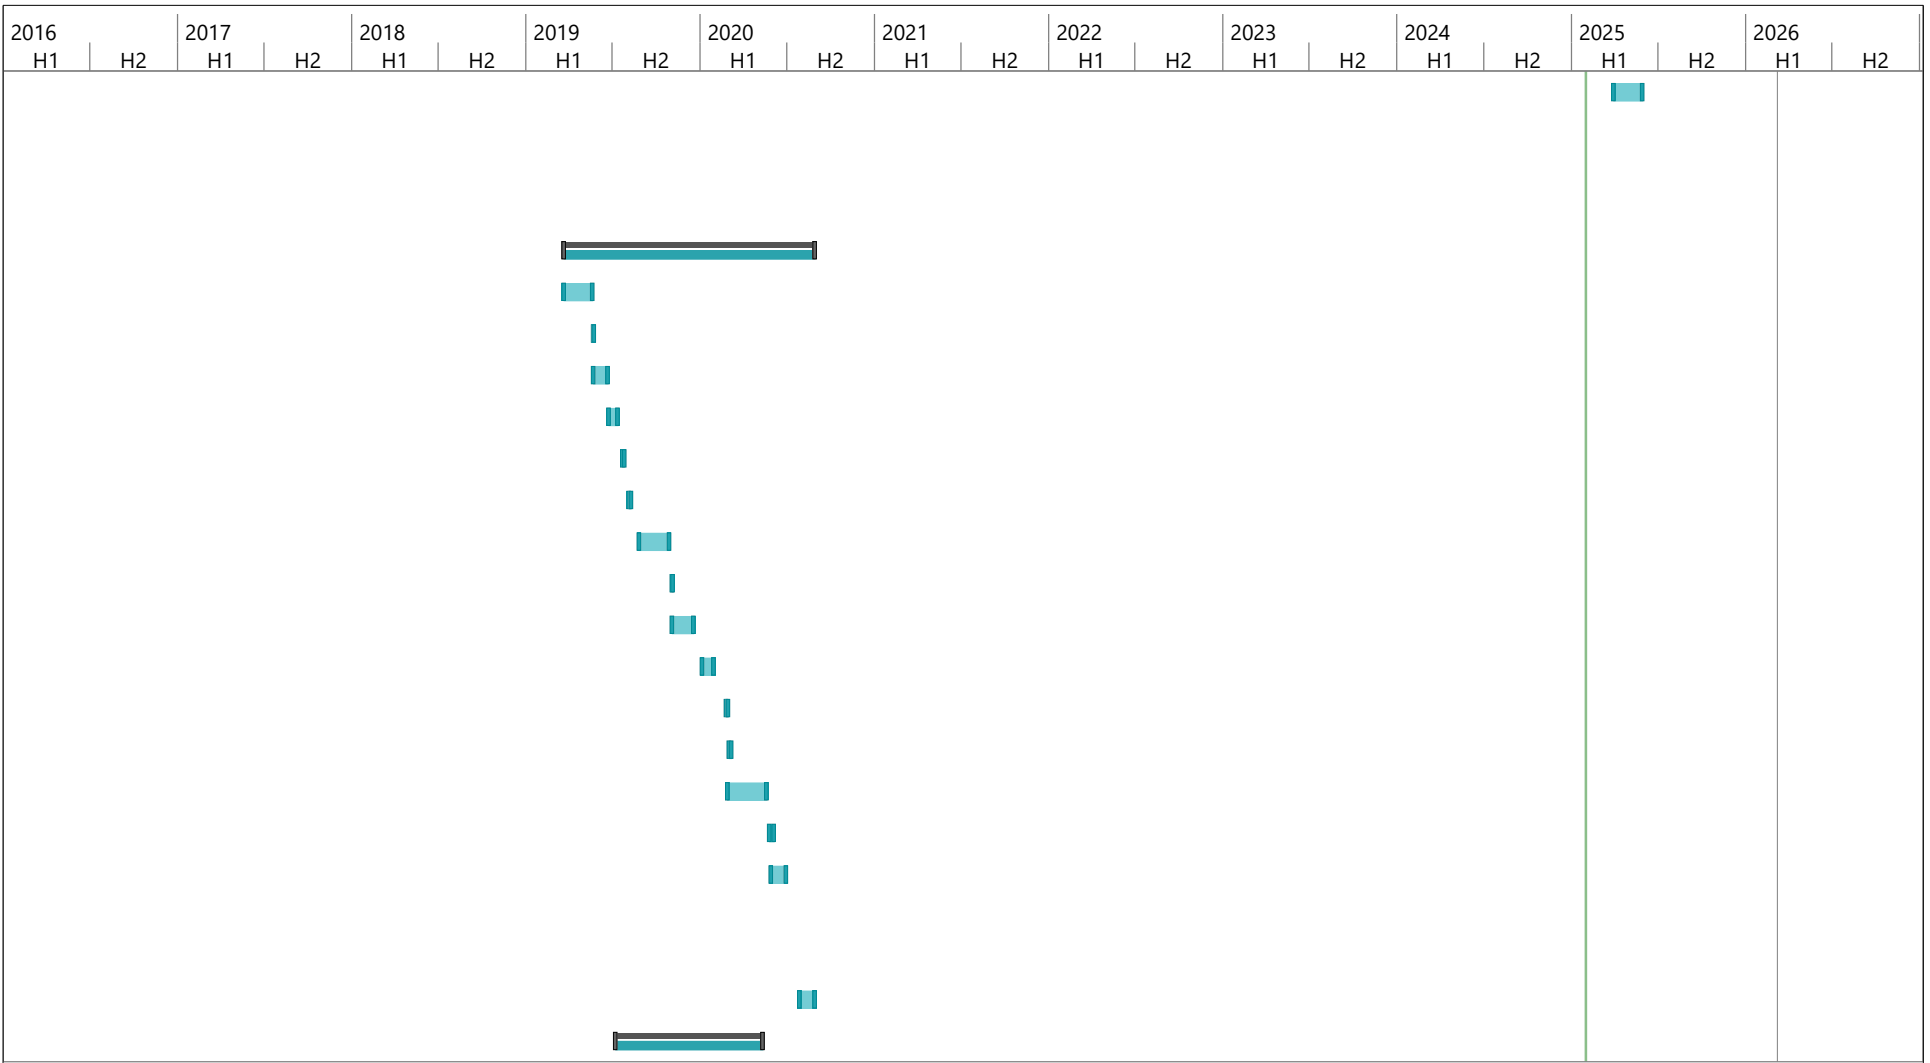


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

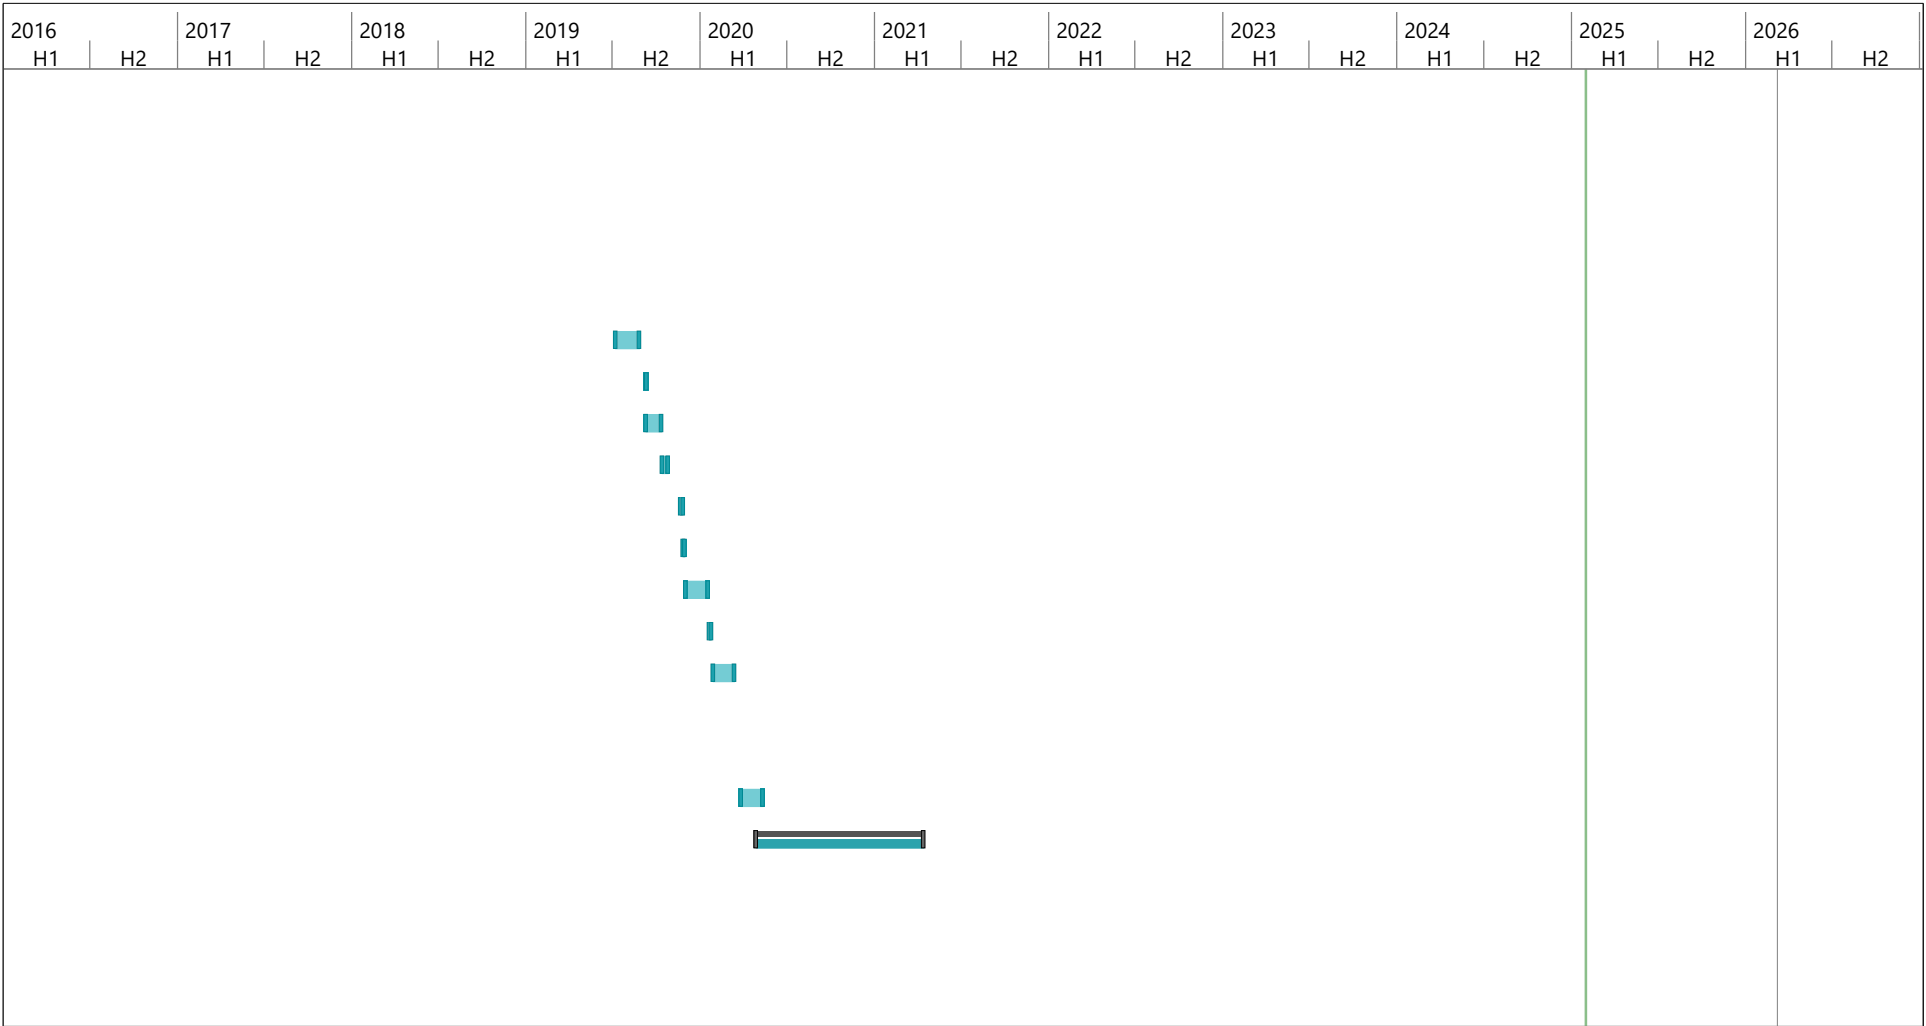


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

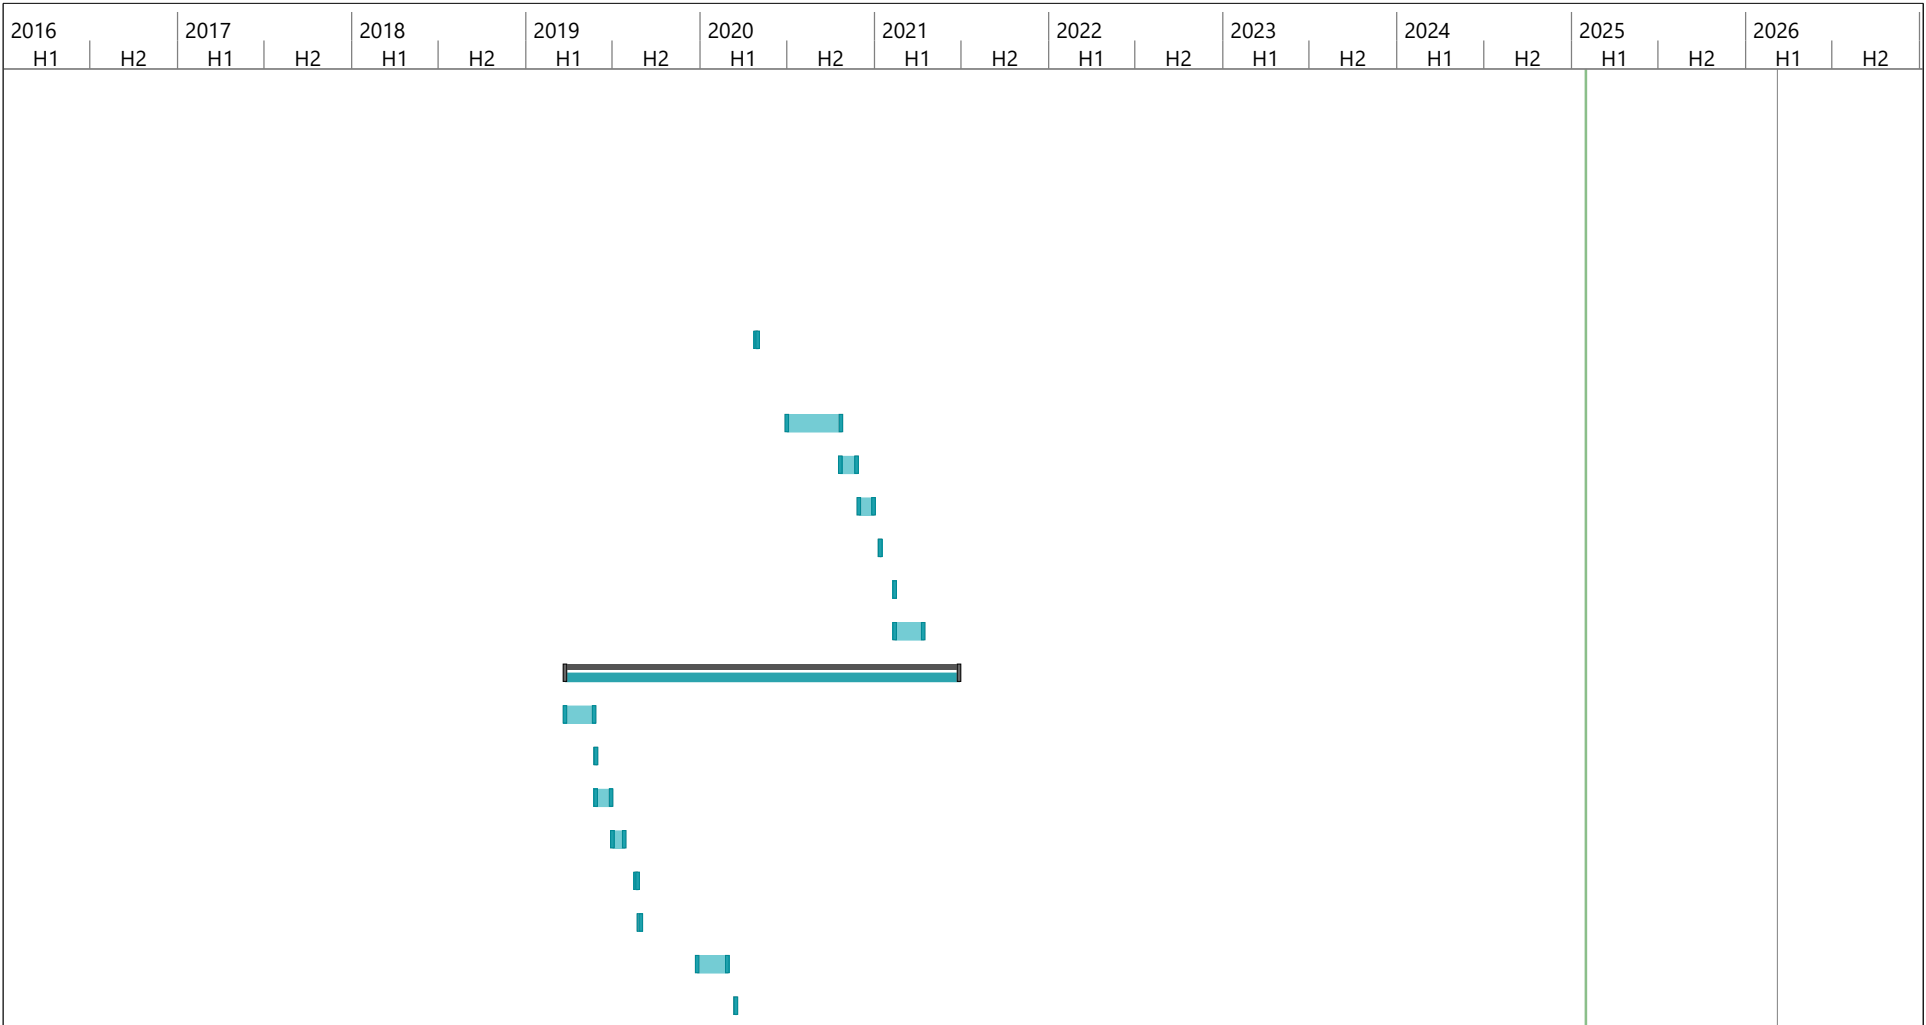


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

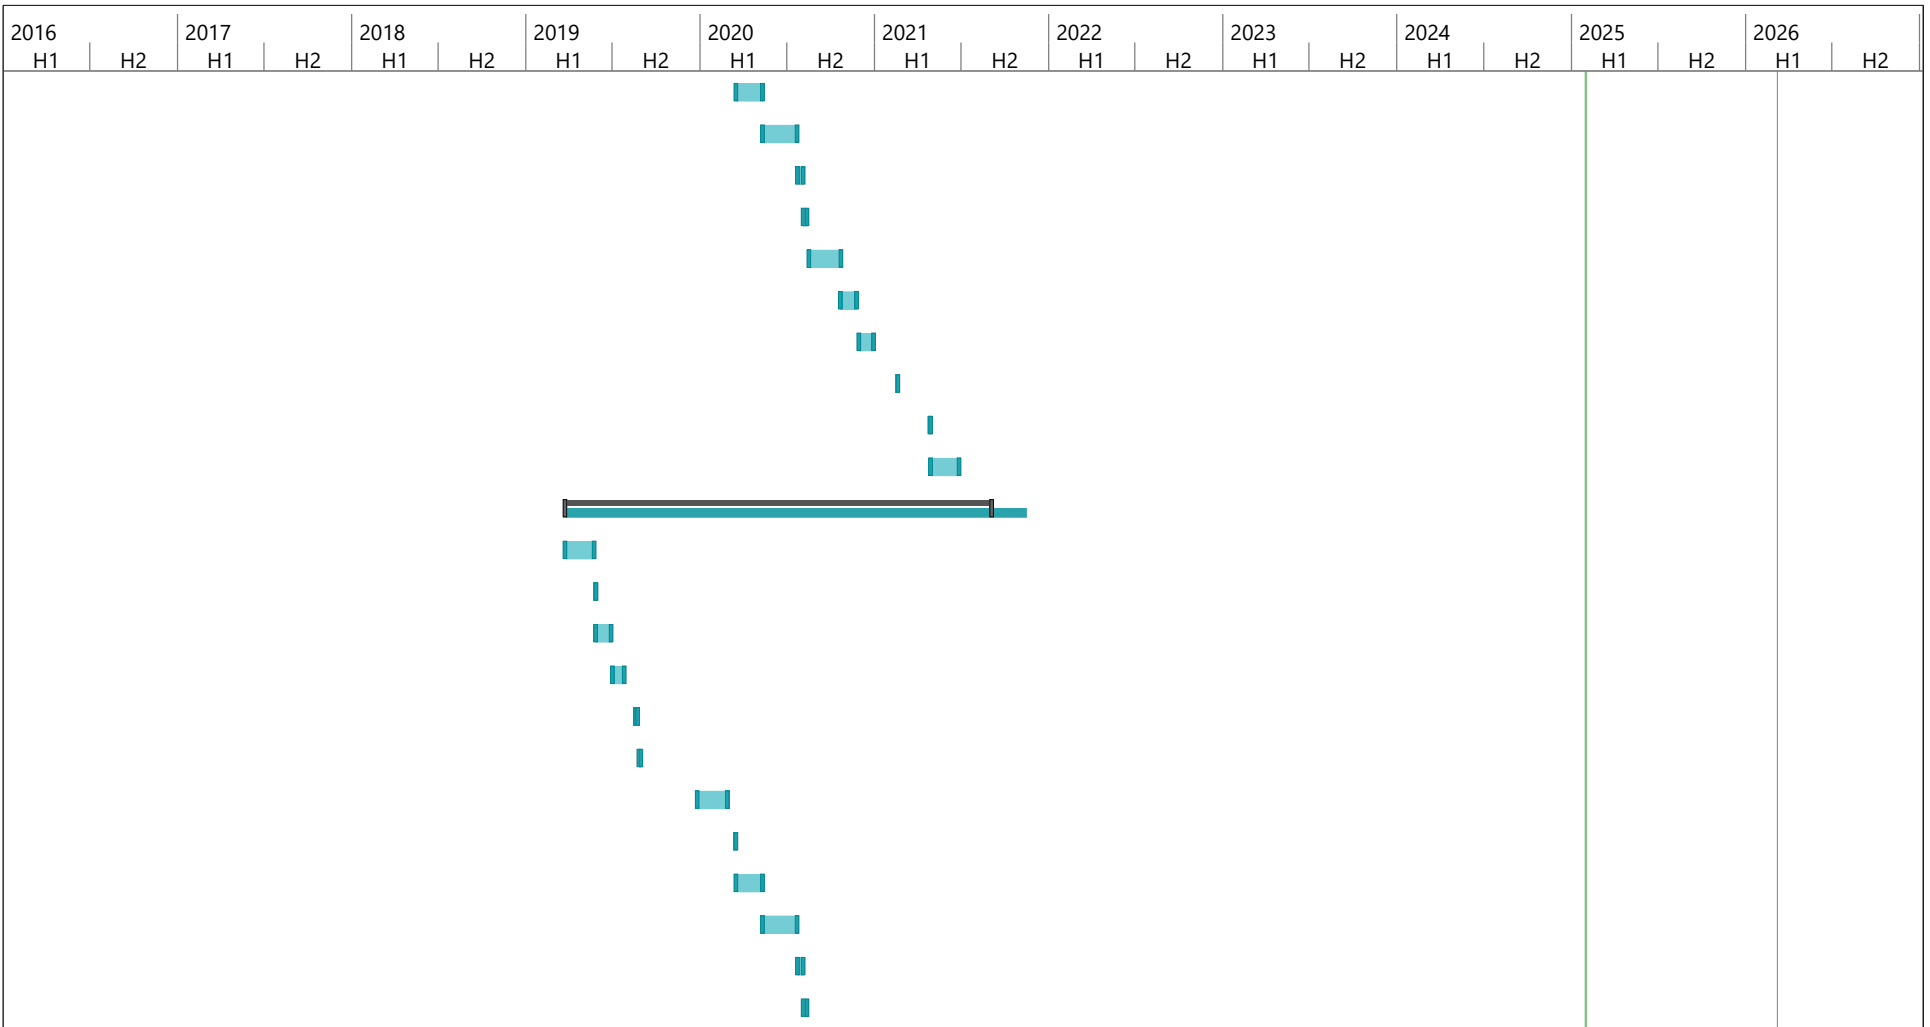


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

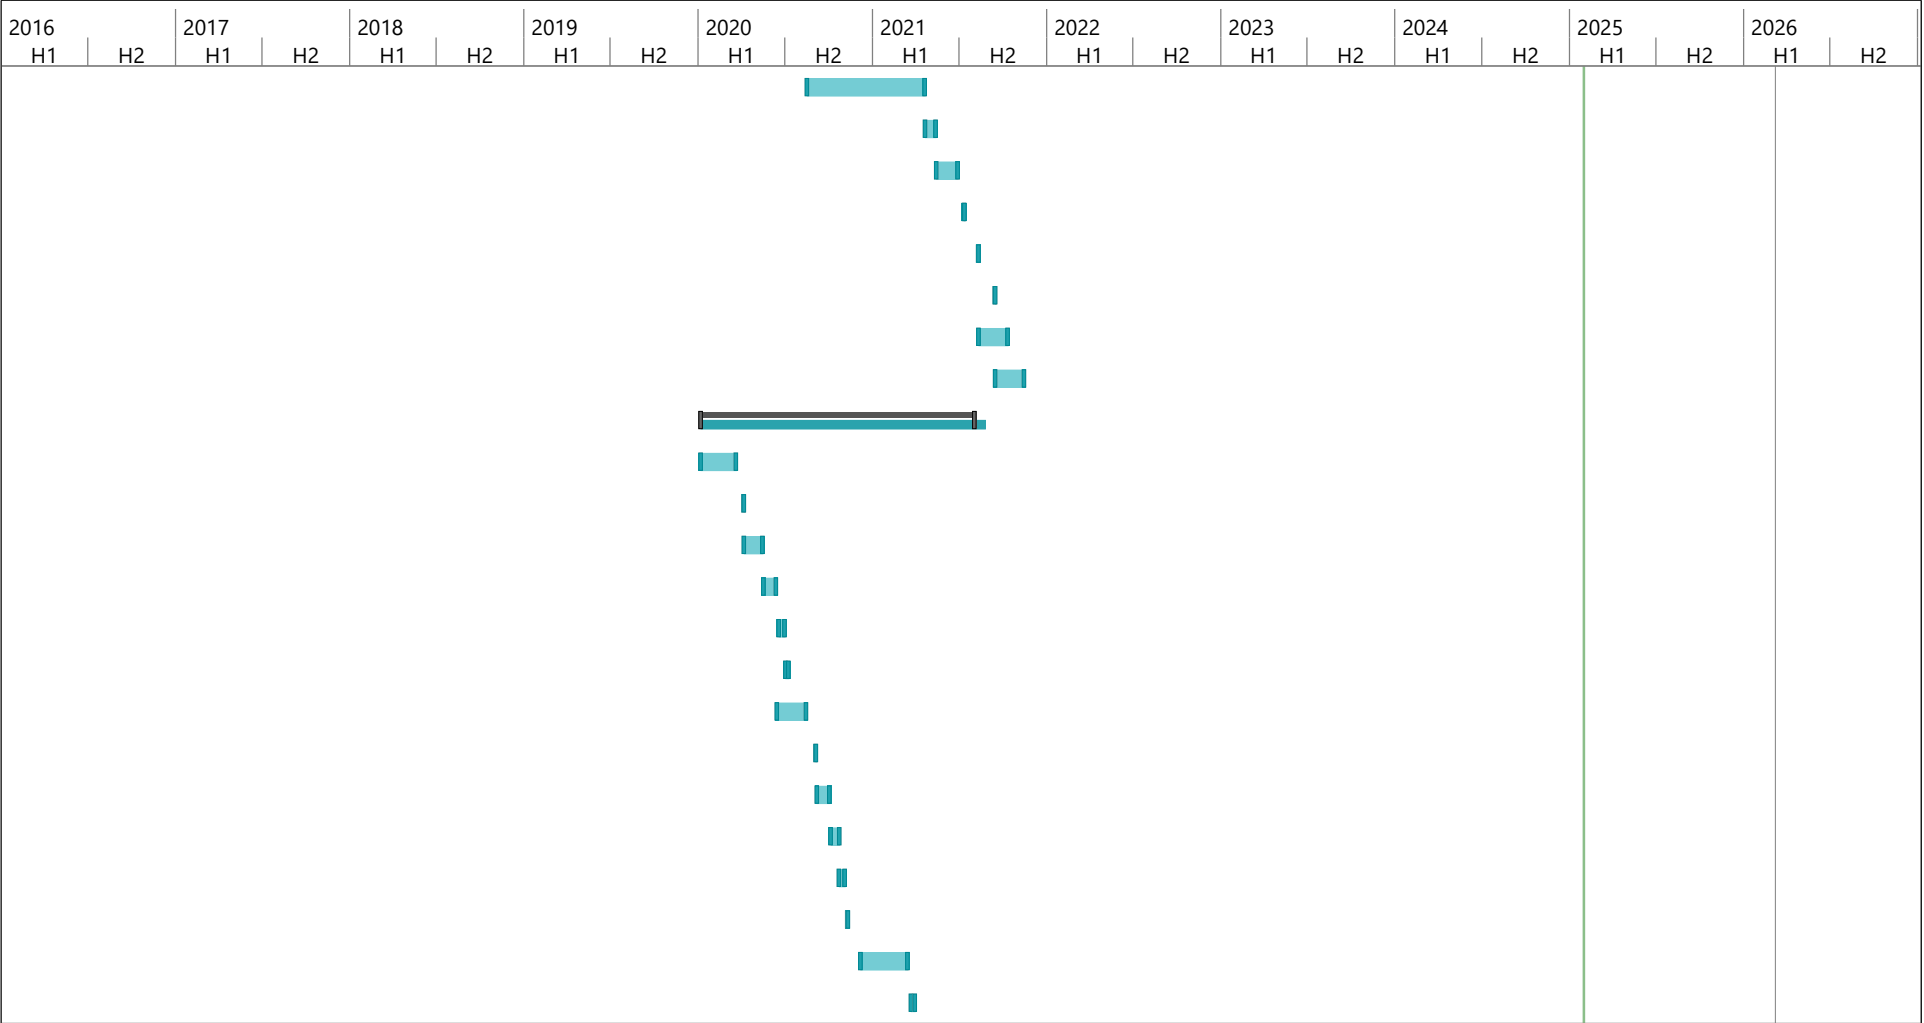


Project: IOU Master Task Timeli
 Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

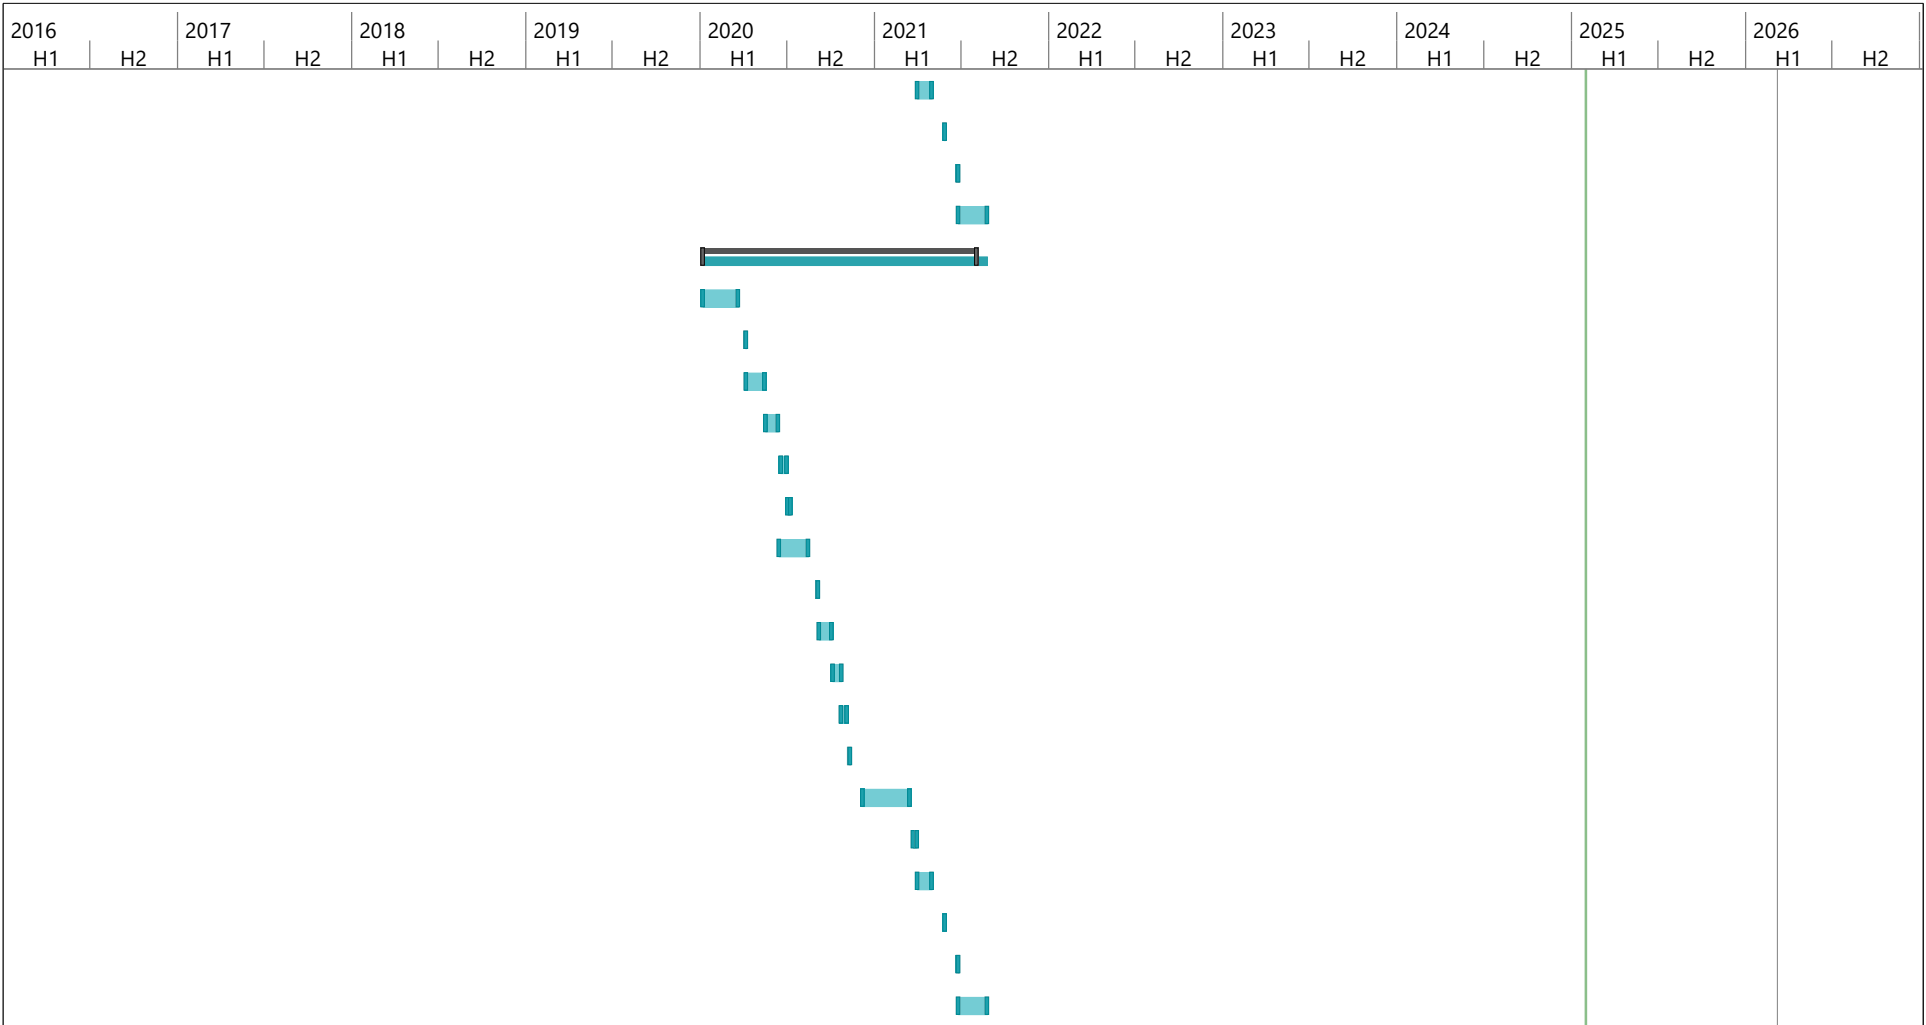


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

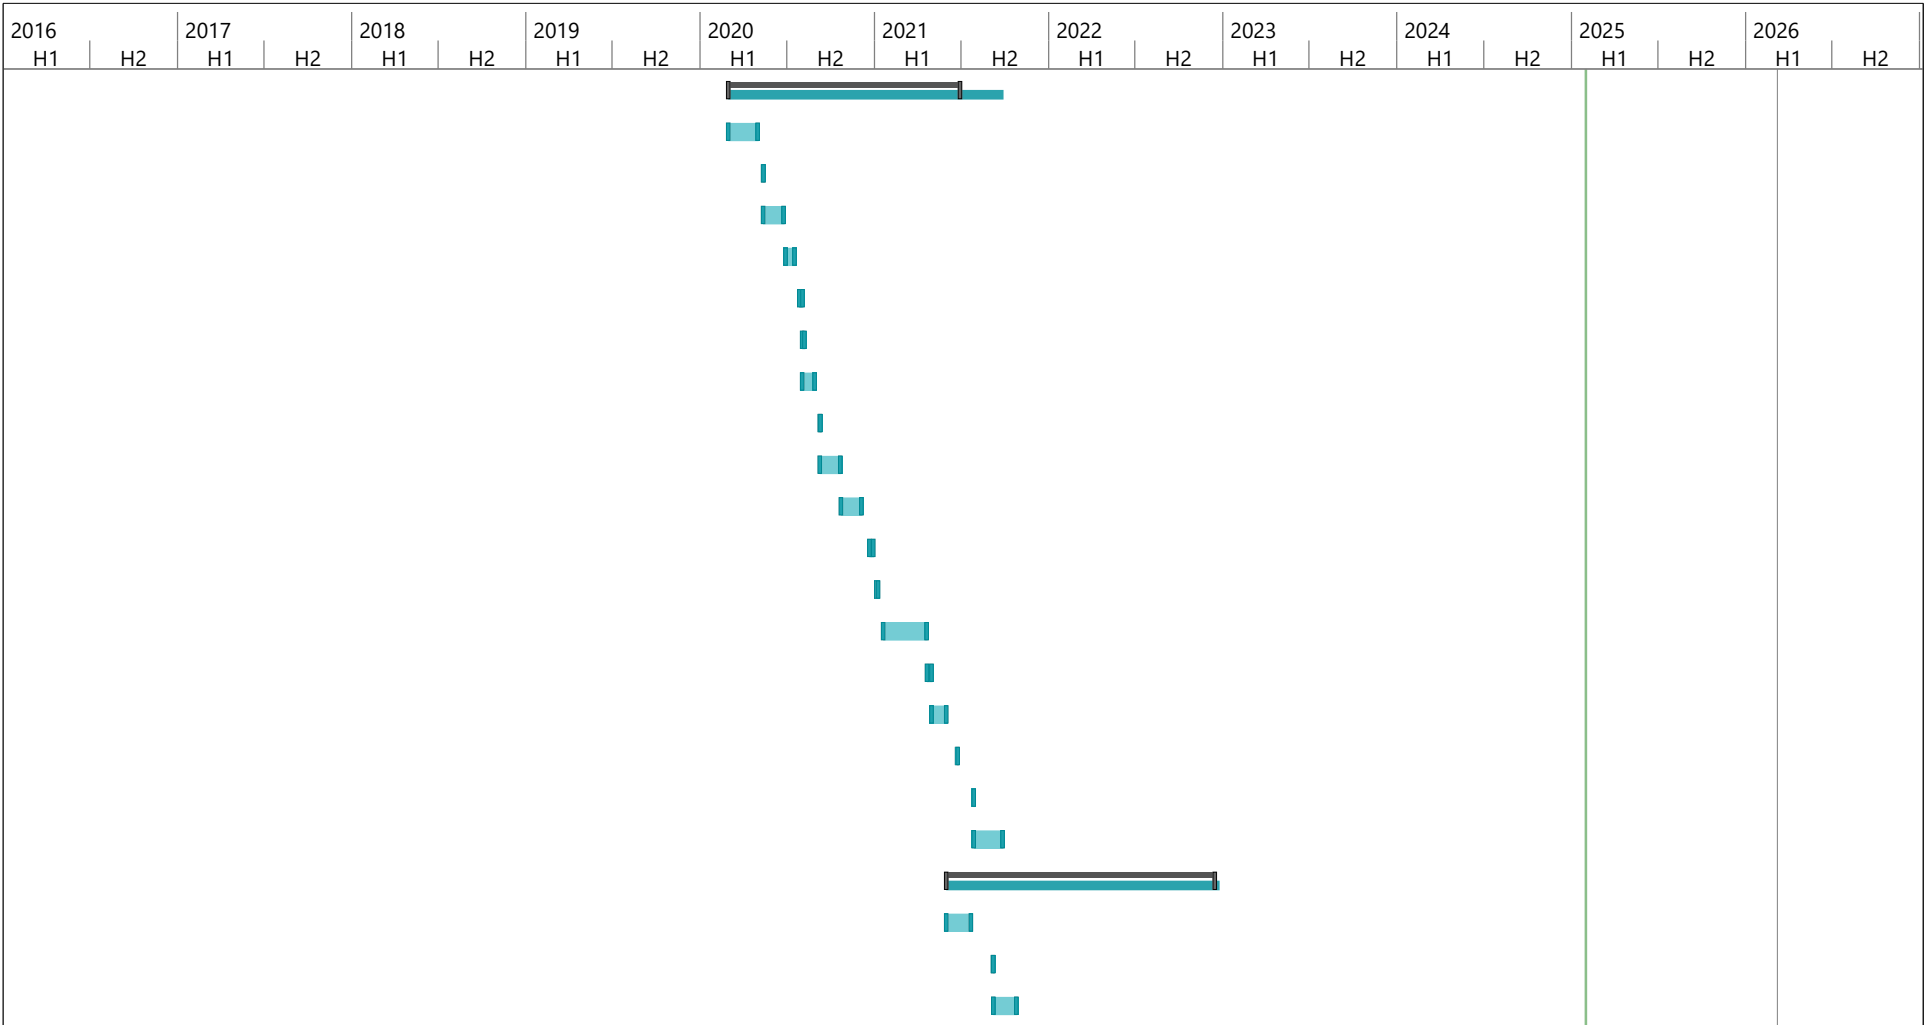


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

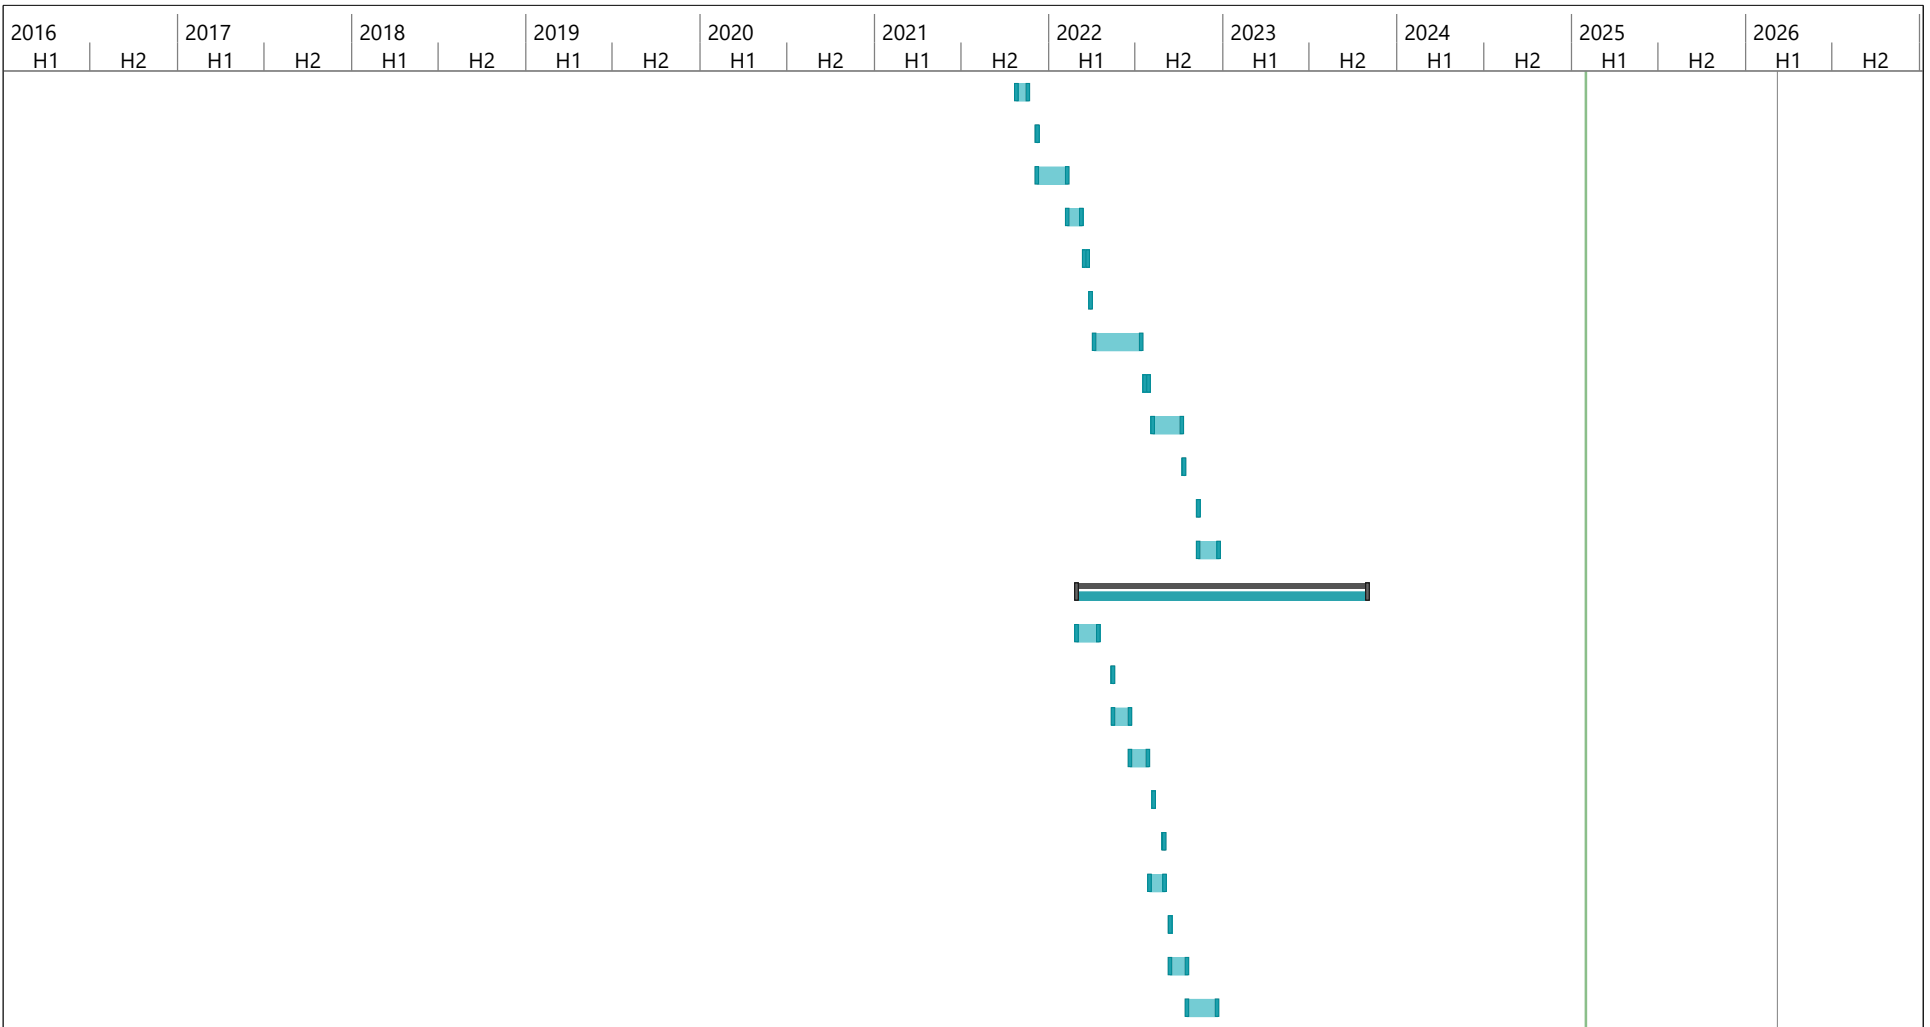


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

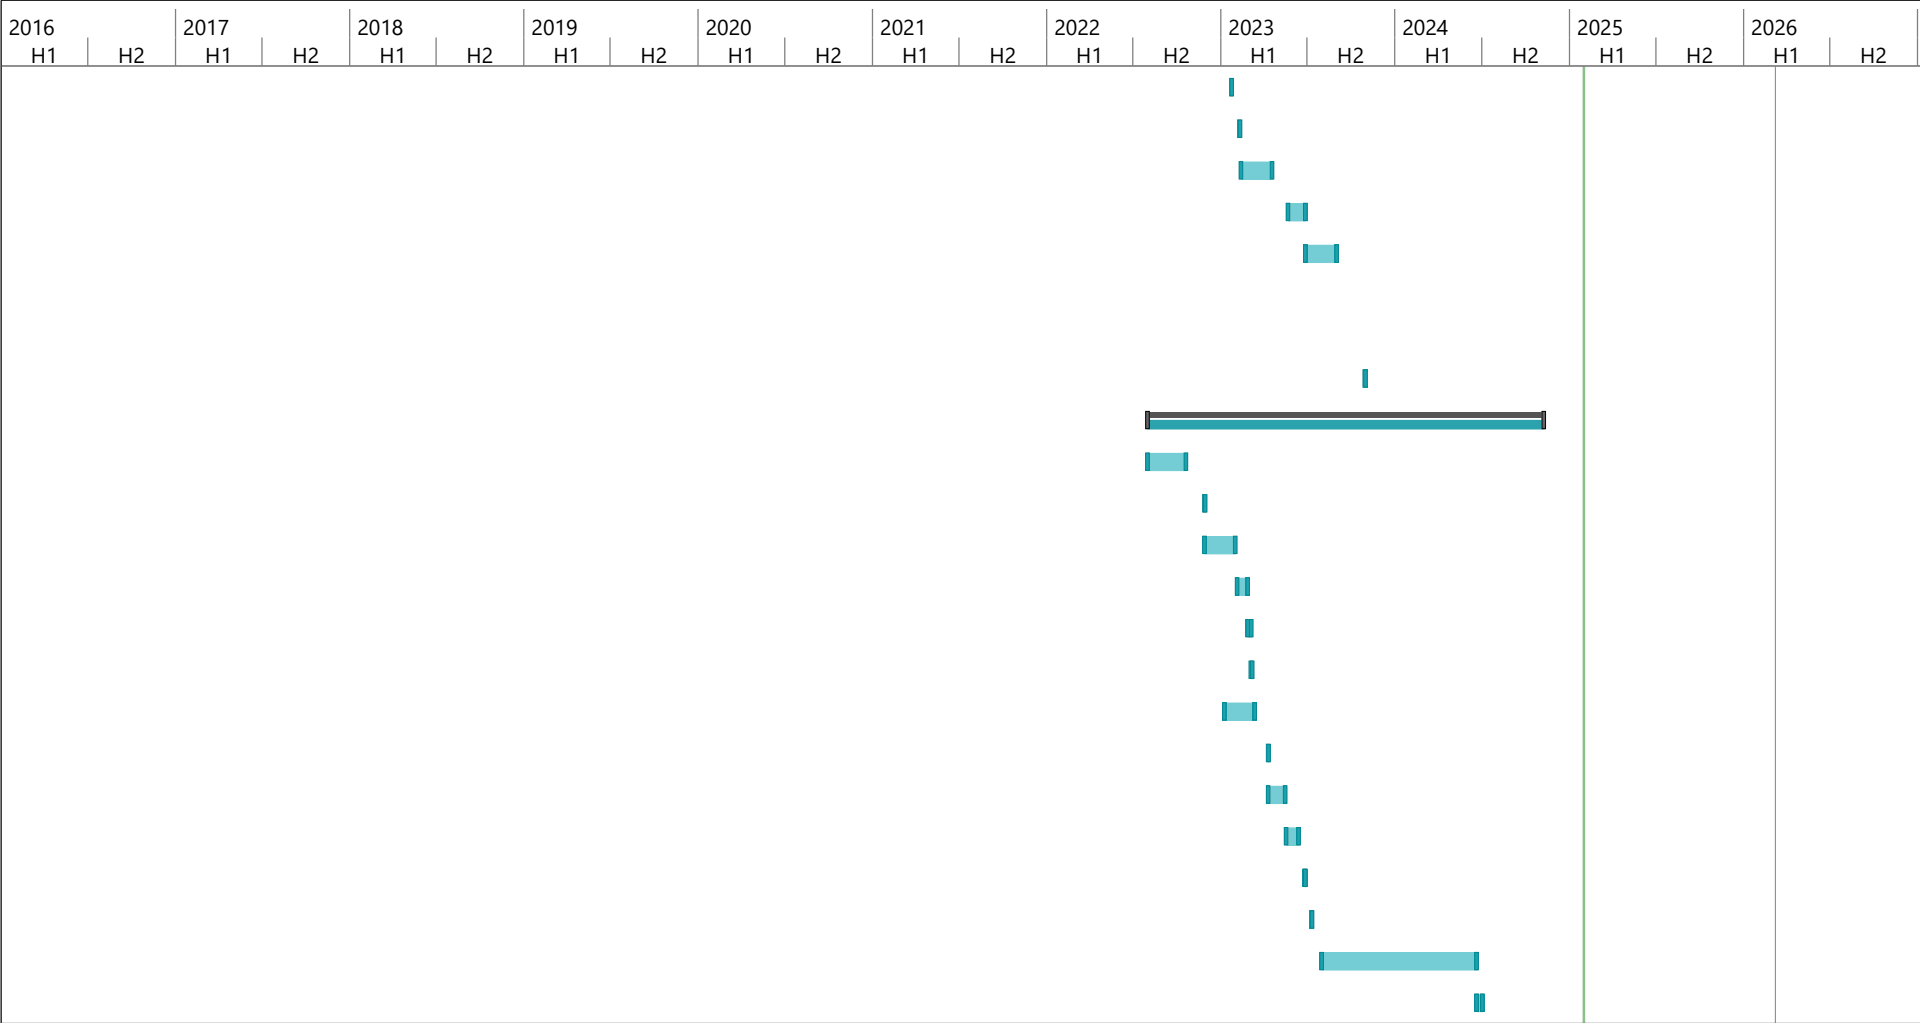


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

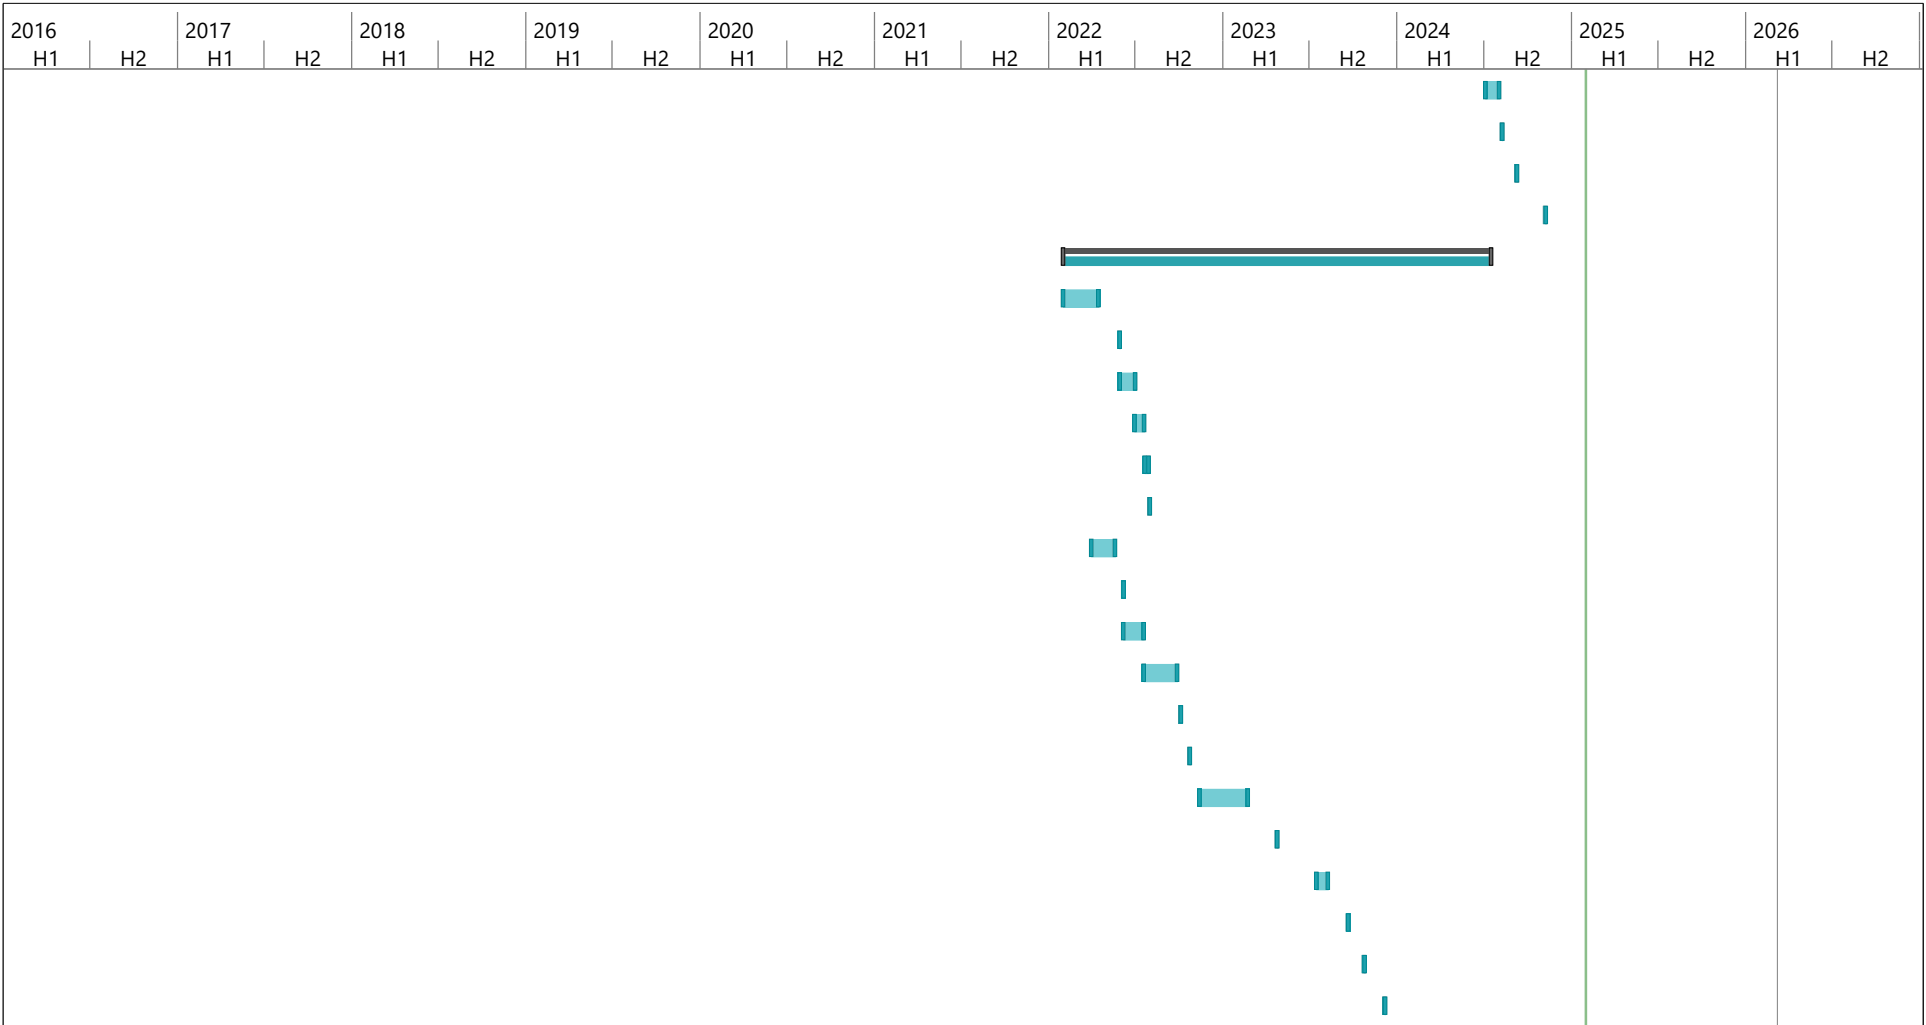


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

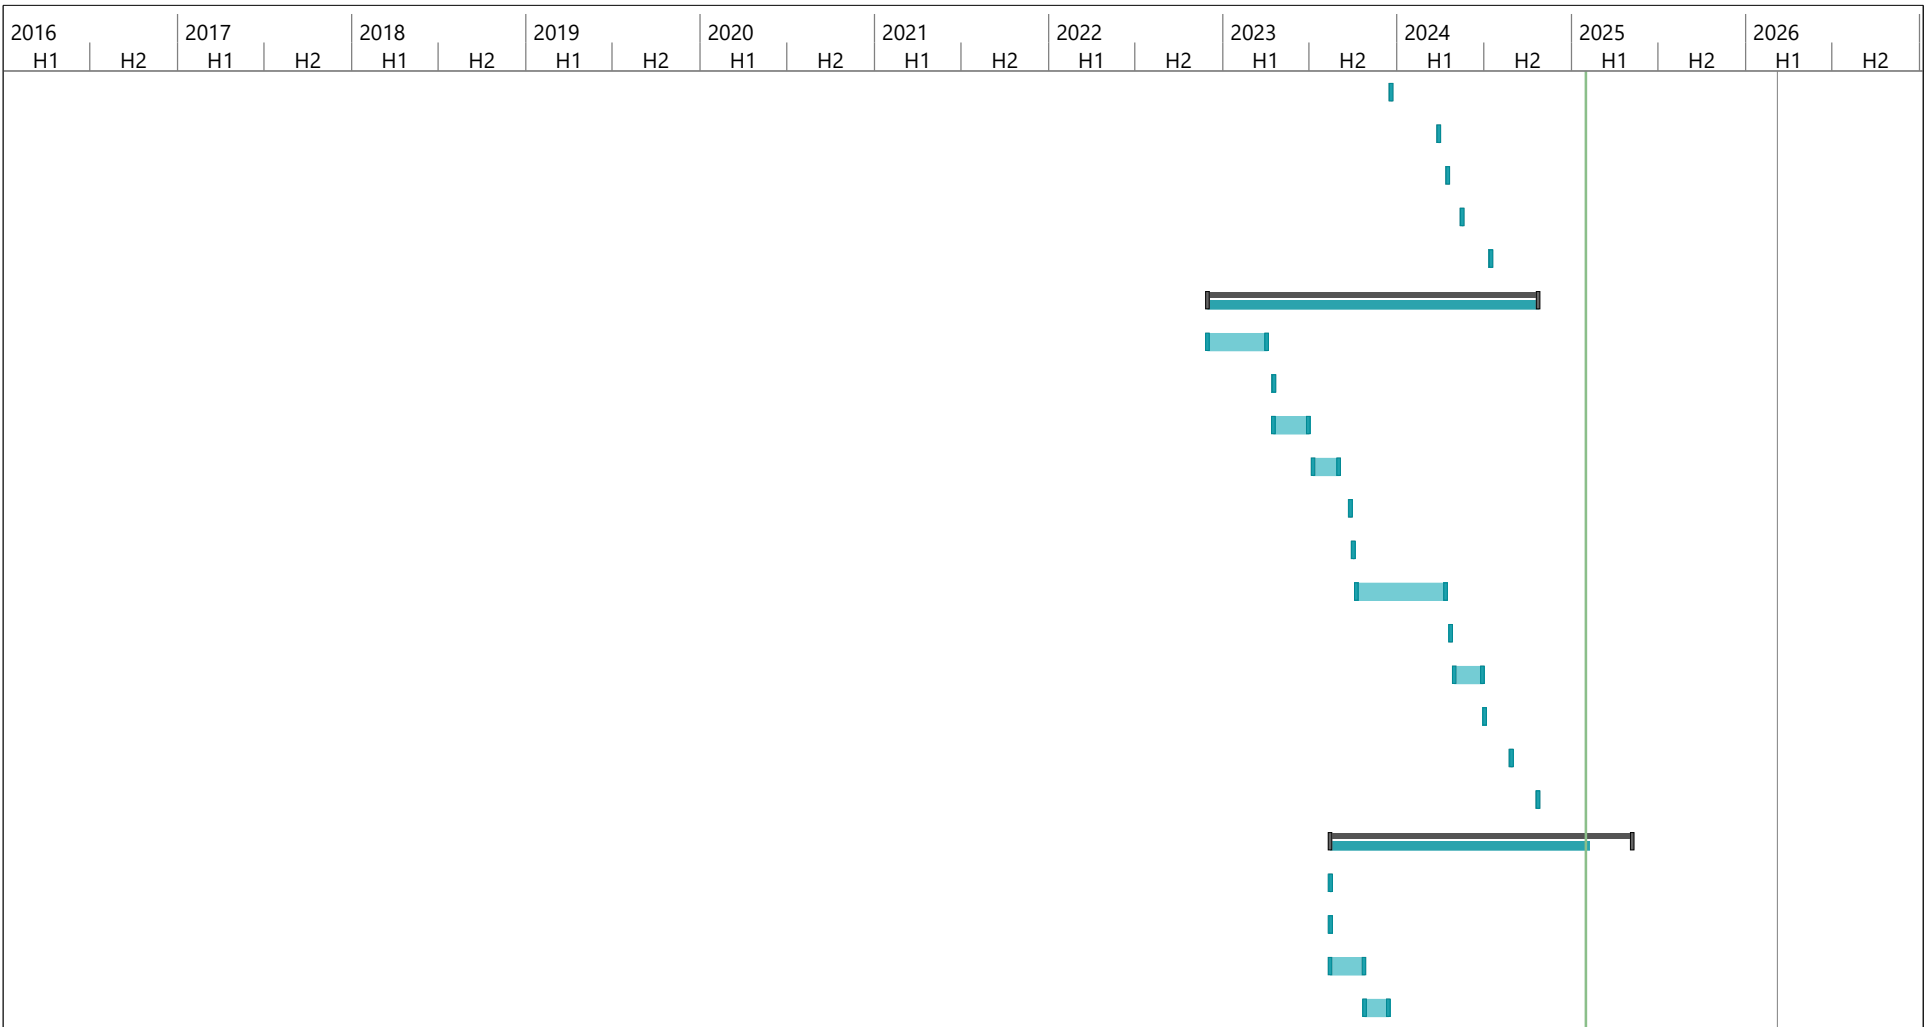


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

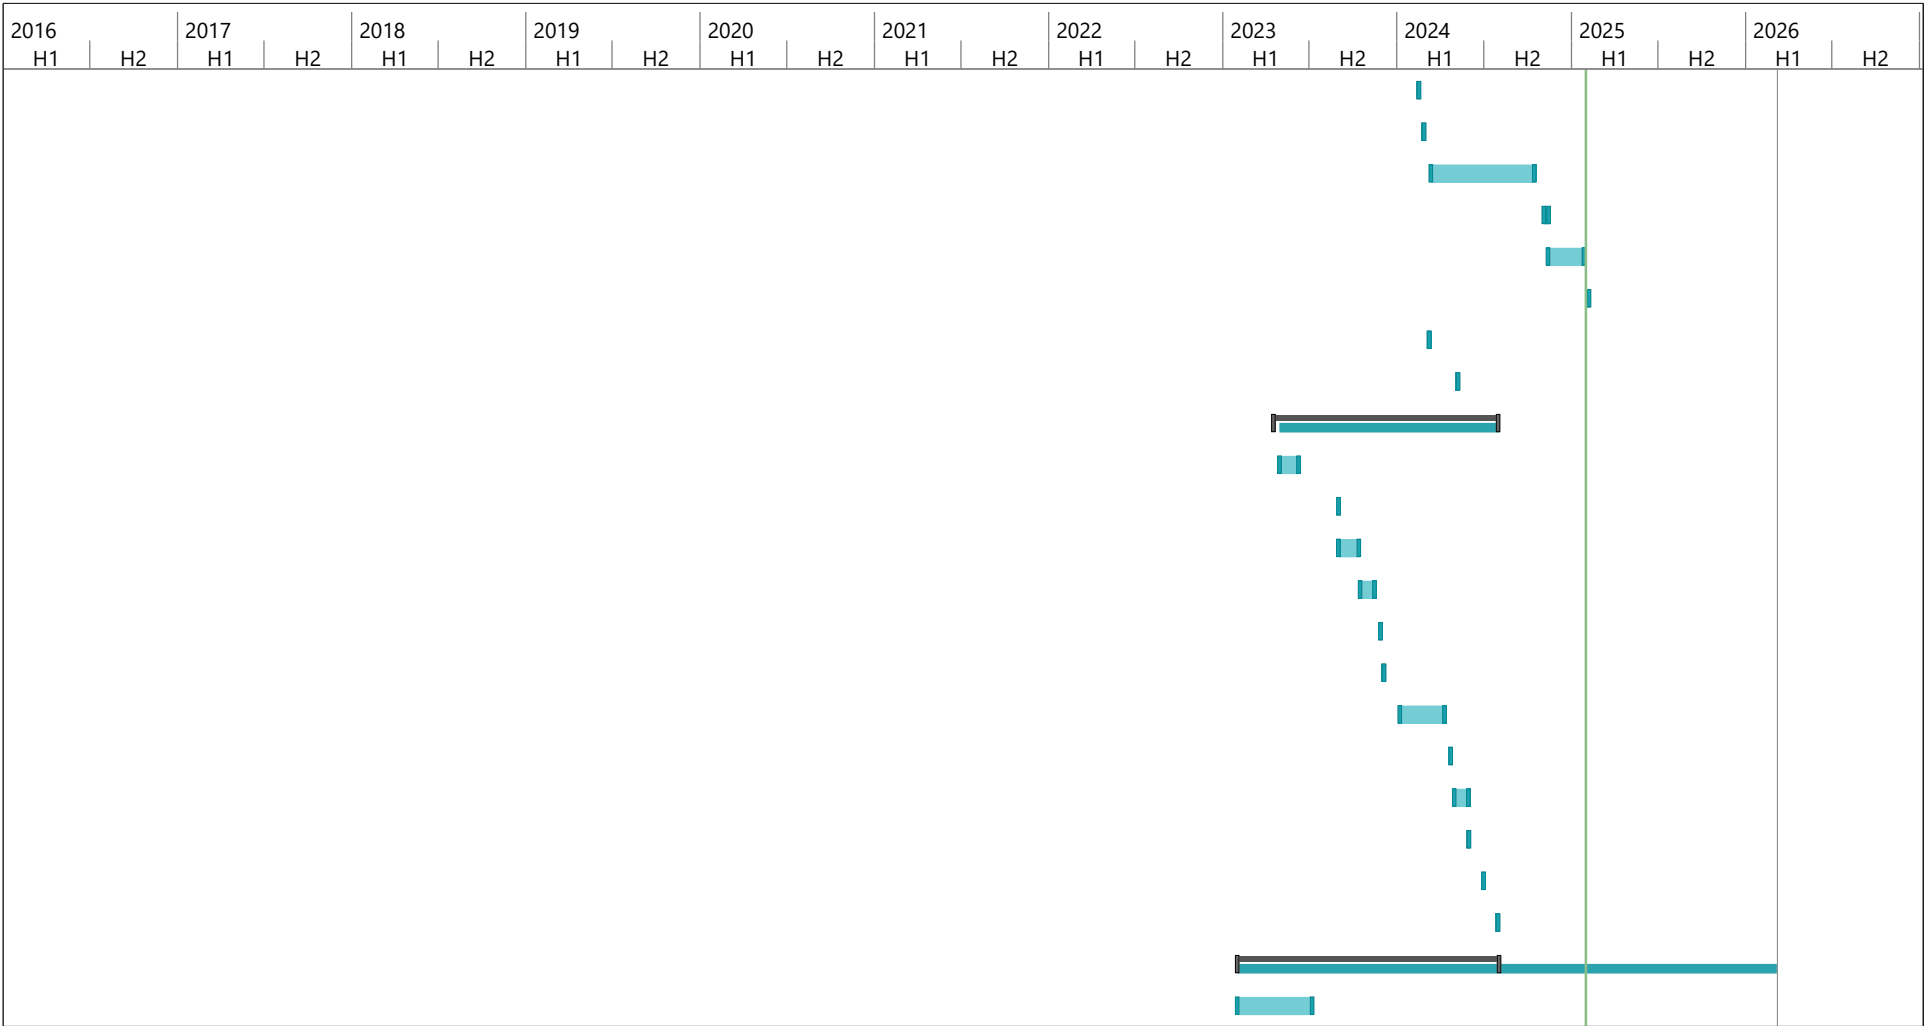


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

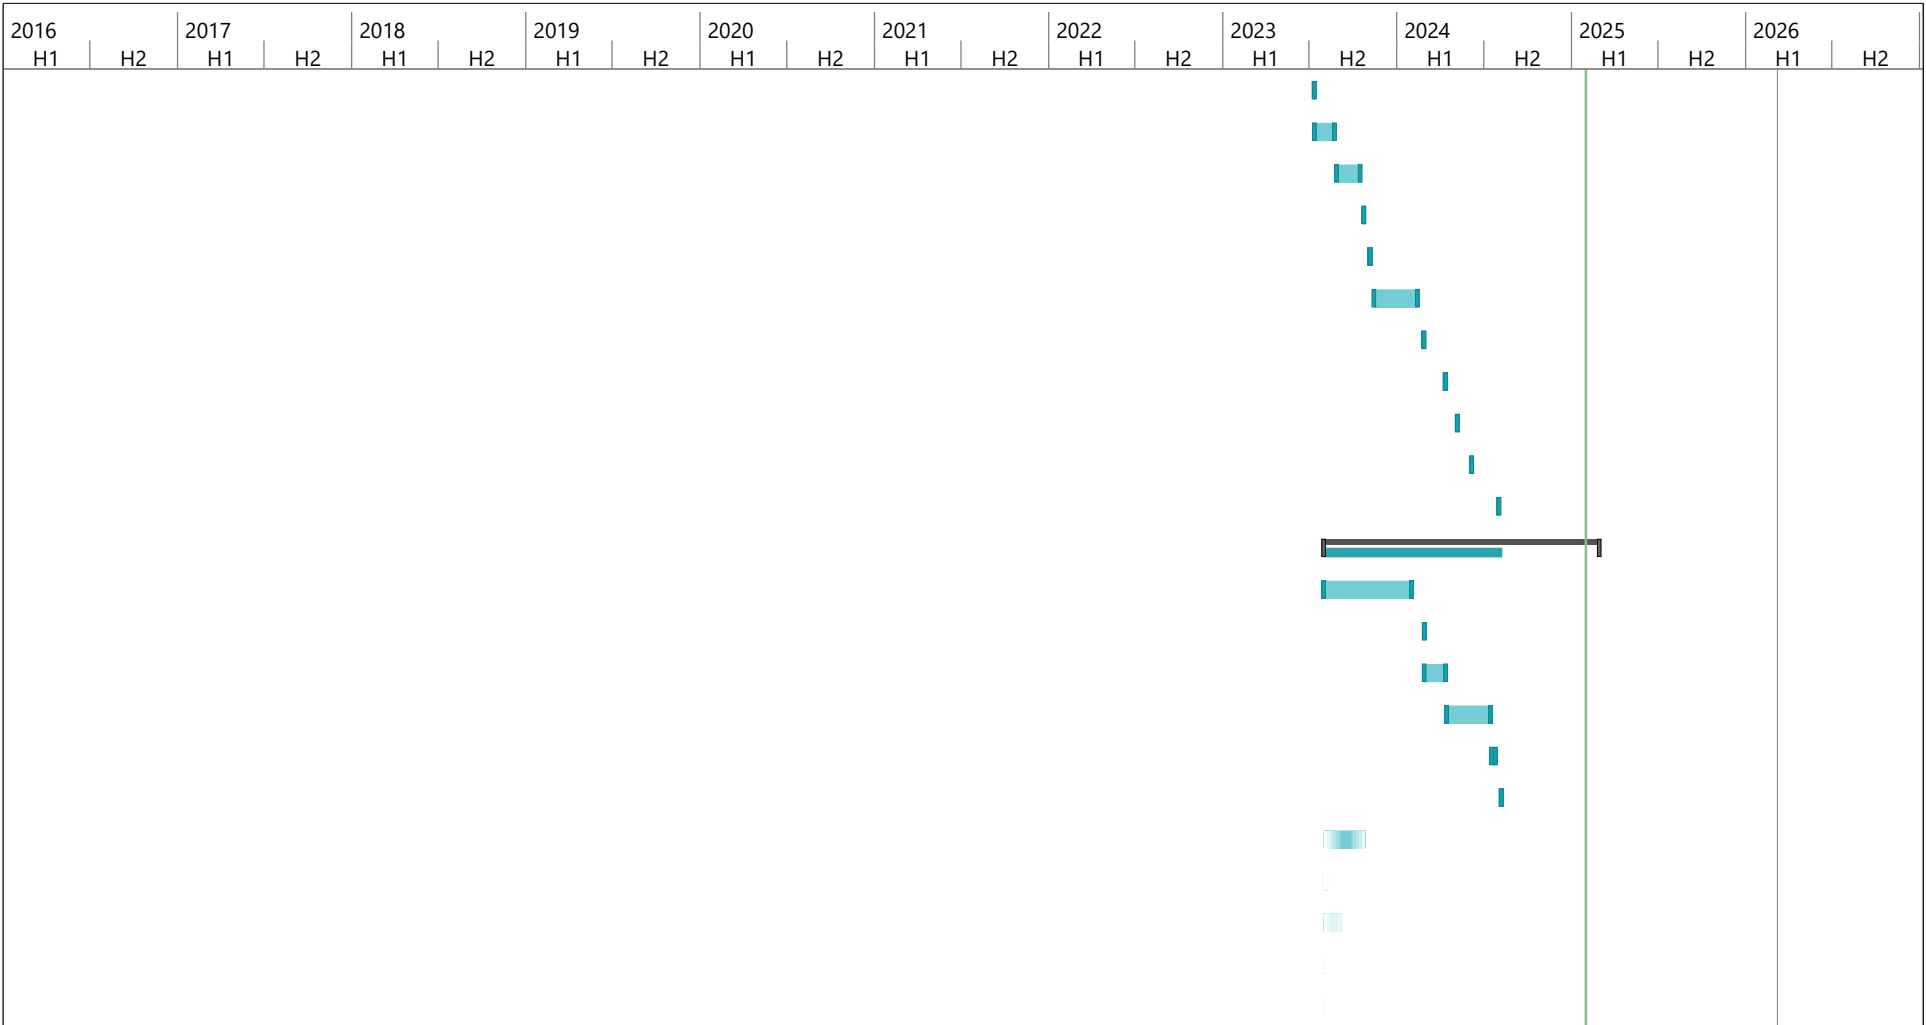


Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

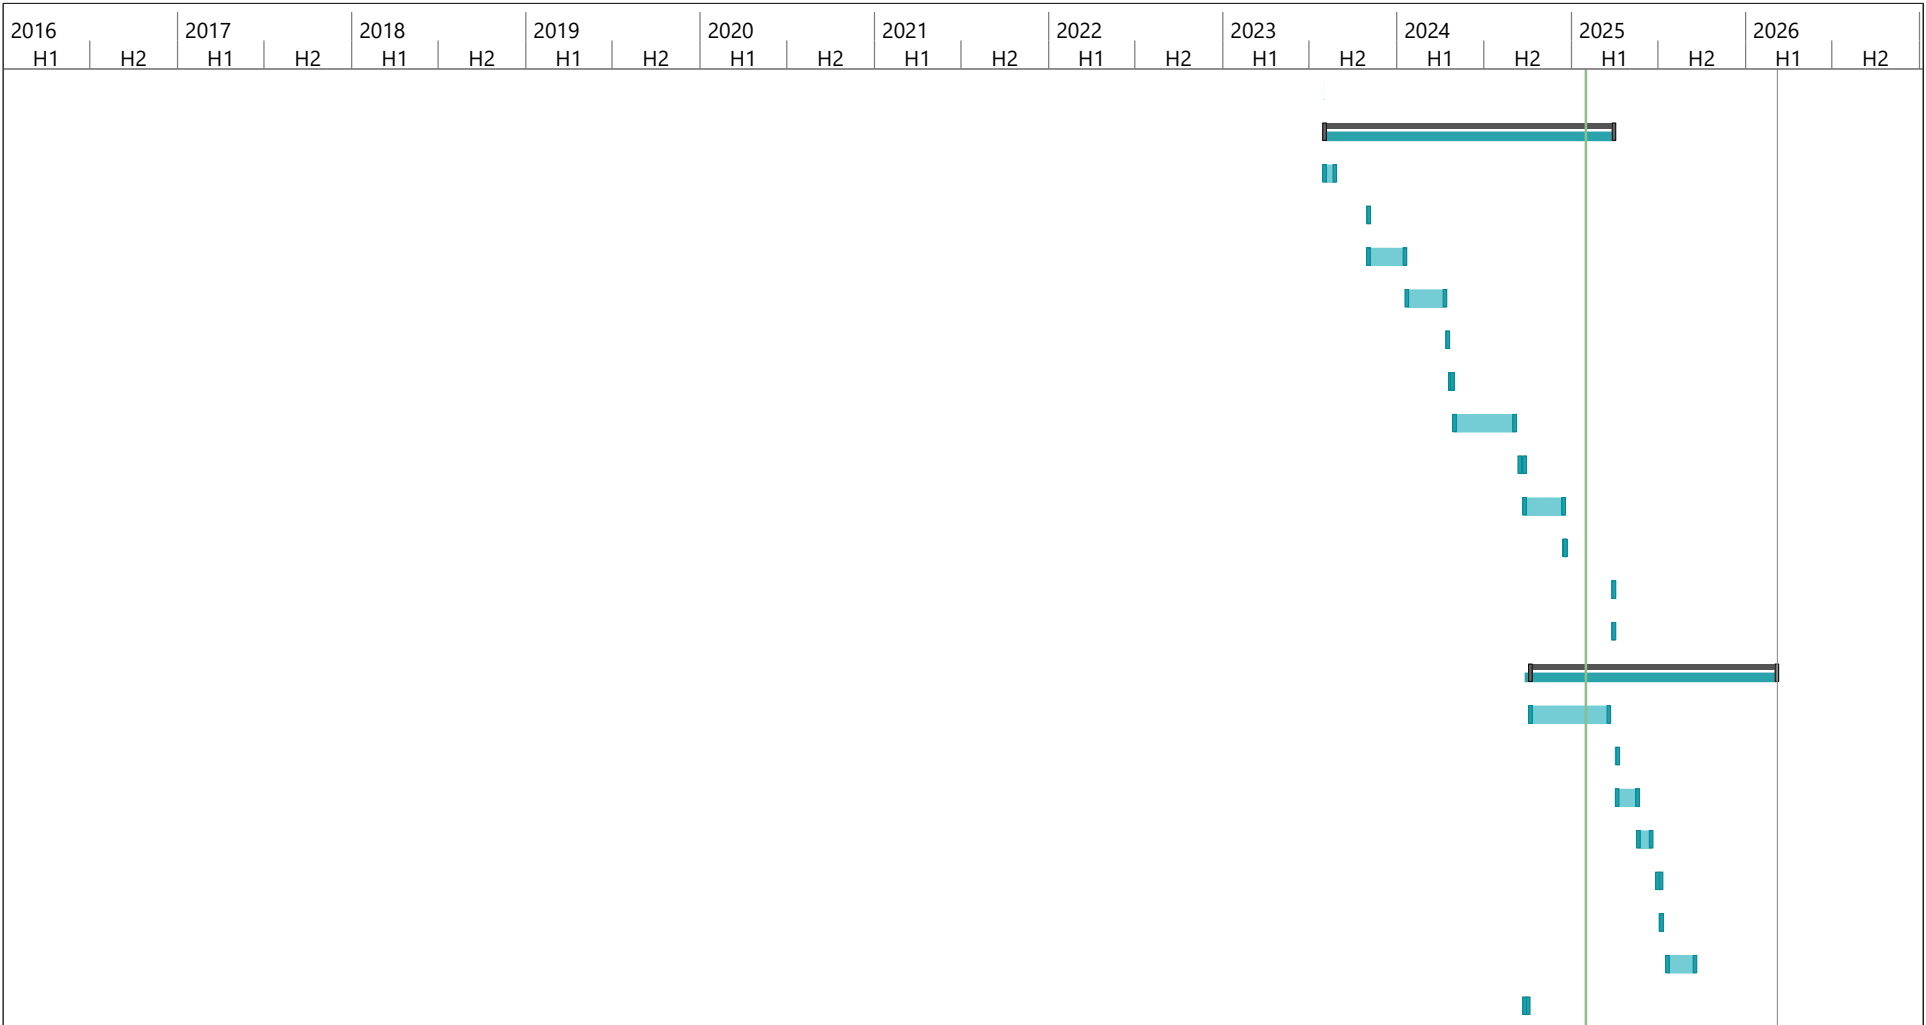

Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: IOU Master Task Timeli
Date: Fri 1/31/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
